

eDeposit Ireland

Social housing construction projects : status report Q3 2019

Item Type	report
Citation	Rebuilding Ireland, 'Social housing construction projects : status report Q3 2019', [report], Department of Housing, Planning and Local Government, 2019-12
Publisher	Department of Housing, Planning and Local Government
Rights	Y
Download date	2026-04-21 07:29:40
Link to Item	https://hdl.handle.net/20.500.14765/93958

Social Housing Construction Projects

Status Report Q3 2019

December 2019


Rebuilding
Ireland

Rebuilding Ireland - Action Plan for Housing and Homelessness

Quarter 3 of 2019: Social Housing Construction Status Report

Rebuilding Ireland: Social Housing Targets

Under Rebuilding Ireland, the Government has committed more than €6 billion to support the accelerated delivery of over 138,000 additional social housing homes to be delivered by end 2021. This will include 83,760 HAP homes, 3,800 RAS homes and over 50,000 new homes, broken down as follows:

Build: 33,617; Acquisition: 6,830; Leasing: 10,036.

It should be noted that, in the context of the review of Rebuilding Ireland and the refocussing of the social housing delivery programme to direct build, the number of newly constructed and built homes to be delivered by 2021 has increased significantly with overall delivery increasing from 47,000 new homes to over 50,000. This has also resulted in the rebalancing of delivery under the construction programme from 26,000 to 33,617 with acquisition targets moving from 11,000 to 6,830.

It is positive to see in the latest Construction Status Report that 6,499 social homes are currently onsite. The delivery of these homes along with the additional 8,050 homes in the pipeline will substantially aid the continued reduction in the number of households on social housing waiting lists. These numbers continue to decline with a 5% reduction of households on the waiting lists between 2018 and 2019 and a 25% reduction since 2016. This progress has been possible due to the strong delivery under Rebuilding Ireland with 90,011 households supported up to end of Q3 2019 since Rebuilding Ireland in 2016.

Social Housing Delivery- General


In 2018, 4,251 new build social housing homes were delivered; a very significant 85% increase on the 2,297 new builds in 2017. The target for 2019 is substantially increased further, to over 6,200 homes and a further 303 long-term vacant LA dwellings to be returned to active use. With this in mind, ambitious targets for this year have been set for each local authority, details of which are available on the Rebuilding Ireland website at: <http://rebuildingireland.ie/news/social-housing-targets-2019/>.

To end Q3 2019 some 2,229 additional homes have been delivered under Build activity, this included 226 vacant local authority dwellings in various states of significant disrepair were brought back to productive use through the Voids Programme in the first three quarters of 2019.




In the first three quarters of 2019, 1,533 homes have been provided by LAs and AHBs under the various acquisition programmes with a particular focus on areas of the country where acquisition of vacant properties represents the most expedient and cost efficient mechanism of delivering new homes for families. A further 630 homes were realised via the Leasing.

Families and individuals in the private rented sector were also supported through the Housing Assistance Payment and schemes such as RAS. Almost 13,000 households (12,853) were supported by HAP in the first three quarters of 2019 and 717 under RAS..


Overall, just under 18,000 (17,962) homes have been delivered in the first nine months of 2019, over 66% of the ambitious target for the year, with progressively increased output expected throughout the remainder of the year as developments in the pipeline materialise.

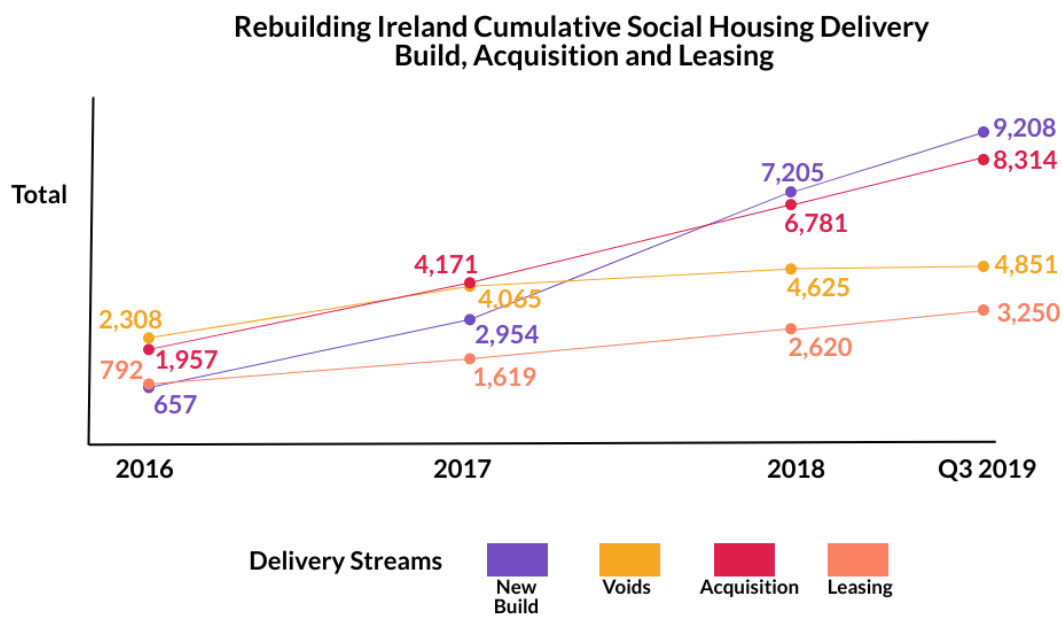

Rebuilding Ireland Total Cumulative Social Housing Delivery

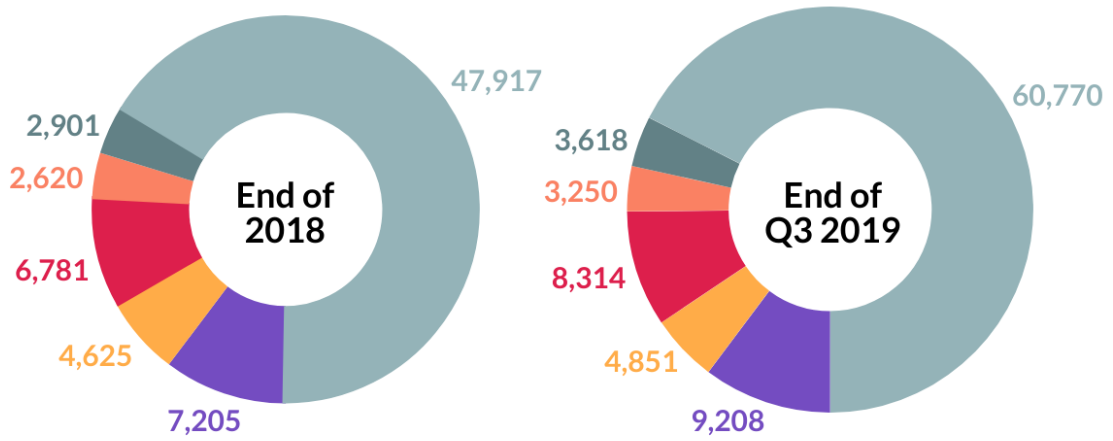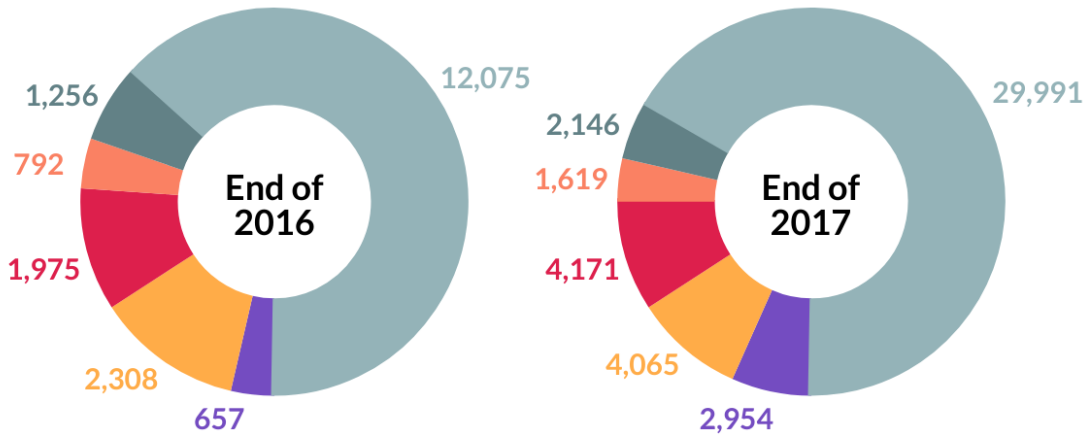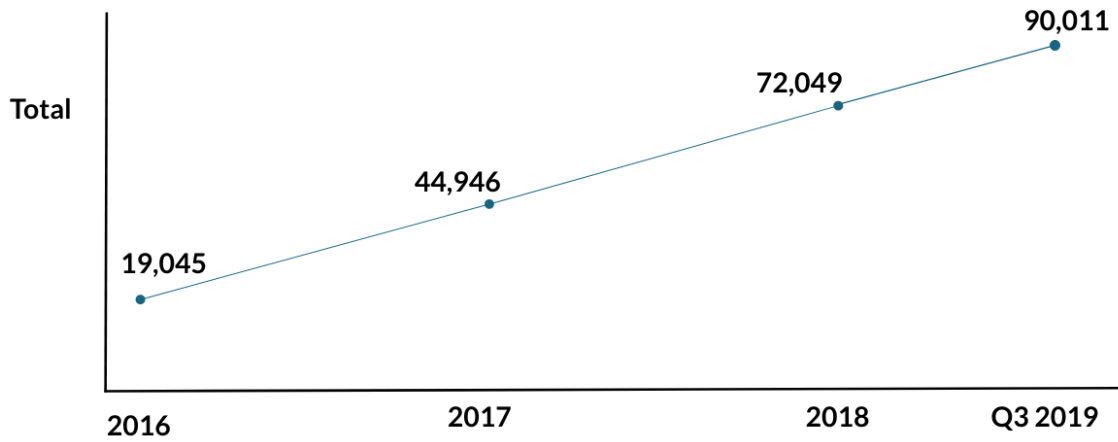

Delivery Streams



Tracking Progress in advancing the Construction Agenda- The Construction Status Report

The Quarter 3 – 2019 Social Housing Construction Projects Status Report has now been finalised and the attached Appendices set out progress made to date in advancing the construction pipeline.

Appendix 1 sets out the current status of schemes, as of the end of Q3 2019.

Appendix 2 sets out the various funding programmes delivering the 22,721 homes now in the pipeline.

PPPs are also reflected in the Construction Status Report with the addition of Bundle 1 and 2 - 999 homes, across 14 schemes and 10 Local Authorities. A further PPP bundle will be added when it reaches the appropriate approval stage.

It should be noted that the Social Housing Construction Status Report does not reflect the totality of the overall Build Programme. In addition to the homes reflected in the Report, local authority Part Vs are being delivered and these are reflected in the overall statistics provided by the Department.

An explanation of the delivery categories and Stages is provided at **Appendix 3**.

Part V is a very important contributor to new build social housing delivery. This delivery stream is not generally reflected in the CSR, however some AHB Part V being delivered as part of larger schemes may be included. To end Q3 2019, 493 Part V homes have been provided. A full breakdown by LA of Part V output is available on the statistics page of the Departments website.

Appendix 1

Table 1	Q4 of 2016		Q4 of 2017		Q1 of 2018		Q2 of 2018		Q3 of 2018		Q4 of 2018		Q1 of 2019		Q2 of 2019		Q3 of 2019	
Approval Status	Schemes*	Homes	Schemes*	Homes	Schemes*	Homes	Schemes*	Homes	Schemes*	Homes	Schemes*	Homes	Schemes*	Homes	Schemes*	Homes	Schemes*	Homes
Stage 1 - Capital Appraisal	165	2,687	156	2,946	157	2,602	145	2,476	109	2,042	71	1,545	134	2,535	135	2,530	116	2,089
Stage 2 - Pre-planning	93	1,279	124	1,715	124	1,958	140	2,336	134	2,076	127	2,000	107	1,945	112	1,820	122	2,016
Stage 3 - Pre-Tender design	32	490	60	613	63	1,368	79	1,842	87	1,660	83	1,694	80	1,326	65	1,307	54	899
Stage 4 - Tender Report or Final Turnkey/CALF approval	63	1,493	93	1,912	96	1,989	78	1,577	128	2,652	129	2,569	132	2,180	166	2,730	179	3,046
Site Start	90	1,829	190	3,646	222	3,932	298	4,602	322	4,933	291	4,992	322	5,598	370	6,439	389	6,499
Site Finish	61	652	223	2,592	268	2,964	327	3,518	393	4,173	598	6,334	641	6,740	711	7,313	785	8,172
Totals	504	8,430	846	13,424	930	14,813	1,067	16,351	1,173	17,536	1,299	19,134	1,416	20,324	1,559	22,139	1,645	22,721

* Some schemes are being delivered in phases and this is reflected in the number in the table, when we say 1,645 schemes this includes schemes being delivered in phases.

Appendix 2

Table 2	Q4 of 2016		Q4 of 2017		Q1 of 2018		Q2 of 2018		Q3 of 2018		Q4 of 2018		Q1 of 2019		Q2 of 2019		Q3 of 2019	
Funding Programme	Schemes*	Homes	Schemes*	Homes	Schemes*	Homes	Schemes*	Homes	Schemes*	Homes	Schemes*	Homes	Schemes*	Homes	Schemes*	Homes	Schemes*	Homes
CALF Construction	28	677	59	1,431	58	1,358	50	1,352	54	1,328	52	1,323	51	1,388	53	1,511	55	1,539
CALF Construction Turnkey	55	1,388	147	2,774	173	3,045	265	3,643	299	4,137	349	5,038	381	5,192	424	5,839	424	5,717
CAS Construction	108	1,048	129	1,218	136	1,282	139	1,310	142	1,371	144	1,405	147	1,431	153	1,473	159	1,519
Regeneration	36	782	47	1,060	49	1,085	50	1,085	50	1,090	54	1,104	55	1,085	56	1,147	53	1,097
SHIP Construction	240	3,571	365	5,124	380	5,304	395	5,433	419	5,634	465	6,057	489	6,310	519	6,651	575	7,376
SHIP Construction Rapid	14	467	26	716	33	894	38	1,008	41	1,093	40	1,141	43	1,315	49	1,441	50	1,444
SHIP Construction Turnkey	23	497	73	1,101	95	1,311	116	1,521	154	1,884	181	2,067	236	2,604	291	3,078	315	3,030
PPP					6	534	14	999	14	999	14	999	14	999	14	999	14	999
Totals	504	8,430	846	13,424	930	14,813	1,067	16,351	1,173	17,536	1,299	19,134	1,416	20,324	1,559	22,139	1,645	22,721

* Some schemes are being delivered in phases and this is reflected in the number in the table, when we say 1,645 schemes this includes schemes being delivered in phases.

Appendix 3- Explanatory notes

The Construction Status report is a full compendium of live LA and AHB new-build activity across the period 2016-2021. The following schemes are represented in the Construction Status Report:

- Social housing Capital Investment Programme (SHCIP)
- Capital Assistance Scheme (CAS)
- Capital Advance Leasing Facility (CALF)
- Public Private Partnership (PPP)

Schemes which have completed in prior reporting periods are retained on the Report, so as to preserve data and provide a full overview of activity.

The Report is published every quarter in open format on the data.gov.ie website, which allows the user to filter and analyse data.

The Social Housing Capital Investment Programme (SHCIP) provides funding to local authorities for the provision of social housing by means of construction and acquisition.

The Capital Assistance Scheme provides essential funding to AHBs for the provision of accommodation for persons with specific categories of housing need such as Homeless and Older Persons, People with Disabilities, Returning Emigrants and Victims of Domestic Violence.

4-Stage Approval Process

The funding approval process for social housing projects supported by the Department under the SHCIP and CAS schemes outlined above is in line with the Government's Capital Works Management Framework (CWMF), the same approach used for other publicly-funded Capital construction projects. While there are nine points of review within the CWMF, the Department has combined these to just four for capital-funded social housing construction projects.

The Departmental approvals themselves represent a small minority only of the time taken in advancing a build project onto site. The approach we follow means that local authorities forward design proposals and costings to the Department sequentially, as the local authorities advance the projects through their own planning work. Check lists, guidance and templates have been issued to the Local Authorities to assist them in this process.

What are the 4 stages?

The four stages are as follows:-

Stage 1 – Capital Appraisal to verify the business case and basic project suitability – this is a light presentation of information; no design and only indicative costs are required at this initial stage.

Stage 2 –Pre-planning outline design and cost check –following site investigations, this involves the level of designs that are required for the Part 8 planning process and a completed QS cost plan; detailed tender drawings and resulting costs are not needed at this stage until planning permission is obtained.

Stage 3 – Pre-tender costs check – the more detailed designs and cost estimates have been prepared by the local authority design team at this stage and a cost check submitted before going to tender, but if

costs are consistent with the earlier stages, then this review will be swift. Unless there have been changes to the design following Part 8/planning, or conditions to be met, the design is not reviewed.

Stage 4 – Tender approval from Department – the tenders have been received and assessed by the local authority and again, if costs are consistent with the earlier stages, this review will be swift.

There is now a Target Programme for advancing social housing capital-funded projects through design, planning and approval. This overall programme sets a target of 59 weeks from stage 1 submission by the local authority, to contract award for the construction. It establishes target turnaround times for the Department to carry out the review process and for the local authority to carry out the design of the scheme, the planning process and the procurement of a builder. While the aim of the programme is to create a realistic but ambitious target programme, it is acknowledged that external factors can affect construction projects; for example, delays can arise at planning, where the views of Councillors and communities are taken into account, but these can be minimised by early engagement. Site condition difficulties should not arise if appropriate site investigations are carried out at the beginning of the process.

The single-stage approval process

A revised single-stage approval process for social housing projects less than €2m has been implemented. The main change from the previous single-stage approach is that in the event that the approved budget is not maintained, a second application for a budget revision will be facilitated on receipt of tenders. This will be facilitated where certain circumstances have caused the costs to rise – for example, tender inflation - and where such an adjustment will not increase the overall budget requirement beyond the €2m level.

Capital Advance Leasing Facility (CALF):

The Department offers financial support to Approved Housing Bodies (AHBs) in the form of a long term loan under the **Capital Advance Leasing Facility (CALF)** to assist with the financing of the **construction** or **acquisition** of homes that will be provided for social housing use. This loan facility can support up to 30% of the eligible capital cost of the project, where the homes will be provided under long-term lease arrangements to local authorities for social housing use. Funding is provided to AHBs through Local Authorities.

CALF approvals do not follow the same approval process as the SHCIP 4-Stage process. The assessment process includes a full financial evaluation which is carried out in conjunction with the Housing Agency. The funding approval may be provided at various stages of project development, including pre-planning for example, in which case the funding approval will be subject to planning. Where a project changes post-approval, a revised application is submitted and a revised approval issues following normal assessment procedures.

Public Private Partnership (PPP):

€300 million was committed in Budget 2015 to providing 1,500 new social housing homes via the Public Private Partnership model. The programme is being delivered in three bundles with a capital value of approximately €100 million each. Each bundle is being developed over a number of sites, spread across different local authorities. Each individual site is to provide between 50 and 100 social housing homes.

The housing homes are delivered using what is termed as an 'availability-based PPP model'. A private sector company designs, builds, finances and maintains the social housing homes. In return, it receives payments which are spread over 25 years.

As the model is 'availability-based', the private sector partner is responsible for ensuring that homes are available for occupation. The local authority is responsible for allocating tenants. The private sector partner provides maintenance and upkeep services for 25 years. After this time, the homes are returned to the State in good condition, subject to reasonable wear and tear.

Bundles are added to the Construction Status Report at tender stage.

Part V data on the CSR:

The Construction Status Report does not contain data on Part V schemes funded under the SHCIP scheme or delivered by LAs without DHPLG funding. It does contain a small number of AHB Part Vs which are advancing as part of larger schemes approved under the Capital Advance Leasing Facility. The full Part V output is published as part of the overall Social Housing Delivery Report.

Disclaimer:

While every effort is made to ensure that the data in the report is accurate at the time of publication, the report now covers 22,721 homes across over 1,645 schemes/phases of schemes and is reliant on the provision and processing of scheme updates and delivery data from 31 Local Authorities. Where errors arise, these will be corrected in the next version published. The most recent published version therefore should always be referred to.

No.	Funding Programme	LA	Scheme/Project Name	No. of Units	Approved Housing Body	Stage 1 Capital Appraisal	Stage 2 Pre Planning	Stage 3 Pre Tender design	Stage 4 Tender Report of Final Turnkey/CALF approval	On site	Completed
1	CALF Turnkey	Carlow	7 units, Rivercourt, Carlow (Phase 1)	3	Co-operative Housing Ireland						Q3-2019
2	CALF Turnkey	Carlow	7 units, Rivercourt, Carlow (Phase 2)	4	Co-operative Housing Ireland					Q1-2019	
3	CALF Turnkey	Carlow	Ballickmoyler, Graigcullen, Carlow (Phase 1)	27	Co-operative Housing Ireland					Q3-2019	
4	CALF Turnkey	Carlow	Ballickmoyler, Graigcullen, Carlow (Phase 2)	30	Co-operative Housing Ireland					Q3-2019	
5	CALF Turnkey	Carlow	Barrett Street, Bagnalstown, Co. Carlow (Phase 1)	10	Tintean Housing Association Ltd						Q1-2018
6	CALF Turnkey	Carlow	Browneshill Rise, Browneshill Road, Chapelstown, Carlow (Phase 1)	15	Túath Housing Association Ltd						Q4-2018
7	CALF Turnkey	Carlow	Browneshill Rise, Browneshill Road, Chapelstown, Carlow (Phase 2)	12	Túath Housing Association Ltd						Q2-2019
8	CALF Turnkey	Carlow	Browneshill Rise, Browneshill Road, Chapelstown, Carlow (Phase 3)	10	Túath Housing Association Ltd						Q2-2019
9	CALF Turnkey	Carlow	Browneshill Rise, Browneshill Road, Chapelstown, Carlow (Phase 4)	6	Túath Housing Association Ltd						Q3-2019
10	CALF Turnkey	Carlow	Browneshill Rise, Browneshill Road, Chapelstown, Carlow (Phase 5)	16	Túath Housing Association Ltd					Q1-2018	
11	CALF Turnkey	Carlow	Browneshill Wood, Browneshill Road, Chapelstown, Carlow (Phase 1)	14	Túath Housing Association Ltd						Q4-2018
12	CALF Turnkey	Carlow	Greenhills, Leighlin Road, Graiguecullen, Carlow (Phase 1)	8	Co-operative Housing Ireland					Q3-2019	
13	CALF Turnkey	Carlow	Laragh Beg, Ballon, Co. Carlow (Phase 1)	14	Co-operative Housing Ireland				Q3-2019		
14	CALF Turnkey	Carlow	Laragh Beg, Ballon, Co. Carlow (Phase 2)	8	Co-operative Housing Ireland				Q3-2019		
15	CALF Turnkey	Carlow	Rivercourt, Carlow (Phase 1)*	8	Co-operative Housing Ireland					Q3-2018	
16	CALF Turnkey	Carlow	Rivercourt, Carlow (Phase 2)	8	Co-operative Housing Ireland					Q3-2018	
17	CALF Turnkey	Carlow	Rivercourt, Carlow (Phase 3)	12	Co-operative Housing Ireland					Q3-2018	
18	CALF Turnkey	Carlow	Rivercourt, Carlow (Phase 4)	9	Co-operative Housing Ireland					Q3-2018	
19	CALF Turnkey	Carlow	Rivercourt, Carlow (Phase 5)	10	Co-operative Housing Ireland					Q3-2018	

20	CALF Turnkey	Carlow	Sleaty Street, Graigcullen, Carlow (Phase 1)	26	Cluid Housing							Q1-2019
21	CAS CONSTRUCTION	Carlow	Gleann na Bearu, Royal Oak Road, Bagenalstown	6	Respond			Stage 3 approved Q4-2017, the scheme is now approved to proceed to tender.				
22	CAS CONSTRUCTION	Carlow	Ballincarrig, Wexford Road	6	Tintean Housing Association Ltd							Q4-2016
23	CAS CONSTRUCTION TURNKEY	Carlow	Pollerton Big, Carlow	6	Tintean Housing Association Ltd				Stage 4 approved Q1-2019, the scheme is fully approved.			
24	SHIP CONSTRUCTION	Carlow	Father Flood Avenue, Rathvilly	8	*N/A							Q1-2019
25	SHIP CONSTRUCTION	Carlow	St. Oliver's Crescent, Myshall	4	*N/A							Q2-2019
26	SHIP CONSTRUCTION	Carlow	St. Mary's Court & Dereen Heights	6	*N/A							Q3-2019
27	SHIP CONSTRUCTION	Carlow	Crowsgrove, Kildavin	1	*N/A							Q2-2019
28	SHIP CONSTRUCTION	Carlow	Shillelagh Road, Tullow, Co. Carlow	6	*N/A				Stage 4 approved Q2-2019, the scheme is fully approved.			
29	SHIP CONSTRUCTION	Carlow	Ardattin	6	*N/A				Stage 4 approved Q2-2019, the scheme is fully approved.			
30	SHIP CONSTRUCTION	Carlow	Brownbog, Hackettstown	1	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.			
31	SHIP CONSTRUCTION	Carlow	Spahill, Borris, Co. Carlow	1	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.			
32	SHIP CONSTRUCTION	Carlow	The Laurels, Carlow Town	5	*N/A							Q2-2018
33	SHIP CONSTRUCTION	Carlow	Ard na Greine, Tullow	16	*N/A							Q4-2018
34	SHIP CONSTRUCTION	Carlow	Dublin Road, Tullow	21	*N/A							Q3-2019
35	SHIP CONSTRUCTION	Carlow	Bagenalstown	20	*N/A							Q2-2019
36	SHIP CONSTRUCTION	Carlow	Bilboa	2	*N/A							Q3-2018
37	SHIP CONSTRUCTION	Carlow	Slate Row, Hackettstown	4	*N/A							Q4-2018
38	SHIP CONSTRUCTION	Carlow	Mount Leinster Park, Carlow	4	*N/A							Q4-2017
39	SHIP CONSTRUCTION	Carlow	Myshall	4	*N/A							Q1-2018

40	SHIP CONSTRUCTION	Carlow	Pound Lane, Borris	4	*N/A							Q3-2017
41	SHIP CONSTRUCTION	Carlow	Rathvilly	10	*N/A							Q2-2017
42	SHIP CONSTRUCTION	Carlow	Moneybeg, Bagenalstown	24	*N/A							Q3-2017
43	SHIP CONSTRUCTION	Carlow	Paulville, Tullow (SRD)	1	*N/A							Q3-2017
44	SHIP CONSTRUCTION	Carlow	Maryborough St., Carlow	5	*N/A							Q1-2018
45	SHIP CONSTRUCTION	Carlow	Drumin, St. Mullins (SRD)	1	*N/A							Q1-2019
46	SHIP CONSTRUCTION	Carlow	Pound Lane, Borris, Co. carlow	9	*N/A		Stage 2 approved Q3-2019, full design/tender being prepared.					
47	SHIP CONSTRUCTION TURNKEY	Carlow	Carrigbrook, Tullow Road, Carlow (Phase 1)	12	*N/A							Q3-2019
48	SHIP CONSTRUCTION TURNKEY	Carlow	Carrigbrook, Tullow Road, Carlow (Phase 2)	51	*N/A						Q4-2017	
49	CALF Turnkey	Cavan	16 Units, Fairgreen Park, Mullagh, Co. Cavan (Phase 1)	16	Clanmil Housing Association Ireland					Q3-2019		
50	CALF Turnkey	Cavan	25 units, Drumalee Manor, Drumalee, Co. Cavan (Phase 1)	12	Túath Housing Association Ltd					Q3-2019		
51	CALF Turnkey	Cavan	25 units, Drumalee Manor, Drumalee, Co. Cavan (Phase 2)	13	Túath Housing Association Ltd					Q3-2019		
52	CALF Turnkey	Cavan	Cluain Dara, Kingscourt, Co Cavan (Phase 1)	16	Cluid Housing							Q4-2016
53	CALF Turnkey	Cavan	Drumalee Manor, Drumalee, Cavan (Phase 1)	4	Túath Housing Association Ltd							Q2-2018
54	CALF Turnkey	Cavan	Drumalee Manor, Drumalee, Cavan (Phase 2)	5	Túath Housing Association Ltd							Q3-2018
55	CALF Turnkey	Cavan	Drumalee Manor, Drumalee, Cavan (Phase 3)	2	Túath Housing Association Ltd							Q4-2018
56	CALF Turnkey	Cavan	Rampart View, Virginia, Co. Cavan (Phase 1)	2	Co-operative Housing Ireland							Q3-2019
57	CALF Turnkey	Cavan	Rampart View, Virginia, Co. Cavan (Phase 2)	6	Co-operative Housing Ireland						Q1-2019	
58	CALF Turnkey	Cavan	Rampart View, Virginia, Co. Cavan (Phase 3)	11	Co-operative Housing Ireland						Q1-2019	
59	CAS CONSTRUCTION TURNKEY	Cavan	Castlemanor Village, Cavan Town	29	Túath Housing Association Ltd							Q3-2019

60	SHIP CONSTRUCTION	Cavan	Rosehill, Mullagh (Phase 6)	8	*N/A							Q1-2019
61	SHIP CONSTRUCTION	Cavan	Butlersbridge	4	*N/A							Q1-2018
62	SHIP CONSTRUCTION	Cavan	Woodlands, Ballyhaise	8	*N/A							Q4-2018
63	SHIP CONSTRUCTION	Cavan	Butlersbridge (Phase 1)	2	*N/A							Q2-2017
64	SHIP CONSTRUCTION	Cavan	Clones Road, Butlersbridge	2	*N/A				Stage 3 approved Q3-2018, the scheme is now approved to proceed to tender.			
65	SHIP CONSTRUCTION	Cavan	Corstruce, Ballinagh	4	*N/A					Stage 4 approved Q3-2019, the scheme is fully approved.		
66	SHIP CONSTRUCTION	Cavan	Main Street, Mullagh	19	*N/A			Stage 2 approved Q2-2019, full design/tender being prepared.				
67	SHIP CONSTRUCTION	Cavan	Elm Grove, Main St, Cavan Town	13	*N/A			Stage 1 approved Q1-2018, outline design and costs being prepared.				
68	SHIP CONSTRUCTION	Cavan	Cavan Road, Ballinagh	15	*N/A			Stage 1 approved Q1-2019, outline design and costs being prepared.				
69	SHIP CONSTRUCTION	Cavan	Main St., Butlersbridge	6	*N/A			Stage 1 approved Q1-2019, outline design and costs being prepared.				
70	SHIP CONSTRUCTION	Cavan	Cluain Dara, Kingscourt	3	*N/A			Stage 1 approved Q1-2019, outline design and costs being prepared.				
71	SHIP CONSTRUCTION	Cavan	Magheranure, Cootehill, Co. Cavan	22	*N/A			Stage 1 approved Q2-2019, outline design and costs being prepared.				
72	SHIP CONSTRUCTION TURNKEY	Cavan	Ashgrove, Derrylurgan, Ballyjamesduff	3	*N/A							Q2-2019
73	SHIP CONSTRUCTION TURNKEY	Cavan	Ashgrove, Derrylurgan, Ballyjamesduff (Phase 2)	4	*N/A							Q2-2019
74	SHIP CONSTRUCTION TURNKEY	Cavan	Ashgrove, Derrylurgan, Ballyjamesduffy (Phase 3)	7	*N/A							Q2-2019
75	CALF Construction	Clare	Revised - Bruachlan, Westbury, Co Clare (Phase 1)	22	Co-operative Housing Ireland						Q1-2017	
76	CALF Turnkey	Clare	Acha Bhile, Loughville, Lahinch Road, Ennis, Co Clare (Phase 1)	12	Cluid Housing							Q2-2018
77	CALF Turnkey	Clare	Acha Bhile, Loughville, Lahinch Road, Ennis, Co Clare (Phase 2)	18	Cluid Housing							Q4-2018
78	CALF Turnkey	Clare	Cluain Ros Leamhan, Roslevan, Tulla Road, Ennis, Co. Clare (Phase 1)	3	Co-operative Housing Ireland							Q4-2018
79	CALF Turnkey	Clare	Cluain Ros Leamhan, Roslevan, Tulla Road, Ennis, Co. Clare (Phase 2)	2	Co-operative Housing Ireland							Q2-2019

80	CALF Turnkey	Clare	Gleann Cora, Newmarket on Fergus, Co. Clare (Phase 1)*	31	Co-operative Housing Ireland				Q2-2019		
81	CALF Turnkey	Clare	Lios Anama, Sixmilebridge, Clare (Phase 1)	28	Co-operative Housing Ireland						Q4-2017
82	CALF Turnkey	Clare	Tullyvarraga, Shannon, Co. Clare (Phase 1)*	47	Co-operative Housing Ireland					Q1-2018	
83	CAS CONSTRUCTION	Clare	Caheercalla, Ennis (Phase 2)	15	Cuan an Chlair Ltd					Q3-2019	
84	CAS CONSTRUCTION	Clare	Laurel Lodge, Clare Road, Ennis	3	Society of Saint Vincent de Paul						Q4-2016
85	CAS CONSTRUCTION	Clare	Monaskeha Heights	4	Newgrove Housing Association Ltd						Q3-2019
86	CAS CONSTRUCTION	Clare	Roo East	4	Thomond Housing Association Ltd						Q4-2018
87	CAS CONSTRUCTION	Clare	9 Elmwood, Ballycannon Heights, Meelick	4	Thomond Housing Association Ltd						Q1-2019
88	CAS CONSTRUCTION	Clare	Teach Rua, Edenvale Ennis	4	Newgrove Housing Association Ltd	Stage 1 approved Q2-2019, outline design and costs being prepared.					
89	CAS CONSTRUCTION TURNKEY	Clare	Haggard View, Clarecastle (Phase 2)	2	Anvers Housing Association Ltd						Q2-2018
90	CAS CONSTRUCTION TURNKEY	Clare	Haggard View, Clarecastle (Phase 1)	2	Anvers Housing Association Ltd						Q1-2018
91	PUBLIC PRIVATE PARTNERSHIP (Bundle 2)	Clare	Shannon East	51	*N/A				Q2-2019		
92	SHIP CONSTRUCTION	Clare	Cappagh Lodge, Sixmilebridge	2	*N/A				Stage 4 approved Q2-2019, the scheme is fully approved.		
93	SHIP CONSTRUCTION	Clare	St. Michaels Place, Kilmihil	2	*N/A				Stage 4 approved Q2-2019, the scheme is fully approved.		
94	SHIP CONSTRUCTION	Clare	Roslevan, Ennis	8	*N/A					Q2-2019	
95	SHIP CONSTRUCTION	Clare	Feakle	13	*N/A					Q4-2018	
96	SHIP CONSTRUCTION	Clare	Glor Srutha, Knockbrack Lower, Clonlara	9	*N/A					Q4-2018	
97	SHIP CONSTRUCTION	Clare	Seaview Park, Quilty	18	*N/A					Q2-2019	
98	SHIP CONSTRUCTION	Clare	Ashline, Kilrush Road, Ennis	40	*N/A		Stage 2 approved Q2-2019, full design/tender being prepared.				
99	SHIP CONSTRUCTION	Clare	Miltown Malbay	27	*N/A		Stage 2 approved Q3-2019, full design/tender being prepared.				

100	SHIP CONSTRUCTION	Clare	Doonaun, Tulla	25	*N/A	Stage 1 approved Q1-2019, outline design and costs being prepared.					
101	SHIP CONSTRUCTION	Clare	Boheraroan, Newmarket-on-Fergus	18	*N/A	Stage 1 approved Q1-2019, outline design and costs being prepared.					
102	SHIP CONSTRUCTION TURNKEY	Clare	River View, School Road, Corofin	2	*N/A						Q4-2018
103	CALF Construction	Cork City	Green Lane, Blackpool, Cork City (Phase 1)	112	Cluid Housing				Q2-2019		
104	CALF Construction	Cork City	Lower Glanmire Road, Cork City (Phase 1)	8	Galtan Ltd					Q1-2019	
105	CALF Construction	Cork City	Lr. Glanmire Road & 2 Braemer, Cork (Phase 1)	3	Galtan Ltd						Q1-2018
106	CALF Construction	Cork City	Lr. Glanmire Road & 2 Braemer, Cork (Phase 2)	3	Galtan Ltd						Q4-2018
107	CALF Turnkey	Cork City	5 units, Shandon Street, Cork (Phase 1)	5	Circle Voluntary Housing Association Ltd						Q3-2019
108	CALF Turnkey	Cork City	Hereford Place, Ballymacthomas Street, Cork City (Phase 1)*	19	Respond				Q3-2019		
109	CALF Turnkey	Cork City	Leeside Apartments, Bachelors Quay, Cork City (Phase 1)	72	Cluid Housing						Q4-2018
110	CALF Turnkey	Cork City	Leeside Apartments, Bachelors Quay, Cork City (Phase 2)	6	Cluid Housing						Q3-2019
111	CALF Turnkey	Cork City	Millerd Street, Cork (Phase 1)	25	Respond					Q1-2019	
112	CALF Turnkey	Cork City	North Abbey Street, Cork City (Phase 1)	6	Respond						Q4-2018
113	CALF Turnkey	Cork City	Revised-The Meadows, Knocknacullen East, Gurrabraher, Cork (Phase 1)	31	Túath Housing Association Ltd						Q4-2018
114	CALF Turnkey	Cork City	Revised-The Meadows, Knocknacullen East, Gurrabraher, Cork (Phase 2)	21	Túath Housing Association Ltd					Q1-2018	
115	CALF Turnkey	Cork City	The Meadows (Phase 2) Gurrabraher, Cork City (Phase 1)	17	Túath Housing Association Ltd					Q1-2019	
116	CALF Turnkey	Cork City	Togher Cross, Lehenaghmore, Co. Cork (Phase 1)	9	Cluid Housing					Q3-2018	
117	CAS CONSTRUCTION	Cork City	Edel House, Grattan Street	37	Good Shepherd Services Ltd					Q2-2019	
118	CAS CONSTRUCTION	Cork City	Saint Vincent's Convent, Vincent's Ave/St. Mary's Street	25	Respond	Stage 1 approved Q2-2015, outline design and costs being prepared.					
119	CAS CONSTRUCTION	Cork City	Thomas Davis Street (Phase 1)	28	Respond		Stage 2 approved Q4-2017, full design/tender being prepared.				

120	CAS CONSTRUCTION	Cork City	Ceanncora Lawn, Ballinlough	1	Cork Mental Health Voluntary Housing Association Ltd							Q3-2018
121	CAS CONSTRUCTION	Cork City	St. Joachim & Anne's, Anglesea Street	8	Simon Community : Cork Simon						Q3-2019	
122	CAS CONSTRUCTION	Cork City	27-29 Dublin Street, Blackpool	10	Respond							Q3-2018
123	REGENERATION	Cork City	Phase 1 B Knocknaheeny	29	*N/A							Q4-2017
124	REGENERATION	Cork City	Phase 2A Knocknaheeny	47	*N/A						Q2-2018	
125	REGENERATION	Cork City	Phase 1 C Knocknaheeny	41	*N/A		Stage 2 approved Q2-2018, full design/tender being prepared.					
126	REGENERATION	Cork City	Phase 2 B Knocknaheeny	38	*N/A		Stage 2 approved Q2-2018, full design/tender being prepared.					
127	REGENERATION	Cork City	Phase 2C Knocknaheeny	24	*N/A					Stage 4 approved Q3-2019, the scheme is fully approved.		
128	REGENERATION	Cork City	Foyle Avenue Infill Housing Development, Foyle Avenue, Knocknaheeny, Cork	2	*N/A		Stage 2 approved Q3-2019, full design/tender being prepared.					
129	REGENERATION	Cork City	Ardmore Avenue, Knocknaheeny, Cork	1	*N/A		Stage 2 approved Q3-2019, full design/tender being prepared.					
130	REGENERATION	Cork City	Phase 3B	62	*N/A	Stage 1 approved Q2-2019, outline design and costs being prepared.						
131	SHIP CONSTRUCTION	Cork City	Arus Mhuire	30	*N/A							Q4-2018
132	SHIP CONSTRUCTION	Cork City	Barrack Street	32	*N/A					Stage 4 approved Q1-2018, the scheme is fully approved.		
133	SHIP CONSTRUCTION	Cork City	FaranFerris	5	*N/A						Q2-2018	
134	SHIP CONSTRUCTION	Cork City	High Street	9	*N/A						Q4-2018	
135	SHIP CONSTRUCTION	Cork City	Tramore Road	4	*N/A							Q4-2018
136	SHIP CONSTRUCTION	Cork City	Whites Street	43	*N/A						Q3-2018	
137	SHIP CONSTRUCTION	Cork City	Woods Street	16	*N/A					Stage 4 approved Q1-2018, the scheme is fully approved.		
138	SHIP CONSTRUCTION	Cork City	Church Road, Blackrock	43	*N/A							Q3-2018
139	SHIP CONSTRUCTION	Cork City	1-5, Ard Aoibhinn, Banduff, Mayfield	5	*N/A							Q3-2018

140	SHIP CONSTRUCTION	Cork City	Corcorans Quay	3	*N/A					Q2-2018	
141	SHIP CONSTRUCTION	Cork City	Blarney Street	25	*N/A					Q2-2018	
142	SHIP CONSTRUCTION	Cork City	Ballinure Road, Cork City	5	*N/A				Stage 4 approved Q3-2018, the scheme is fully approved.		
143	SHIP CONSTRUCTION	Cork City	Moss Lane, Riverway, Cork	5	*N/A				Stage 4 approved Q3-2018, the scheme is fully approved.		
144	SHIP CONSTRUCTION	Cork City	7-11 Gerald Griffin Street, Cork	13	*N/A					Q2-2019	
145	SHIP CONSTRUCTION	Cork City	29/30 Lower John Street, Cork	17	*N/A					Q1-2019	
146	SHIP CONSTRUCTION	Cork City	Skehard Road, Blackrock, Cork	16	*N/A				Stage 4 approved Q2-2019, the scheme is fully approved.		
147	SHIP CONSTRUCTION	Cork City	Coach Street, Cork	13	*N/A				Stage 4 approved Q2-2019, the scheme is fully approved.		
148	SHIP CONSTRUCTION	Cork City	Shanakiel Road, Cork	20	*N/A				Stage 4 approved Q2-2019, the scheme is fully approved.		
149	SHIP CONSTRUCTION	Cork City	Spring Lane, Blackpool, Cork	8	*N/A				Stage 4 approved Q2-2019, the scheme is fully approved.		
150	SHIP CONSTRUCTION	Cork City	Glen Ryan Road, Cork	9	*N/A				Stage 4 approved Q2-2019, the scheme is fully approved.		
151	SHIP CONSTRUCTION	Cork City	Poulavone, Ballincollig	57	*N/A					Q3-2019	
152	SHIP CONSTRUCTION	Cork City	The Meadows, Knocknacullen	1	*N/A						Q3-2016
153	SHIP CONSTRUCTION	Cork City	Boyces Street	51	*N/A			Stage 3 approved Q1-2019, the scheme is now approved to proceed to tender.			
154	SHIP CONSTRUCTION	Cork City	Shandon Street/John Philpott Curran Street	9	*N/A				Stage 4 approved Q1-2019, the scheme is fully approved.		
155	SHIP CONSTRUCTION	Cork City	St. Johns Well	6	*N/A					Q4-2018	
156	SHIP CONSTRUCTION	Cork City	Churchfield Place East	3	*N/A						Q4-2018
157	SHIP CONSTRUCTION	Cork City	Deanrock, Togher	8	*N/A						Q4-2018
158	SHIP CONSTRUCTION	Cork City	Gerald Griffin Street	42	*N/A				Stage 4 approved Q3-2017, the scheme is fully approved.		
159	SHIP CONSTRUCTION	Cork City	Cappanoole	2	*N/A						Q4-2016

160	SHIP CONSTRUCTION	Cork City	Bramble Cottages	5	*N/A		Stage 2 approved Q3-2019, full design/tender being prepared.					
161	SHIP CONSTRUCTION	Cork City	Errigal Heights, The Glen, Cork City	20	*N/A	Stage 1 approved Q3-2018, outline design and costs being prepared.						
162	SHIP CONSTRUCTION	Cork City	Glenamoy Lawn, Mayfield, Cork	2	*N/A		Stage 2 approved Q3-2019, full design/tender being prepared.					
163	SHIP CONSTRUCTION	Cork City	Deanrock, Togher (Phase 2)	7	*N/A							Q1-2019
164	SHIP CONSTRUCTION	Cork City	Hollywood Estate Infill Housing, Blarney Road, Cork	7	*N/A	Stage 1 approved Q2-2019, outline design and costs being prepared.						
165	SHIP CONSTRUCTION	Cork City	Deanrock, Togher (Phase 3)	50	*N/A							Q3-2019
166	SHIP CONSTRUCTION	Cork City	Clover Hill Court, Bessboro Road, Mahon, Cork	51	*N/A	Stage 1 approved Q2-2019, outline design and costs being prepared.						
167	SHIP CONSTRUCTION	Cork City	Westside, Model Farm Road, Cork	32	*N/A	Stage 1 approved Q2-2019, outline design and costs being prepared.						
168	SHIP CONSTRUCTION	Cork City	Gerald Griffin Apartments - Block 7, North Monastery Road / St. Vincent's Road, Cork	6	*N/A	Stage 1 approved Q3-2019, outline design and costs being prepared.						
169	SHIP CONSTRUCTION TURNKEY	Cork City	1-4 Marble Lane	4	*N/A							Q4-2017
170	SHIP CONSTRUCTION TURNKEY	Cork City	Sheridan Park, Tramore Road	28	*N/A							Q4-2016
171	SHIP CONSTRUCTION TURNKEY	Cork City	37-39 Dublin Street, Blackpool, Cork	5	*N/A							Q2-2018
172	SHIP CONSTRUCTION TURNKEY	Cork City	6-10, Ard Aoibhinn, Banduff, Mayfield	5	*N/A							Q4-2018
173	SHIP CONSTRUCTION TURNKEY	Cork City	2 Deanrock Cottages, Togher	4	*N/A							Q4-2018
174	SHIP CONSTRUCTION TURNKEY	Cork City	258 & 259 Blarney Street, Cork	2	*N/A							Q1-2018
175	SHIP CONSTRUCTION TURNKEY	Cork City	1 & 2 The Groves, Skehard Road, Cork	2	*N/A							Q2-2018
176	SHIP CONSTRUCTION TURNKEY	Cork City	3B & 9B South Terrace Court, South Terrace, Cork	2	*N/A							Q4-2018
177	SHIP CONSTRUCTION TURNKEY	Cork City	Ballinlough Road / Knockree Lawn, Ballinlough, Cork	6	*N/A							Q2-2019
178	SHIP CONSTRUCTION TURNKEY	Cork City	Ard na Ri, Banduff Road, Cork	10	*N/A					Stage 4 approved Q2-2019, the scheme is fully approved.		
179	SHIP CONSTRUCTION TURNKEY	Cork City	Gearney's Boreen, Commons Road, Cork	3	*N/A							Q2-2019

180	SHIP CONSTRUCTION TURNKEY	Cork City	Ard na Ri, Banduff Road, Cork (Phase 2)	10	*N/A				Stage 4 approved Q2-2019, the scheme is fully approved.		
181	SHIP CONSTRUCTION TURNKEY	Cork City	134A Eagle Valley, Sarsfield Road	1	*N/A					Q1-2018	
182	CALF Construction	Cork County	Duntahane, Fermoy, Co. Cork (Phase 1)	46	Respond					Q4-2018	
183	CALF Construction	Cork County	Firgrove Harrisons lane (Phase 1)	6	Co-operative Housing Ireland						Q4-2017
184	CALF Construction	Cork County	Post Tender - Radharc An tSaile, Cappagh, Ballynacubby, Kinsale, Co Cork (Phase 1)	40	Cluid Housing					Q4-2018	
185	CALF Turnkey	Cork County	3 units, Mullavale, Castletownroche, Co. Cork (Phase 1)	3	Respond						Q2-2019
186	CALF Turnkey	Cork County	Beach Road, Passage West, Co. Cork (Phase 1)	3	Cluid Housing						Q4-2017
187	CALF Turnkey	Cork County	College Manor, Cobh (Phase 1)	10	Túath Housing Association Ltd						Q4-2016
188	CALF Turnkey	Cork County	Coolroe, Ballincollig, Co. Cork (Phase 1)*	44	Respond					Q3-2019	
189	CALF Turnkey	Cork County	Market Green, Knockgriffin, Midleton, Co. Cork (Phase 1)	20	Respond					Q4-2018	
190	CALF Turnkey	Cork County	Market Green, Knockgriffin, Midleton, Co. Cork (Phase 2)*	22	Respond					Q4-2018	
191	CALF Turnkey	Cork County	Mullavale, Castletownroche, Co. Cork (Phase 1)	6	Respond						Q4-2018
192	CALF Turnkey	Cork County	Tanners Field, Bandon, Co Cork (Phase 1)	11	Túath Housing Association Ltd						Q3-2019
193	CALF Turnkey	Cork County	Ticknock, Cobh, Cork (Phase 1)	8	Respond						Q4-2018
194	CALF Turnkey	Cork County	Weston, Carrigaline, Co. Cork (Phase 1)	7	Respond						Q2-2018
195	CAS CONSTRUCTION	Cork County	Sisters of Mercy Church and Convent at Knocknamuck, Bantry Bay	16	Cluid Housing Association		Stage 2 approved Q1-2019, full design/tender being prepared.				
196	CAS CONSTRUCTION	Cork County	Cuan Barra, Kilmore, Ballingeary	3	Coiste Tithe Uíbh Laoire Teoranta						Q3-2018
197	CAS CONSTRUCTION	Cork County	Caim Hill, Townlands, Rosscarbery	9	Rosscarbery Housing Association Ltd						Q1-2019
198	CAS CONSTRUCTION	Cork County	Avenue House, Bandon	9	Bandon Geriatric & Community Council						Q1-2018
199	CAS CONSTRUCTION	Cork County	Church View, Love Lane, Charleville	4	Charleville Care Project Ltd					Q1-2019	

220	SHIP CONSTRUCTION	Cork County	Newtown House , Bantry	1	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
221	SHIP CONSTRUCTION	Cork County	Fairfield, Masseytown, Macroom	7	*N/A						Q4-2018
222	SHIP CONSTRUCTION	Cork County	12 & 14 Droum, Castletownbere	2	*N/A						Q4-2018
223	SHIP CONSTRUCTION	Cork County	Kilnagleary, Carrigaline (Phase 4)	15	*N/A		Stage 2 approved Q1-2019, full design/tender being prepared.				
224	SHIP CONSTRUCTION	Cork County	Oliver Plunkett Hill, Fermoy	10	*N/A						Q2-2017
225	SHIP CONSTRUCTION	Cork County	Townsend Street, Skibbereen	6	*N/A					Q3-2019	
226	SHIP CONSTRUCTION	Cork County	Forest View, Mallow	10	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
227	SHIP CONSTRUCTION	Cork County	11/10 Harbour Hill, Cobh	1	*N/A						Q2-2018
228	SHIP CONSTRUCTION	Cork County	Kilnagleary Carrigaline	10	*N/A						Q4-2018
229	SHIP CONSTRUCTION	Cork County	Kilnagleary Carrigaline (Phase 1A & 1B (ii))	16	*N/A						Q1-2019
230	SHIP CONSTRUCTION	Cork County	Kilnagleary Carrigaline (Phase 1C)	18	*N/A						Q1-2019
231	SHIP CONSTRUCTION	Cork County	Kearney's field Dunmanway	18	*N/A			Stage 3 approved Q3-2019, the scheme is now approved to proceed to tender.			
232	SHIP CONSTRUCTION	Cork County	Madonna House, Ballincollig (Phase 2)	6	*N/A	Stage 1 approved Q2-2018, outline design and costs being prepared.					
233	SHIP CONSTRUCTION	Cork County	Richmond Court, Bandon	4	*N/A	Stage 1 approved Q2-2018, outline design and costs being prepared.					
234	SHIP CONSTRUCTION	Cork County	Brigown Road, Mitchelstown	8	*N/A					Q2-2019	
235	SHIP CONSTRUCTION	Cork County	Sleaveen Sleaveen East, Macroom	8	*N/A			Stage 3 approved Q2-2019, the scheme is now approved to proceed to tender.			
236	SHIP CONSTRUCTION	Cork County	Kilnagleary, Carrigaline Phase 1B	5	*N/A						Q4-2018
237	SHIP CONSTRUCTION	Cork County	Tudor Grove, Ballincollig	16	*N/A					Q2-2019	
238	SHIP CONSTRUCTION	Cork County	Pound Lane, Kilworth	6	*N/A	Stage 1 approved Q2-2019, outline design and costs being prepared.					
239	SHIP CONSTRUCTION	Cork County	24 Glenview Terrace Lyre Co Cork	1	*N/A	Stage 1 approved Q2-2019, outline design and costs being prepared.					

240	SHIP CONSTRUCTION	Cork County	Broomfield West, Avoncore, Midelton	10	*N/A	Stage 1 approved Q2-2019, outline design and costs being prepared.					
241	SHIP CONSTRUCTION	Cork County	Uplands (Phase 2), College Road, Fermoy	11	*N/A		Stage 2 approved Q3-2019, full design/tender being prepared.				
242	SHIP CONSTRUCTION	Cork County	Lissoran, Ballinspittle	4	*N/A		Stage 2 approved Q3-2019, full design/tender being prepared.				
243	SHIP CONSTRUCTION	Cork County	Tower View/Cúirt na Silíni, Cloyne, East Cork - Phase 2	2	*N/A				Stage 4 approved Q2-2018, the scheme is fully approved.		
244	SHIP CONSTRUCTION TURNKEY	Cork County	Church Road/Station Road, Carrigtwohill	18	*N/A						Q2-2018
245	SHIP CONSTRUCTION TURNKEY	Cork County	Inis Alainn & Castleoaks, Bandon	11	*N/A						Q4-2017
246	SHIP CONSTRUCTION TURNKEY	Cork County	Gleann Tuairigh, Youghal	3	*N/A						Q4-2018
247	SHIP CONSTRUCTION TURNKEY	Cork County	Millview Road, Kanturk	21	*N/A					Q3-2018	
248	SHIP CONSTRUCTION TURNKEY	Cork County	Clondulane, Fermoy	2	*N/A						Q4-2017
249	SHIP CONSTRUCTION TURNKEY	Cork County	College Wood, Cobh	31	*N/A						Q4-2017
250	SHIP CONSTRUCTION TURNKEY	Cork County	Castletreasure, Douglas (Phase 3)	12	*N/A						Q4-2017
251	SHIP CONSTRUCTION TURNKEY	Cork County	Crann Ard, Fermoy	17	*N/A					Q4-2017	
252	SHIP CONSTRUCTION TURNKEY	Cork County	CulAird Carraigtwohill	29	*N/A						Q4-2017
253	SHIP CONSTRUCTION TURNKEY	Cork County	Castletreasure, Douglas	12	*N/A						Q1-2017
254	SHIP CONSTRUCTION TURNKEY	Cork County	Castletreasure, Douglas (Phase 2)	16	*N/A						Q1-2017
255	SHIP CONSTRUCTION TURNKEY	Cork County	Claragh Road, Millstreet	5	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
256	SHIP CONSTRUCTION TURNKEY	Cork County	St. Mary's Road, Dunmanway	14	*N/A					Q3-2018	
257	SHIP CONSTRUCTION TURNKEY	Cork County	Glanworth, Fermoy	10	*N/A				Stage 4 approved Q1-2018, the scheme is fully approved.		
258	SHIP CONSTRUCTION TURNKEY	Cork County	Quartermown, Mallow	5	*N/A					Q2-2019	
259	SHIP CONSTRUCTION TURNKEY	Cork County	HazelBrook, Ballyvinter, Mallow	8	*N/A					Q1-2019	

260	SHIP CONSTRUCTION TURNKEY	Cork County	Beacon Point, Baltimore	6	*N/A							Q2-2019
261	SHIP CONSTRUCTION TURNKEY	Cork County	Corrin View, Fermoy	6	*N/A							Q2-2019
262	SHIP CONSTRUCTION TURNKEY	Cork County	No. 43 & No. 50 Chapel Court, Skibbereen	2	*N/A							Q3-2018
263	SHIP CONSTRUCTION TURNKEY	Cork County	Cul Na Smear, Bandon	14	*N/A							Q4-2018
264	SHIP CONSTRUCTION TURNKEY	Cork County	Glen Dara, Ard Cashel, Watergrasshill	6	*N/A							Q4-2018
265	SHIP CONSTRUCTION TURNKEY	Cork County	Clarendon Brooks, Carrs Hill, Douglas	9	*N/A							Q2-2019
266	SHIP CONSTRUCTION TURNKEY	Cork County	Sweetfields, Youghal	15	*N/A						Q1-2019	
267	SHIP CONSTRUCTION TURNKEY	Cork County	Lismire	4	*N/A							Q4-2018
268	SHIP CONSTRUCTION TURNKEY	Cork County	Rylane, Mount Rivers, Co. Cork.	3	*N/A					Stage 4 approved Q2-2018, the scheme is fully approved.		
269	SHIP CONSTRUCTION TURNKEY	Cork County	Clarendon Brooks, Carrs Hill, Douglas Phase 3	11	*N/A						Q1-2019	
270	SHIP CONSTRUCTION TURNKEY	Cork County	Seafield, Bantry,	3	*N/A						Q3-2018	
271	SHIP CONSTRUCTION TURNKEY	Cork County	Eyerias, Castletownbere	6	*N/A						Q2-2019	
272	SHIP CONSTRUCTION TURNKEY	Cork County	Parklands, Youghal	13	*N/A							Q4-2018
273	SHIP CONSTRUCTION TURNKEY	Cork County	Oliver Plunkett Place, Doneraile	6	*N/A						Q3-2018	
274	SHIP CONSTRUCTION TURNKEY	Cork County	No.9 and No.10 Chapel Court, Skibbereen,	2	*N/A							Q4-2018
275	SHIP CONSTRUCTION TURNKEY	Cork County	Tir Cluain, Middleton	8	*N/A							Q4-2018
276	SHIP CONSTRUCTION TURNKEY	Cork County	College Mews, Cobh	6	*N/A							Q4-2018
277	SHIP CONSTRUCTION TURNKEY	Cork County	Milleenacola, Bantry	51	*N/A						Q2-2019	
278	SHIP CONSTRUCTION TURNKEY	Cork County	Rathcormac	4	*N/A							Q4-2018
279	SHIP CONSTRUCTION TURNKEY	Cork County	Fairgreen, Mallow	12	*N/A					Stage 4 approved Q3-2018, the scheme is fully approved.		

300	SHIP CONSTRUCTION TURNKEY	Cork County	Baltimore, West Cork	12	*N/A					Q3-2019	
301	SHIP CONSTRUCTION TURNKEY	Cork County	No. 11 & 12 Chapel Court, Skibbereen, Co. Cork	2	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
302	SHIP CONSTRUCTION TURNKEY	Cork County	Cluain Ard, Freemount	4	*N/A					Q3-2019	
303	SHIP CONSTRUCTION TURNKEY	Cork County	Glengarriff	5	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
304	SHIP CONSTRUCTION TURNKEY	Cork County	The Cove, Glandore, Co. Cork	4	*N/A					Q3-2019	
305	SHIP CONSTRUCTION TURNKEY	Cork County	Copper Point, Schull, Co. Cork	7	*N/A				Stage 4 approved Q2-2019, the scheme is fully approved.		
306	SHIP CONSTRUCTION TURNKEY	Cork County	An Tui, Lisgoold, Leamlara	3	*N/A					Q1-2019	
307	SHIP CONSTRUCTION TURNKEY	Cork County	Millstreet Road, Macroom	12	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
308	SHIP CONSTRUCTION TURNKEY	Cork County	Clarendon Brooks, Carrs Hill, Douglas Phase 2	14	*N/A				Stage 4 approved Q2-2018, the scheme is fully approved.		
309	SHIP CONSTRUCTION TURNKEY	Cork County	Cluain Cairn, Station Road, Carrigtwohill	19	*N/A					Q2-2019	
310	SHIP CONSTRUCTION TURNKEY	Cork County	Glenbeg The Beeches, Boherbue	12	*N/A					Q1-2019	
311	SHIP CONSTRUCTION TURNKEY	Cork County	No. 4, 52 & 53 Chapel Court, Skibbereen, Co. Cork	3	*N/A					Q1-2019	
312	SHIP CONSTRUCTION TURNKEY	Cork County	Millview Road, Kanturk	11	*N/A					Q3-2018	
313	SHIP CONSTRUCTION TURNKEY	Cork County	An Tui, Lisgoold, Leamlara, Co. Cork	1	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
314	SHIP CONSTRUCTION TURNKEY	Cork County	HazelBrook, Ballyvinter, Mallow Phase 2	8	*N/A						Q3-2019
315	CALF Construction	DLR	Abbeyview, Monkstown, Co. Dublin (Phase 1)	11	Cluid Housing					Q3-2019	
316	CALF Construction	DLR	Cromlech Fields, Loughlinstown, Ballybrack, Dublin (Phase 1)	34	Co-operative Housing Ireland				Q1-2019		
317	CALF Construction	DLR	Enniskerry Road, Sandyford, Dublin 18 (Phase 1)	53	Respond					Q3-2019	
318	CALF Construction	DLR	Enniskerry Road, Sandyford, Dublin 19, (Phase 1)	52	Túath Housing Association Ltd					Q3-2019	
319	CALF Turnkey	DLR	Ardilea Crescent, Clonskeagh, Dublin 14 (Phase 1)*	8	Túath Housing Association Ltd						Q4-2018

360	CALF Turnkey	Donegal	Ballaghderg, Letterkenny, Co Donegal (Phase 1)*	33	Respond					Q4-2017	
361	CALF Turnkey	Donegal	Forge Road, Donegal (Phase 1)	4	Cluid Housing						Q3-2016
362	CAS CONSTRUCTION	Donegal	Glenrowan House, Drumkeen, Stranorlar	5	Apex Housing Association				Stage 4 approved Q2-2019, the scheme is fully approved.		
363	CAS CONSTRUCTION	Donegal	Willowbrook, Glencar, Letterkenny	40	Apex Housing Association		Stage 2 approved Q3-2019, full design/tender being prepared.				
364	CAS CONSTRUCTION	Donegal	Meenmore, Dungloe	15	County Donegal Parents and Friends Housing Association Ltd			Stage 3 approved Q3-2018, the scheme is now approved to proceed to tender.			
365	CAS CONSTRUCTION	Donegal	Railway Park, Drumrooske, Donegal Town	10	Oaklee Housing Trust					Q2-2019	
366	CAS CONSTRUCTION	Donegal	Dunshenny House, Derry Road, Carndonagh	5	Apex Housing Association						Q2-2018
367	CAS CONSTRUCTION	Donegal	Raphoe Road, Castlefinn	20	Habinteg Housing Association (Ireland) Ltd	Stage 1 approved Q1-2018, outline design and costs being prepared.					
368	SHIP CONSTRUCTION	Donegal	Donegal Road, Ballybofey	14	*N/A			Stage 3 approved Q3-2019, the scheme is now approved to proceed to tender.			
369	SHIP CONSTRUCTION	Donegal	Meadow Hill, Raphoe	11	*N/A			Stage 3 approved Q2-2019, the scheme is now approved to proceed to tender.			
370	SHIP CONSTRUCTION	Donegal	Radharc na Tra Breige, Malin (Phase 3)	8	*N/A					Q2-2019	
371	SHIP CONSTRUCTION	Donegal	Cois Abhainn, St Johnston (Phase 2)	6	*N/A					Q1-2019	
372	SHIP CONSTRUCTION	Donegal	Emerald Drive, Killybegs (Phase 6)	9	*N/A					Q4-2018	
373	SHIP CONSTRUCTION	Donegal	Long Lane, Letterkenny	29	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
374	SHIP CONSTRUCTION	Donegal	Rockytown, Buncrana (Phase 1)	21	*N/A			Stage 3 approved Q3-2019, the scheme is now approved to proceed to tender.			
375	SHIP CONSTRUCTION	Donegal	Manorcunningham (Phase 2)	8	*N/A						Q4-2018
376	SHIP CONSTRUCTION	Donegal	Abbots Wood, Carndonagh (Ph 2)	4	*N/A						Q4-2018
377	SHIP CONSTRUCTION	Donegal	Ardara (Phase 3)	8	*N/A						Q2-2017
378	SHIP CONSTRUCTION	Donegal	Newtoncunningham	7	*N/A						Q4-2018
379	SHIP CONSTRUCTION	Donegal	Railway Park, Drumrooske, Donegal Town	24	*N/A					Q2-2019	

400	CALF Construction	Dublin City	Post Tender - Wad River Close Phase 2, Ballymun, Dublin 9 (Phase 1)	9	Cluid Housing					Q4-2018	
401	CALF Construction	Dublin City	POST TENDER Dolphin Park, Rialto, Dublin 8 (Phase 1)	43	Fold Housing Association Ireland Ltd					Q2-2018	
402	CALF Construction	Dublin City	Post Tender Johns Lane West Dublin 8 (Phase 1)	31	Focus Ireland						Q4-2018
403	CALF Construction	Dublin City	POST TENDER, Poplar Row, Ballybough, Dublin 3 (Phase 1)	29	Oaklee Housing					Q3-2018	
404	CALF Construction	Dublin City	Revised - Dominic Place, Dublin (Phase 1)	9	The Paddy McGrath Housing Project					Q2-2019	
405	CALF Construction	Dublin City	Revised - St Mary's Mansions, Dublin 1 (Phase 1)	80	Cluid Housing					Q4-2017	
406	CALF Construction	Dublin City	Revised Post Tender - Raleigh Square, Crumlin (Phase 1)	33	Túath Housing Association Ltd					Q2-2017	
407	CALF Construction	Dublin City	Richmond Road, Dublin 9 (Phase 1)	40	Co-operative Housing Ireland						Q4-2018
408	CALF Turnkey	Dublin City	An Riasc, Finglas, Phase 1,2,3 and 4 (Phase 1)	14	Túath Housing Association Ltd						Q4-2016
409	CALF Turnkey	Dublin City	An Riasc, Finglas, Phase 1,2,3 and 4 (Phase 2)	21	Túath Housing Association Ltd						Q1-2017
410	CALF Turnkey	Dublin City	An Riasc, Finglas, Phase 1,2,3 and 4 (Phase 3)	10	Túath Housing Association Ltd						Q2-2017
411	CALF Turnkey	Dublin City	An Riasc, Finglas, Phase 1,2,3 and 4 (Phase 4)	3	Túath Housing Association Ltd						Q3-2017
412	CALF Turnkey	Dublin City	An Riasc, Finglas, Phase 1,2,3 and 4 (Phase 5)	1	Túath Housing Association Ltd						Q4-2018
413	CALF Turnkey	Dublin City	Aughrim Street, Stoneybatter, Dublin 7 (Phase 1)	4	Clanmil Housing Association Ireland				Q3-2019		
414	CALF Turnkey	Dublin City	Balfe Road, Crumlin, Dublin 12 (Phase 1)*	16	Respond						Q4-2018
415	CALF Turnkey	Dublin City	Block A Northbank, Castleforbes, Dublin 1 (Phase 1)*	26	Túath Housing Association Ltd						Q2-2018
416	CALF Turnkey	Dublin City	Bluebell Avenue, Dublin 12 (Phase 1)	7	Túath Housing Association Ltd						Q4-2018
417	CALF Turnkey	Dublin City	Bow Lane West, Dublin 8 (Phase 1)	18	Oaklee Housing					Q4-2017	
418	CALF Turnkey	Dublin City	Camac Park, Bluebell, Dublin 12 (Phase 1)	5	Túath Housing Association Ltd					Q2-2019	
419	CALF Turnkey	Dublin City	Canal Meadows, Bluebell, Dublin 12 (Phase 1)	4	Túath Housing Association Ltd						Q1-2019

420	CALF Turnkey	Dublin City	Chanel College, Coolock Village, Malahide Road, Dublin 5 (Phase 1)*	16	Respond							Q4-2017
421	CALF Turnkey	Dublin City	Clongriffin, Dublin 13 (Phase 1)*	84	The Iveagh Trust							Q2-2019
422	CALF Turnkey	Dublin City	Crumlin Village, Dublin 12 (Phase 1)	3	Cluid Housing							Q2-2017
423	CALF Turnkey	Dublin City	Crumlin Village, Dublin 12 (Phase 2)	2	Cluid Housing							Q3-2017
424	CALF Turnkey	Dublin City	Merville Court, Merville Avenue, Fairview (Phase 1)	5	Co-operative Housing Ireland							Q1-2017
425	CALF Turnkey	Dublin City	Millrose House, Bluebell Avenue, Dublin 12 (Phase 1)	8	Cluid Housing							Q4-2017
426	CALF Turnkey	Dublin City	Ravensdale Court, Kimmage, Dublin 12. (Phase 1)	12	Túath Housing Association Ltd				Q3-2019			
427	CALF Turnkey	Dublin City	St Agnes Convent, Armagh Road, Crumlin, Dublin 12 (Phase 1)	97	Fold Housing Association Ireland Ltd					Q1-2018		
428	CALF Turnkey	Dublin City	Stormanstown Hall, Ballymun Road, (revised) (Phase 1)	42	Oaklee Housing							Q3-2018
429	CALF Turnkey	Dublin City	Sundrive Mews, Kimmage, Dublin 12 (Phase 1)	9	Cluid Housing					Q3-2018		
430	CALF Turnkey	Dublin City	Thornwood, Beaumont (Phase 1)	28	Túath Housing Association Ltd							Q2-2016
431	CALF Turnkey	Dublin City	Thornwood, Beaumont (Phase 2)	18	Túath Housing Association Ltd							Q4-2016
432	CALF Turnkey	Dublin City	Thornwood, Beaumont (Phase 3)	14	Túath Housing Association Ltd							Q1-2017
433	CALF Turnkey	Dublin City	Thornwood, Beaumont (Phase 4)	8	Túath Housing Association Ltd							Q1-2017
434	CALF Turnkey	Dublin City	Tonleegy Road, Dublin 5 (Phase 1)	47	Fold Housing Association Ireland Ltd							Q4-2018
435	CAS CONSTRUCTION	Dublin City	Beech Hill	19	Royal Hospital Donnybrook Voluntary Housing Association Ltd							Q4-2018
436	CAS CONSTRUCTION	Dublin City	Ellis Court, Dublin	22	Túath Housing Association Ltd					Q3-2019		
437	CAS CONSTRUCTION	Dublin City	Martanna House, High Park, Grace Park Road, Dublin 9	8	Respond							Q4-2018
438	CAS CONSTRUCTION	Dublin City	1 - 2 Rafter's Lane, Dublin 12	11	Walkinston Housing Association Ltd (WALK)						Q3-2018	
439	CAS CONSTRUCTION	Dublin City	180-187 Townsend Street	18	Peter McVerry Trust Ltd			Stage 3 approved Q4-2018, the scheme is now approved to proceed to tender.				

440	CAS CONSTRUCTION	Dublin City	Old Kilmainham Road, Dublin 8	11	Arlington Novas Ireland Ltd	Stage 1 approved Q1-2017, outline design and costs being prepared.					
441	CAS CONSTRUCTION	Dublin City	26 New Street South, Dublin 8	8	Peter McVerry Trust Ltd			Stage 3 approved Q1-2019, the scheme is now approved to proceed to tender.			
442	CAS CONSTRUCTION	Dublin City	Broome Lodge, Dunmanus, Dublin 7	10	Cluid Housing Association						Q4-2017
443	CAS CONSTRUCTION	Dublin City	St Agatha's Court, North William Street, Dublin 1	11	Peter McVerry Trust Ltd						Q2-2017
444	CAS CONSTRUCTION	Dublin City	55B Arbour Hill, Dublin 7	18	Simon Community : Dublin Simon		Stage 2 approved Q2-2018, full design/tender being prepared.				
445	CAS CONSTRUCTION	Dublin City	St. Michael's Estate, Inchicore, Dublin 8 - Housing Pilot Project	52	Circle Voluntary Housing Association Ltd		Stage 2 approved Q2-2019, full design/tender being prepared.				
446	CAS CONSTRUCTION	Dublin City	Shaw Street, Dublin 2	12	Peter McVerry Trust Ltd	Stage 1 approved Q1-2018, outline design and costs being prepared.					
447	CAS CONSTRUCTION SINGLE STAGE	Dublin City	13A Casement Drive / 307A Casement Road, Finglas, Dublin 11	4	Arlington Novas Ireland Ltd				Stage 4 approved Q3-2019, the scheme is fully approved.		
448	CAS CONSTRUCTION TURNKEY	Dublin City	61 & 63 Rathoath Avenue, Finglas, Dublin 11	6	Arlington Novas Ireland Ltd						Q3-2019
449	PUBLIC PRIVATE PARTNERSHIP (Bundle 1)	Dublin City	Ayrfield, Malahide Road	150	*N/A						Q1-2019
450	PUBLIC PRIVATE PARTNERSHIP (Bundle 1)	Dublin City	Scribblestown	70	*N/A						Q1-2019
451	REGENERATION	Dublin City	St. Teresa's Gardens	54	*N/A						Q4-2018
452	REGENERATION	Dublin City	Dolphin House, Dublin 8	100	*N/A						Q3-2018
453	REGENERATION	Dublin City	Dominick Street (East side)	72	*N/A						Q1-2019
454	REGENERATION	Dublin City	Sackville Avenue Cottages	11	*N/A			Stage 3 approved Q3-2019, the scheme is now approved to proceed to tender.			
455	REGENERATION	Dublin City	O'Devaney Gardens	56	*N/A						Q3-2018
456	REGENERATION	Dublin City	Charlemont	79	*N/A						Q4-2017
457	REGENERATION	Dublin City	Maxwell Road	9	*N/A						Q2-2016
458	REGENERATION	Dublin City	Buttercup, Darndale	19	*N/A						Q4-2017
459	REGENERATION	Dublin City	Buttercup, Darndale	9	*N/A						Q1-2018

500	CALF Turnkey	Fingal	Castlegrange Park (2) Clonsilla (Phase 4)	21	Túath Housing Association Ltd							Q1-2017
501	CALF Turnkey	Fingal	Castlegrange Park (2) Clonsilla (Phase 5)	8	Túath Housing Association Ltd							Q2-2017
502	CALF Turnkey	Fingal	Drynam Heath, Feltrim Road, Swords, Co. Dublin (Phase 1)*	17	Túath Housing Association Ltd						Q1-2019	
503	CALF Turnkey	Fingal	Lanesborough Close, Finglas, Dublin 11 (Phase 1)*	21	Cluid Housing							Q4-2018
504	CALF Turnkey	Fingal	Martello Place, Balbriggan, Co Dublin (Phase 1)	18	Respond							Q3-2018
505	CALF Turnkey	Fingal	Millers Glen, Oldtown, Swords, Co. Dublin (Phase 1)*	10	The Iveagh Trust						Q3-2018	
506	CALF Turnkey	Fingal	Millers Glen, Oldtown, Swords, Co. Dublin (Phase 2)*	18	The Iveagh Trust						Q3-2018	
507	CALF Turnkey	Fingal	Millers Glen, Phase 3, Oldtown, Swords (Phase 1)*	14	The Iveagh Trust						Q3-2018	
508	CALF Turnkey	Fingal	Northwood Green, Santry, Dublin 9 (Phase 1)*	6	Respond							Q4-2018
509	CALF Turnkey	Fingal	Northwood, Ballymun Cross, Santry, Dublin 9 (Phase 1)	25	Respond						Q3-2018	
510	CALF Turnkey	Fingal	Northwood, Ballymun Cross, Santry, Dublin 9 (Phase 2)*	30	Respond						Q3-2018	
511	CALF Turnkey	Fingal	Old Corduff Road, Blanchardstown, Dublin 15 (Phase 1)*	28	Respond						Q4-2018	
512	CALF Turnkey	Fingal	Pappan Grove, Northwood, Santry, Dublin 9 (Phase 1)*	35	Túath Housing Association Ltd							Q3-2019
513	CALF Turnkey	Fingal	St Marnock's Bay, Portmarnock, Co Dublin (Phase 1)*	10	Cluid Housing							Q4-2017
514	CALF Turnkey	Fingal	St Werburghs Court Drynam Rd Swords Co Dublin (Phase 1)*	18	Túath Housing Association Ltd							Q4-2017
515	CALF Turnkey	Fingal	Station Manor, Station Road, Portmarnock, Co. Dublin (Phase 1)*	3	Circle Voluntary Housing Association Ltd							Q2-2019
516	CALF Turnkey	Fingal	Station Manor, Station Road, Portmarnock, Co. Dublin (Phase 2)*	8	Circle Voluntary Housing Association Ltd						Q4-2017	
517	CALF Turnkey	Fingal	Taylor Hill Crescent, Balbriggan, Co. Dublin (Phase 1)	4	Cluid Housing							Q4-2018
518	CALF Turnkey	Fingal	Taylor Hill, Balbriggan, Co. Dublin (Phase 1)*	31	Cluid Housing							Q4-2018
519	CALF Turnkey	Fingal	The Hermitage, Balgriffin, Co Dublin (Phase 1)*	54	Cluid Housing							Q4-2017

540	SHIP CONSTRUCTION	Fingal	Racecourse Commons, Lusk (Phase 2.5)	25	*N/A							Q4-2018
541	SHIP CONSTRUCTION	Fingal	Tucketts Lane, Howth, Co Dublin	8	*N/A		Stage 2 approved Q2-2019, full design/tender being prepared.					
542	SHIP CONSTRUCTION	Fingal	Wellview Infill	20	*N/A		Stage 2 approved Q1-2019, full design/tender being prepared.					
543	SHIP CONSTRUCTION	Fingal	Rowlestown (Phase 3)	6	*N/A						Q2-2018	
544	SHIP CONSTRUCTION	Fingal	Rowlestown (Phase 4)	6	*N/A			Stage 3 approved Q4-2017, the scheme is now approved to proceed to tender.				
545	SHIP CONSTRUCTION	Fingal	Outlands, Rathbeale Road, Swords, Co.Dublin	11	*N/A	Stage 1 approved Q3-2019, outline design and costs being prepared.						
546	SHIP CONSTRUCTION	Fingal	Rowlestown (Phase 2)	4	*N/A							Q3-2019
547	SHIP CONSTRUCTION RAPID	Fingal	Avondale, Mulhuddart, Dublin 15	42	*N/A						Q3-2018	
548	SHIP CONSTRUCTION RAPID	Fingal	Hansfield, Ongar, Dublin 15	36	*N/A							Q3-2017
549	SHIP CONSTRUCTION RAPID	Fingal	Pinewood, Balbriggan	20	*N/A							Q2-2018
550	SHIP CONSTRUCTION RAPID	Fingal	Wellview, Mulhuddart	20	*N/A							Q4-2017
551	SHIP CONSTRUCTION RAPID	Fingal	Church Road, Mulhuddart, Dublin 15	22	*N/A						Q4-2018	
552	SHIP CONSTRUCTION TURNKEY	Fingal	Blackmills Grove, Blakestown Road, Mulhuddart	10	*N/A							Q2-2017
553	SHIP CONSTRUCTION TURNKEY	Fingal	Balgriffin Grove, Malahide Road, Balgriffin	6	*N/A							Q1-2017
554	SHIP CONSTRUCTION TURNKEY	Fingal	Hansfield (Phase 1), Ongar, Dublin 15	16	*N/A							Q1-2018
555	SHIP CONSTRUCTION TURNKEY	Fingal	Hansfield (Phase 2), Ongar, Dublin 15	16	*N/A							Q2-2018
556	SHIP CONSTRUCTION TURNKEY	Fingal	Ravenswood, North Road, Finglas (Phase 2)	2	Peter McVerry Trust Ltd							Q4-2018
557	SHIP CONSTRUCTION TURNKEY	Fingal	Boroimhe, Swords	6	*N/A							Q3-2018
558	SHIP CONSTRUCTION TURNKEY	Fingal	Cnoc Dubh, Ballyboughal	6	*N/A							Q4-2018
559	SHIP CONSTRUCTION TURNKEY	Fingal	Kenure Gate, Park Road, Rush	4	*N/A							Q4-2018

580	SHIP CONSTRUCTION	Galway City	Ballymoneen Road (Phase 1)	14	*N/A							Q2-2018
581	SHIP CONSTRUCTION	Galway City	Monivea Road, Ballybaan More	7	*N/A		Stage 2 approved Q1-2019, full design/tender being prepared.					
582	SHIP CONSTRUCTION	Galway City	Monivea Road, Ballybaan More	58	*N/A			Stage 3 approved Q2-2019, the scheme is now approved to proceed to tender.				
583	SHIP CONSTRUCTION	Galway City	Headford Road, Castlegar	70	*N/A		Stage 1 approved Q3-2018, outline design and costs being prepared.					
584	SHIP CONSTRUCTION TURNKEY	Galway City	Radharc na Gréine, (Glasshouse Site) Monivea Road (Phase 1)	6	*N/A							Q3-2019
585	SHIP CONSTRUCTION TURNKEY	Galway City	Radharc na Gréine (Glasshouse Site), Monivea Road - (Phase 2)	16	*N/A						Q4-2018	
586	SHIP CONSTRUCTION TURNKEY	Galway City	Radharc na Gréine (Glasshouse Site), Monivea Road - (Phase 3)	10	*N/A						Q4-2018	
587	SHIP CONSTRUCTION TURNKEY	Galway City	Radharc na Gréine (Glasshouse Site), Monivea Road - (Phase 4)	14	*N/A						Q4-2018	
588	SHIP CONSTRUCTION TURNKEY	Galway City	Radharc na Gréine (Glasshouse Site), Monivea Road - (Phase 5)	4	*N/A						Q4-2018	
589	CALF Construction	Galway County	Spiddal Cottages, Co Galway (Phase 1)	23	Cluid Housing							Q3-2017
590	CALF Turnkey	Galway County	Cnoc na Si, Portumna, Co Galway (Phase 1)	10	Co-operative Housing Ireland							Q2-2018
591	CALF Turnkey	Galway County	Dunloe Street, Ballinasloe, Co. Galway (Phase 1)	9	Co-operative Housing Ireland						Q3-2018	
592	CALF Turnkey	Galway County	Sliabh Carran, Gort, Co Galway (Phase 1)	9	Túath Housing Association Ltd				Q1-2019			
593	CALF Turnkey	Galway County	Tir an Choir, Vicars Choral, Tuam, Co. Galway (Phase 1)	12	Co-operative Housing Ireland		Stage 1 approved Q3-2019, outline design and costs being prepared.					
594	CAS CONSTRUCTION	Galway County	Letterfrack (Phase 2)	11	Cluid Housing Association			Stage 2 approved Q2-2018, full design/tender being prepared.				
595	CAS CONSTRUCTION	Galway County	Rossaveal Cottages, Ros a Mhíl, South Connemara	8	Tearmann Eanna Teoranta		Stage 1 approved Q4-2016, outline design and costs being prepared.					
596	CAS CONSTRUCTION	Galway County	Cregboy, Claregalway	14	Claregalway and District Day Care Centre							Q3-2019
597	CAS CONSTRUCTION	Galway County	Mountbellew	5	Mountbellew Voluntary Homes Association		Stage 1 approved Q3-2015, outline design and costs being prepared.					
598	CAS CONSTRUCTION	Galway County	Springfield, Parkmore (Ballinasloe)	4	Peter Triest Housing Association Ltd		Stage 1 approved Q2-2017, outline design and costs being prepared.					
599	CAS CONSTRUCTION	Galway County	Letterfrack (Phase 1)	13	Cluid Housing Association							Q2-2016

600	CAS CONSTRUCTION	Galway County	Dunlo Hill, Ballinasloe	18	Cuid Housing Association					Q4-2018	
601	CAS CONSTRUCTION	Galway County	Caheoy, Athenry	4	Peter Triest Housing Association Ltd	Stage 1 approved Q3-2017, outline design and costs being prepared.					
602	CAS CONSTRUCTION	Galway County	Aggard More, Craughwell	4	Peter Triest Housing Association Ltd					Q2-2019	
603	CAS CONSTRUCTION	Galway County	The Old Post Office, Inverin	4	Tearmann Eanna Teoranta					Q3-2019	
604	CAS CONSTRUCTION TURNKEY	Galway County	Tubber Road, Gort	10	Inis Housing Association Ltd				Stage 4 approved Q3-2019, the scheme is fully approved.		
605	SHIP CONSTRUCTION	Galway County	Esker Fields, Ballinasloe	2	*N/A					Q2-2018	
606	SHIP CONSTRUCTION	Galway County	Garbally Drive, Ballinasloe	10	*N/A						Q3-2019
607	SHIP CONSTRUCTION	Galway County	Na Clocha Rua, An Cheathrú Rua	4	*N/A					Q2-2019	
608	SHIP CONSTRUCTION	Galway County	Ardrahan (SRD)	1	*N/A						Q4-2017
609	SHIP CONSTRUCTION	Galway County	Callowfinish, Carna (SRD)	1	*N/A						Q2-2018
610	SHIP CONSTRUCTION	Galway County	Waterdale, Claregalway (SRD)	1	*N/A						Q4-2018
611	SHIP CONSTRUCTION	Galway County	Corndulla (SRD)	1	*N/A						Q1-2019
612	SHIP CONSTRUCTION	Galway County	Cill Chiarán (SRD)	1	*N/A						Q3-2018
613	SHIP CONSTRUCTION	Galway County	Kinvara (SRD)	1	*N/A						Q3-2018
614	SHIP CONSTRUCTION	Galway County	Cnoc na Carraige, Roundstone, Co. Galway	14	*N/A					Q3-2019	
615	SHIP CONSTRUCTION	Galway County	Hospital Road, Clifden	26	*N/A	Stage 1 approved Q1-2018, outline design and costs being prepared.					
616	SHIP CONSTRUCTION	Galway County	Bridge Court, Ahascragh, Ballinasloe	17	*N/A		Stage 2 approved Q2-2019, full design/tender being prepared.				
617	SHIP CONSTRUCTION	Galway County	Caisleán Raithlín, Ardrahan	12	*N/A		Stage 2 approved Q2-2019, full design/tender being prepared.				
618	SHIP CONSTRUCTION	Galway County	Barrack Street, Loughrea	5	*N/A					Q3-2019	
619	SHIP CONSTRUCTION	Galway County	Gilmartin Road, Tuam. Phase 2	24	*N/A						Q3-2019

620	SHIP CONSTRUCTION	Galway County	Cartron, Kinvarra	10	*N/A	Stage 1 approved Q2-2018, outline design and costs being prepared.					
621	SHIP CONSTRUCTION	Galway County	Gort Ui Lochlainn, Moycullen	30	*N/A	Stage 1 approved Q3-2018, outline design and costs being prepared.					
622	SHIP CONSTRUCTION	Galway County	Gilmartin Road, Tuam	16	*N/A						Q4-2018
623	SHIP CONSTRUCTION	Galway County	Tir an Bhui, TUam, Co. Galway	51	*N/A	Stage 1 approved Q2-2019, outline design and costs being prepared.					
624	SHIP CONSTRUCTION	Galway County	Gilmartin Road, Tuam, Phase 3	19	*N/A					Q4-2017	
625	SHIP CONSTRUCTION TURNKEY	Galway County	Lorro gate, Prospect, Athenry	14	*N/A						Q4-2017
626	SHIP CONSTRUCTION TURNKEY	Galway County	Arvough, Kinvara	6	*N/A						Q4-2017
627	SHIP CONSTRUCTION TURNKEY	Galway County	Castlecourt, Abbey Street, Portumna	10	*N/A						Q4-2017
628	SHIP CONSTRUCTION TURNKEY	Galway County	Asthorn Avenue, Headford	10	*N/A						Q4-2018
629	SHIP CONSTRUCTION TURNKEY	Galway County	Cuirt na hAbhann, Claregalway	8	*N/A						Q4-2018
630	SHIP CONSTRUCTION TURNKEY	Galway County	Tullahill, Loughrea	19	*N/A				Stage 4 approved Q2-2019, the scheme is fully approved.		
631	SHIP CONSTRUCTION TURNKEY	Galway County	Tullahill, Loughrea - Phase 2	42	*N/A				Stage 4 approved Q2-2019, the scheme is fully approved.		
632	SHIP CONSTRUCTION TURNKEY	Galway County	An Fuaran Estate, Oranmore	4	*N/A					Q2-2019	
633	SHIP CONSTRUCTION TURNKEY	Galway County	Kylebroughlan, Moycullen	44	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
634	CALF Turnkey	Kerry	Barraduff, Killarney, Co. Kerry (Phase 1)*	56	Co-operative Housing Ireland				Q3-2019		
635	CALF Turnkey	Kerry	Cathair Lakes Farrantoreen Road, Killorglin, Co Kerry (Phase 1)	5	Cluid Housing						Q2-2016
636	CALF Turnkey	Kerry	Deerpark Avenue, Tralee, Co. Kerry (Phase 1)	4	Co-operative Housing Ireland					Q1-2019	
637	CALF Turnkey	Kerry	Derreen, Killarney, Co Kerry (Phase 1)*	61	Cluid Housing					Q4-2018	
638	CALF Turnkey	Kerry	Doon Road, Lisloose, Tralee, Co. Kerry (Phase 1)*	14	Co-operative Housing Ireland					Q4-2018	
639	CALF Turnkey	Kerry	Dromcairn, Tralee, Co. Kerry (Phase 1)	12	Cluid Housing					Q1-2019	

640	CALF Turnkey	Kerry	Dun Ard, Doon Road, Ballybunnon, Co Kerry (Phase 1)	14	Respond							Q4-2018
641	CALF Turnkey	Kerry	Dun Ard, Doon Road, Ballybunnon, Co Kerry (Phase 2)	2	Respond						Q3-2018	
642	CALF Turnkey	Kerry	Dun Ard, Doon Road, Ballybunnon, Co Kerry (Phase 3)	6	Respond						Q3-2018	
643	CALF Turnkey	Kerry	Fortfield, Tralee, Co. Kerry (Phase 1)*	15	Cluid Housing						Q4-2018	
644	CALF Turnkey	Kerry	Killeen, Abbeydorney Road, Tralee, Co. Kerry (Phase 1)*	17	Cluid Housing						Q1-2019	
645	CALF Turnkey	Kerry	Oakwood, Coolegreen, Killarney, Co. Kerry (Phase 1)	59	Cluid Housing							Q3-2019
646	CALF Turnkey	Kerry	The Grove, Dingle, Co. Kerry (Phase 1)*	20	Cluid Housing						Q1-2019	
647	CAS CONSTRUCTION	Kerry	Armagh House, Killarney	6	Cluid Housing Association					Stage 4 approved Q3-2019, the scheme is fully approved.		
648	CAS CONSTRUCTION	Kerry	22 College Road, Castleisland	4	Kerry Emigrant Support Housing Association Ltd							Q4-2018
649	CAS CONSTRUCTION	Kerry	Chamfers Place	18	Cluid Housing Association		Stage 2 approved Q1-2018, full design/tender being prepared.					
650	CAS CONSTRUCTION	Kerry	The Parsonage, Caherciveen	5	Caherciveen Social Services (Housing) Ltd							Q4-2018
651	CAS CONSTRUCTION	Kerry	Hawley Park Apartments, St Martins Park, Mitchels Rd, Tralee	15	Kingdom Voluntary Housing Association		Stage 2 approved Q1-2019, full design/tender being prepared.					
652	CAS CONSTRUCTION	Kerry	The Presentation Convent, Rathmore	4	Social Action Group Rathmore						Q4-2018	
653	REGENERATION	Kerry	Croilar Na Mistaelach, Tralee	11	*N/A							Q4-2018
654	REGENERATION	Kerry	Urban Terrace, Tralee	2	*N/A							Q4-2016
655	REGENERATION	Kerry	Clonmore Road, Tralee	3	*N/A							Q4-2016
656	REGENERATION	Kerry	St Martin's Park, Tralee	4	*N/A							Q4-2018
657	REGENERATION	Kerry	Dingle Road, Tralee	1	*N/A							Q2-2018
658	SHIP CONSTRUCTION	Kerry	Pinewood Estate, Killarney	6	*N/A						Q1-2019	
659	SHIP CONSTRUCTION	Kerry	Glannagilligh, Caragh Lake, Killorglin (SRD)	1	*N/A					Stage 4 approved Q3-2019, the scheme is fully approved.		

660	SHIP CONSTRUCTION	Kerry	Knockawinna, Brosna, Co Kerry	1	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
661	SHIP CONSTRUCTION	Kerry	Carrigannon, Lyreacrumpane (SRD)	1	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
662	SHIP CONSTRUCTION	Kerry	Cleandries, Causeway	1	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
663	SHIP CONSTRUCTION	Kerry	Cois Gallain, Killorglin	14	*N/A					Q1-2019	
664	SHIP CONSTRUCTION	Kerry	Rathmore/Barraduff	20	*N/A			Stage 3 approved Q2-2019, the scheme is now approved to proceed to tender.			
665	SHIP CONSTRUCTION	Kerry	Ardbhearna, Kenmare	22	*N/A						Q4-2018
666	SHIP CONSTRUCTION	Kerry	Bill Kinnerk Road, Tralee	4	*N/A						Q1-2018
667	SHIP CONSTRUCTION	Kerry	Cuirt Eaglaise, Milltown	8	*N/A					Q4-2018	
668	SHIP CONSTRUCTION	Kerry	Killeen, Tralee	21	*N/A						Q3-2019
669	SHIP CONSTRUCTION	Kerry	Lixnaw	4	*N/A						Q4-2017
670	SHIP CONSTRUCTION	Kerry	The Park, Killarney	20	*N/A						Q1-2018
671	SHIP CONSTRUCTION	Kerry	Courthouse Lawn, Listowel	7	*N/A					Q4-2018	
672	SHIP CONSTRUCTION	Kerry	Dreenagh, Ballyheigue (SRD)	1	*N/A						Q1-2017
673	SHIP CONSTRUCTION	Kerry	Glenach, Ballybunion	20	*N/A			Stage 3 approved Q4-2018, the scheme is now approved to proceed to tender.			
674	SHIP CONSTRUCTION	Kerry	Callinafercy, Milltown	1	*N/A						Q4-2018
675	SHIP CONSTRUCTION	Kerry	Cahernaboshina, Ventry	1	*N/A						Q4-2018
676	SHIP CONSTRUCTION	Kerry	An Carrigin, Tralee	28	*N/A					Q2-2019	
677	SHIP CONSTRUCTION	Kerry	Pinewood Estate, Killarney	1	*N/A						Q4-2018
678	SHIP CONSTRUCTION	Kerry	Drom West, Glenbeigh	1	*N/A			Stage 3 approved Q3-2017, the scheme is now approved to proceed to tender.			
679	SHIP CONSTRUCTION	Kerry	Meanus, Killorglin	1	*N/A						Q3-2019

680	SHIP CONSTRUCTION	Kerry	Tullig Beg, Killorglin	1	*N/A							Q3-2019
681	SHIP CONSTRUCTION	Kerry	Owngarry, Killorglin	1	*N/A						Q1-2019	
682	SHIP CONSTRUCTION	Kerry	Lohercannon, Tralee	61	*N/A				Stage 3 approved Q3-2019, the scheme is now approved to proceed to tender.			
683	SHIP CONSTRUCTION	Kerry	Ballinakilly Lower, Glenbeigh	1	*N/A				Stage 3 approved Q3-2017, the scheme is now approved to proceed to tender.			
684	SHIP CONSTRUCTION	Kerry	Ashgrove, Listowel	1	*N/A							Q3-2017
685	SHIP CONSTRUCTION	Kerry	Cullenagh Upper, Beaufort	1	*N/A				Stage 3 approved Q4-2017, the scheme is now approved to proceed to tender.			
686	SHIP CONSTRUCTION	Kerry	Farranwilliam, Ardferit	22	*N/A						Q3-2019	
687	SHIP CONSTRUCTION	Kerry	Ballyrickard, Tralee	20	*N/A			Stage 2 approved Q2-2019, full design/tender being prepared.				
688	SHIP CONSTRUCTION	Kerry	Crogorts, Tralee	30	*N/A			Stage 2 approved Q3-2019, full design/tender being prepared.				
689	SHIP CONSTRUCTION	Kerry	Rock Rd., Killarney	10	*N/A			Stage 2 approved Q2-2019, full design/tender being prepared.				
690	SHIP CONSTRUCTION	Kerry	Gortamullin, Kenmare (Phase4)	14	*N/A				Stage 3 approved Q3-2019, the scheme is now approved to proceed to tender.			
691	SHIP CONSTRUCTION	Kerry	Baile an Gharrai, Lixnaw (PHASE 2)	10	*N/A				Stage 3 approved Q3-2019, the scheme is now approved to proceed to tender.			
692	SHIP CONSTRUCTION	Kerry	Rathass, Tralee	4	*N/A			Stage 1 approved Q3-2019, outline design and costs being prepared.				
693	SHIP CONSTRUCTION	Kerry	Woodview Place, Tarbert	22	*N/A			Stage 2 approved Q3-2019, full design/tender being prepared.				
694	SHIP CONSTRUCTION	Kerry	Marconi South, Ballybunion	12	*N/A			Stage 1 approved Q3-2019, outline design and costs being prepared.				
695	SHIP CONSTRUCTION	Kerry	Shanakill, Tralee	8	*N/A			Stage 1 approved Q3-2019, outline design and costs being prepared.				
696	SHIP CONSTRUCTION	Kerry	Rusheen, Ballylongford	6	*N/A			Stage 1 approved Q3-2019, outline design and costs being prepared.				
697	SHIP CONSTRUCTION TURNKEY	Kerry	Ard Na Si, Lispole	2	*N/A							Q1-2018
698	SHIP CONSTRUCTION TURNKEY	Kerry	1-4 Steeple Meadow View, Milltown	4	*N/A							Q4-2017
699	SHIP CONSTRUCTION TURNKEY	Kerry	Meadow Park, Milltown	9	*N/A							Q2-2018

720	CALF Turnkey	Kildare	Fenton Green, Kilcock, Co Kildare (Phase 7)*	9	Túath Housing Association Ltd					Q2-2018	
721	CALF Turnkey	Kildare	Fenton Green, Kilcock, Co Kildare (Phase 8)	9	Túath Housing Association Ltd					Q2-2018	
722	CALF Turnkey	Kildare	Kilbelin Abbey, Newbridge, Co. Kildare (Phase 1)*	4	Cluid Housing					Q2-2019	
723	CALF Turnkey	Kildare	Kilbelin Abbey, Newbridge, Co. Kildare (Phase 2)*	4	Cluid Housing					Q2-2019	
724	CALF Turnkey	Kildare	Millfield Manor, Newbridge, Co. Kildare (Phase 1)*	19	Cluid Housing						Q3-2018
725	CALF Turnkey	Kildare	Morristown, Newbridge, Co Kildare (Phase 1)	14	Cluid Housing						Q1-2018
726	CALF Turnkey	Kildare	Morristown, Newbridge, Co. Kildare (Phase 1)*	4	Cluid Housing						Q2-2018
727	CALF Turnkey	Kildare	Oaktree, Tully Road, Kildare Town (Phase 1)*	10	Túath Housing Association Ltd						Q2-2018
728	CALF Turnkey	Kildare	Oaktree, Tully Road, Kildare Town (Phase 2)*	7	Túath Housing Association Ltd						Q3-2018
729	CALF Turnkey	Kildare	Revised Rye Abbey, Kilcock, Co Kildare (apts) (Phase 1)	33	Cluid Housing						Q2-2017
730	CALF Turnkey	Kildare	Roseberry Hill, Newbridge (Phase 1)	13	Túath Housing Association Ltd						Q2-2017
731	CALF Turnkey	Kildare	Roseberry Hill, Newbridge (Phase 2)	16	Túath Housing Association Ltd						Q4-2017
732	CALF Turnkey	Kildare	Roseberry Hill, Newbridge (Phase 3)	16	Túath Housing Association Ltd						Q1-2018
733	CALF Turnkey	Kildare	Rye Abbey, Kilcock - revised (houses) (Phase 1)	4	Cluid Housing						Q2-2017
734	CALF Turnkey	Kildare	The Vestry, Glebelands, Athy, Co. Kildare (Phase 1)	18	Respond					Q4-2018	
735	CALF Turnkey	Kildare	The Vestry, Glebelands, Athy, Co. Kildare (Phase 1)*	18	Respond					Q3-2019	
736	CALF Turnkey	Kildare	The Vestry, Glebelands, Athy, Co. Kildare (Phase 2)	32	Respond					Q4-2018	
737	CALF Turnkey	Kildare	White Oaks, Rickardstown, Newbridge, Co. Kildare (Phase 1)*	14	Cluid Housing						Q4-2018
738	CALF Turnkey	Kildare	White Oaks, Rickardstown, Newbridge, Co. Kildare (Phase 2)	24	Cluid Housing						Q4-2018
739	CALF Turnkey	Kildare	White Oaks, Rickardstown, Newbridge, Co. Kildare (Phase 3)	20	Cluid Housing						Q1-2019

740	CALF Turnkey	Kildare	White Oaks, Rickardstown, Newbridge, Co. Kildare (Phase 4)	2	Cluid Housing						Q1-2018	
741	CAS CONSTRUCTION	Kildare	Craddockstown, Naas	3	KARE Promoting Inclusion for People with Intellectual Disabilities				Stage 3 approved Q3-2019, the scheme is now approved to proceed to tender.			
742	CAS CONSTRUCTION	Kildare	Main St., Kilcullen	4	Camphill Communities of Ireland			Stage 2 approved Q4-2017, full design/tender being prepared.				
743	CAS CONSTRUCTION	Kildare	El Kantara, Newbridge	2	KARE Promoting Inclusion for People with Intellectual Disabilities	Stage 1 approved Q1-2016, outline design and costs being prepared.						
744	CAS CONSTRUCTION	Kildare	Jigginstown House, Naas	12	Homeless Care Ltd				Stage 4 approved Q2-2019, the scheme is fully approved.			
745	PUBLIC PRIVATE PARTNERSHIP (Bundle 1)	Kildare	Craddockstown, Naas	74	*N/A						Q1-2019	
746	PUBLIC PRIVATE PARTNERSHIP (Bundle 2)	Kildare	Butterstream, Clane	77	*N/A					Q2-2019		
747	SHIP CONSTRUCTION	Kildare	Hillview Terrace, Narraghmore	4	*N/A			Stage 2 approved Q3-2019, full design/tender being prepared.				
748	SHIP CONSTRUCTION	Kildare	Athgarvan Village	18	*N/A						Q1-2019	
749	SHIP CONSTRUCTION	Kildare	Rathasker Road, Naas	48	*N/A				Stage 3 approved Q3-2019, the scheme is now approved to proceed to tender.			
750	SHIP CONSTRUCTION	Kildare	Dunmurry Rise, Bishopsland	32	*N/A							Q3-2019
751	SHIP CONSTRUCTION	Kildare	Anne Street, Prosperous	12	*N/A						Q1-2019	
752	SHIP CONSTRUCTION	Kildare	Beechgrove, Rathangan	18	*N/A						Q4-2018	
753	SHIP CONSTRUCTION	Kildare	Kilcock (Phase 2.1)	6	*N/A							Q4-2017
754	SHIP CONSTRUCTION	Kildare	Athgarvan Road, Newbridge	13	*N/A							Q3-2018
755	SHIP CONSTRUCTION	Kildare	Newtown, Leixlip	4	*N/A	Stage 1 approved Q3-2017, outline design and costs being prepared.						
756	SHIP CONSTRUCTION	Kildare	Coill Dubh	10	*N/A			Stage 2 approved Q2-2018, full design/tender being prepared.				
757	SHIP CONSTRUCTION	Kildare	Kilcock (Phase 2.2)	13	*N/A							Q1-2018
758	SHIP CONSTRUCTION	Kildare	Skenagun, Castledermot	2	*N/A	Stage 1 approved Q3-2018, outline design and costs being prepared.						
759	SHIP CONSTRUCTION RAPID	Kildare	Old Greenfield Road, Maynooth	47	*N/A			Stage 2 approved Q3-2019, full design/tender being prepared.				

760	SHIP CONSTRUCTION TURNKEY	Kildare	Bodkin Place, Kilmeague	16	*N/A							Q4-2017
761	SHIP CONSTRUCTION TURNKEY	Kildare	Drogheda Street, Monasterevin	6	*N/A							Q4-2017
762	SHIP CONSTRUCTION TURNKEY	Kildare	Oaktree, Tully Road, Kildare Town	8	*N/A							Q3-2018
763	SHIP CONSTRUCTION TURNKEY	Kildare	Moore Abbey Court, Monasterevin	2	*N/A							Q1-2018
764	SHIP CONSTRUCTION TURNKEY	Kildare	Drogheda Street, Monasterevin	7	*N/A							Q1-2018
765	SHIP CONSTRUCTION TURNKEY	Kildare	Moss Brook, Prosperous	2	*N/A							Q1-2018
766	SHIP CONSTRUCTION TURNKEY	Kildare	Hawthorn Manor, Brockagh, Coill Dubh	2	*N/A							Q4-2018
767	SHIP CONSTRUCTION TURNKEY	Kildare	Whitethorn Park, Allenwood	2	*N/A							Q3-2018
768	SHIP CONSTRUCTION TURNKEY	Kildare	The Pike, Castledermot	6	*N/A							Q4-2018
769	SHIP CONSTRUCTION TURNKEY	Kildare	Grove Lane, Robertstown	3	*N/A						Q1-2017	
770	SHIP CONSTRUCTION TURNKEY	Kildare	Brookes Mill, Prosperous	5	*N/A							Q4-2018
771	SHIP CONSTRUCTION TURNKEY	Kildare	The Green, Elsmore Naas	5	*N/A							Q4-2018
772	SHIP CONSTRUCTION TURNKEY	Kildare	Oakwood Park, Derrinturn	10	*N/A							Q1-2019
773	SHIP CONSTRUCTION TURNKEY	Kildare	Oakwood Park, Derrinturn	19	*N/A						Q4-2018	
774	SHIP CONSTRUCTION TURNKEY	Kildare	Beech Park Wood, Leixlip	4	*N/A							Q3-2019
775	SHIP CONSTRUCTION TURNKEY	Kildare	Oaktree, Tully Road, Kildare Town	18	*N/A							Q2-2019
776	SHIP CONSTRUCTION TURNKEY	Kildare	Oakwood Park, Derrinturn	10	*N/A							Q3-2019
777	SHIP CONSTRUCTION TURNKEY	Kildare	Oaktree, Tully Road, Kildare Town (Phase 2)	20	*N/A							Q3-2019
778	SHIP CONSTRUCTION TURNKEY	Kildare	Cluin Dara, Derrinturn, Kildare	1	*N/A							Q2-2019
779	SHIP CONSTRUCTION TURNKEY	Kildare	School Walk, Allenwood	4	*N/A					Stage 4 approved Q3-2019, the scheme is fully approved.		

780	SHIP CONSTRUCTION TURNKEY	Kildare	Stoneleigh, Naas	6	*N/A						Q1-2019	
781	CALF Construction	Kilkenny	Park Lane, Friary Walk, Callan, Co Kilkenny (Phase 1)*	16	Cluid Housing							Q2-2019
782	CALF Construction	Kilkenny	Walkin St Kilkenny (Phase 1)	27	Oaklee Housing						Q3-2018	
783	CALF Turnkey	Kilkenny	Castlehyde, Rosbercon (Phase 1)	4	Co-operative Housing Ireland							Q4-2018
784	CALF Turnkey	Kilkenny	Castlehyde, Rosbercon (Phase 2)	6	Co-operative Housing Ireland							Q4-2018
785	CALF Turnkey	Kilkenny	Golf Links Road, Kilkenny (Phase 1)*	39	Respond						Q2-2018	
786	CALF Turnkey	Kilkenny	Logan Square, Thomastown, Co Kilkenny (Phase 1)*	16	Oaklee Housing							Q2-2017
787	CALF Turnkey	Kilkenny	Love Lane, Castlecomer, Co. Kilkenny (Phase 1)	4	Co-operative Housing Ireland							Q3-2019
788	CALF Turnkey	Kilkenny	Margaret's Field, Callan Road, Kilkenny City (Phase 1)	40	Respond						Q1-2019	
789	CALF Turnkey	Kilkenny	Nuncio Road, Kilkenny (Phase 1)	50	Respond						Q4-2018	
790	CALF Turnkey	Kilkenny	O'Loughlin Court, Kilkenny (Phase 1)	2	Respond							Q4-2018
791	CALF Turnkey	Kilkenny	Side Road, Moneenroe, Castlecomer, Co. Kilkenny (Phase 1)	9	Oaklee Housing							Q3-2018
792	CAS CONSTRUCTION	Kilkenny	Kingsriver, Ennisnag	2	Kingsriver Housing Association Limited		Stage 2 approved Q1-2019, full design/tender being prepared.					
793	CAS CONSTRUCTION	Kilkenny	Garrin Green	6	SOS Kilkenny Housing Association Ltd							Q4-2018
794	CAS CONSTRUCTION	Kilkenny	Hazelbrook, Newrath	2	Waterford Dove Housing Association							Q1-2018
795	CAS CONSTRUCTION	Kilkenny	Good Shepherd Centre - Wing 1952	12	The Good Shepherd Centre (Kilkenny) Ltd							Q4-2018
796	CAS CONSTRUCTION	Kilkenny	"Brooke House", Thomastown	5	Camphill Communities of Ireland							Q3-2017
797	CAS CONSTRUCTION	Kilkenny	Friary Walk, Callan	12	Cluid Housing Association							Q3-2016
798	CAS CONSTRUCTION	Kilkenny	Garden Cottage, The Workhouse, Callan	1	Camphill Communities of Ireland							Q4-2017
799	CAS CONSTRUCTION	Kilkenny	"Red Barn" Patrick Street, Ballyragget	12	Good Shepherd Services Ltd		Stage 2 approved Q4-2018, full design/tender being prepared.					

840	CALF Turnkey	Laois	Bellingham, Portlaoise, Co. Laois (Phase 2)	6	Cluid Housing					Q1-2017	
841	CALF Turnkey	Laois	Bellingham, Portlaoise, Co. Laois (Phase 3)	5	Cluid Housing					Q1-2017	
842	CALF Turnkey	Laois	Bellingham, Portlaoise, Co. Laois (Phase 4)*	9	Cluid Housing					Q1-2017	
843	CALF Turnkey	Laois	Bellingham, Portlaoise, Co. Laois (Phase 5)*	6	Cluid Housing					Q1-2017	
844	CALF Turnkey	Laois	Borris Road, Portlaoise, Co. Laois (Phase 1)*	17	Túath Housing Association Ltd					Q3-2019	
845	CALF Turnkey	Laois	Borris Road, Portlaoise, Co. Laois (Phase 2)	19	Túath Housing Association Ltd					Q3-2019	
846	CALF Turnkey	Laois	Corrig Glen, Station Road, Portarlinton, Co. Laois (Phase 1)	17	Túath Housing Association Ltd						Q3-2018
847	CALF Turnkey	Laois	Corrig Glen, Station Road, Portarlinton, Co. Laois (Phase 2)	9	Túath Housing Association Ltd						Q4-2018
848	CALF Turnkey	Laois	Corrig Glen, Station Road, Portarlinton, Co. Laois (Phase 3)	13	Túath Housing Association Ltd						Q4-2018
849	CALF Turnkey	Laois	Droimnin, Stradbally, Co Laois (Phase 1)	6	Cluid Housing						Q3-2018
850	CALF Turnkey	Laois	Lake Drive, Kilminchy, Co. Laois (Phase 1)	10	Oaklee Housing					Q3-2019	
851	CALF Turnkey	Laois	Main Street, Stradbally, Co. Laois (Phase 1)	16	North & East Housing Association Ltd					Q1-2019	
852	CALF Turnkey	Laois	Wilton Lawns, Portarlinton, Co. Laois (Phase 1)	2	Respond				Q2-2019		
853	CAS CONSTRUCTION	Laois	Presentation Convent & Lands, Portlaoise,	47	Sophia Housing Association Ltd	Stage 1 approved Q3-2018, outline design and costs being prepared.					
854	SHIP CONSTRUCTION	Laois	Harpurs Lane, Portlaoise	1	*N/A					Q1-2019	
855	SHIP CONSTRUCTION	Laois	Hillview, Portlaoise	2	*N/A				Stage 4 approved Q3-2018, the scheme is fully approved.		
856	SHIP CONSTRUCTION	Laois	The Orchard, Stradbally	6	*N/A				Stage 4 approved Q4-2018, the scheme is fully approved.		
857	SHIP CONSTRUCTION	Laois	Moore Street, Rathdowney	6	*N/A			Stage 3 approved Q3-2019, the scheme is now approved to proceed to tender.			
858	SHIP CONSTRUCTION	Laois	Ballymorris Road, Portarlinton	22	*N/A					Q3-2019	
859	SHIP CONSTRUCTION	Laois	Gleann na Glaise, Ballyroan	10	*N/A		Stage 2 approved Q3-2018, full design/tender being prepared.				

860	SHIP CONSTRUCTION	Laois	Pattison Est. Mountmellick	10	*N/A		Stage 2 approved Q3-2018, full design/tender being prepared.				
861	SHIP CONSTRUCTION	Laois	Shannon Street, Mountrath	6	*N/A			Stage 3 approved Q3-2018, the scheme is now approved to proceed to tender.			
862	SHIP CONSTRUCTION	Laois	Conniberry Way, Old Knockmay Road, Portlaoise	33	*N/A						Q2-2018
863	SHIP CONSTRUCTION	Laois	Harbour Court, Mountmellick	6	*N/A	Stage 1 approved Q3-2018, outline design and costs being prepared.					
864	SHIP CONSTRUCTION	Laois	Mooreville, Rathdowney	8	*N/A	Stage 1 approved Q3-2018, outline design and costs being prepared.					
865	SHIP CONSTRUCTION	Laois	Coolroe, Ballybrittas	1	*N/A	Stage 1 approved Q4-2018, outline design and costs being prepared.					
866	SHIP CONSTRUCTION	Laois	Sean Doire, Cork Road, Durrrow	22	*N/A		Stage 2 approved Q3-2019, full design/tender being prepared.				
867	SHIP CONSTRUCTION	Laois	St Kieran's Park, Errill	14	*N/A	Stage 1 approved Q1-2019, outline design and costs being prepared.					
868	SHIP CONSTRUCTION	Laois	Clonrooske, Knockmay	11	*N/A	Stage 1 approved Q3-2019, outline design and costs being prepared.					
869	SHIP CONSTRUCTION	Laois	Carraig Glas, Stradbally	26	*N/A	Stage 1 approved Q3-2019, outline design and costs being prepared.					
870	CAS CONSTRUCTION	Leitrim	Ballinamore	2	Society of Saint Vincent de Paul						Q4-2017
871	SHIP CONSTRUCTION	Leitrim	Autumn View, Summerhill, Carrick on Shannon	27	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
872	SHIP CONSTRUCTION	Leitrim	Taobh Tire, Manorhamilton (Phase 2)	7	*N/A						Q4-2018
873	SHIP CONSTRUCTION TURNKEY	Leitrim	Roosky	7	*N/A					Q1-2019	
874	SHIP CONSTRUCTION TURNKEY	Leitrim	Drumshanbo	9	*N/A						Q3-2019
875	CALF Construction	Limerick	Hyde Road, Limerick City (Phase 1)	20	Cluid Housing						Q1-2018
876	CALF Turnkey	Limerick	Ballygrennan Close, Moyross, Limerick (Phase 1)	2	Respond						Q4-2018
877	CALF Turnkey	Limerick	Ballygrennan Close, Moyross, Limerick (Phase 2)	2	Respond						Q4-2018
878	CALF Turnkey	Limerick	Ballygrennan Close, Moyross, Limerick (Phase 3)	2	Respond						Q4-2018
879	CALF Turnkey	Limerick	Cluain Ard, Fedamore, Co Limerick (Phase 1)	2	Co-operative Housing Ireland						Q1-2018

880	CALF Turnkey	Limerick	Cluain Ard, Fedamore, Co Limerick (Phase 2)	2	Co-operative Housing Ireland							Q3-2018
881	CALF Turnkey	Limerick	Drominbeg, Rhebogue, Limerick (Phase 1)	10	Co-operative Housing Ireland				Q2-2019			
882	CALF Turnkey	Limerick	Drominbeg, Rhebogue, Limerick (Phase 2)	10	Co-operative Housing Ireland				Q2-2019			
883	CALF Turnkey	Limerick	Revised - Ard Aulin, Mungret, Co Limerick (Phase 1)	7	Cluid Housing							Q2-2017
884	CAS CONSTRUCTION	Limerick	Towerfield Crescent, Croom	13	Croom Voluntary Housing Association Ltd		Stage 2 approved Q2-2019, full design/tender being prepared.					
885	CAS CONSTRUCTION	Limerick	Cappamore	10	Cappamore Housing Association Ltd		Stage 2 approved Q1-2019, full design/tender being prepared.					
886	CAS CONSTRUCTION	Limerick	Speakers Corner, Limerick City	4	Simon Community : Midwest Simon							Q3-2018
887	CAS CONSTRUCTION	Limerick	Cuan Mhuire, Bruree	6	Cuan Mhuire Teoranta							Q3-2018
888	CAS CONSTRUCTION	Limerick	Mirth, Thomondgate	18	Associated Charities Trust Ltd		Stage 1 approved Q3-2017, outline design and costs being prepared.					
889	CAS CONSTRUCTION	Limerick	Cois na Feile, Abbeyfeale	12	Cluid Housing Association							Q4-2016
890	CAS CONSTRUCTION	Limerick	2/3 Mallow Street	6	Peter McVerry Trust Ltd		Stage 1 approved Q1-2018, outline design and costs being prepared.					
891	CAS CONSTRUCTION	Limerick	St. Pauls Convent, Kilfinane	9	Sophia Housing Association Ltd		Stage 1 approved Q4-2018, outline design and costs being prepared.					
892	CAS CONSTRUCTION	Limerick	McGarry House, 7 Alphonsus Street	8	Arlington Novas Ireland Ltd		Stage 1 approved Q3-2019, outline design and costs being prepared.					
893	CAS CONSTRUCTION	Limerick	47 & 48 Main Street, Croom, Limerick	4	Croom Voluntary Housing Association Ltd		Stage 1 approved Q3-2019, outline design and costs being prepared.					
894	CAS CONSTRUCTION TURNKEY	Limerick	Carebright Community, Ardykeohane, Bruff	6	Carebright Ltd							Q1-2019
895	CAS CONSTRUCTION TURNKEY	Limerick	Barrack Mews, Brennan's Row, Cathedral Place	3	Arlington Novas Ireland Ltd						Q3-2019	
896	CAS CONSTRUCTION TURNKEY	Limerick	Barrack Mews, Brennan's Row, Cathedral place	3	Arlington Novas Ireland Ltd						Q3-2019	
897	REGENERATION	Limerick	Lord Edward Street, P2: Main Contract	79	*N/A							Q4-2017
898	REGENERATION	Limerick	Lord Edward Street, P2: Main Contract	2	*N/A							Q1-2017
899	REGENERATION	Limerick	Gaol Lane	1	*N/A		Stage 2 approved Q3-2016, full design/tender being prepared.					

900	REGENERATION	Limerick	Sheep / Athlunkards Street	8	Túath Housing Association Ltd		Stage 2 approved Q2-2014, full design/tender being prepared.				
901	REGENERATION	Limerick	Churchfield	19	*N/A						Q1-2018
902	REGENERATION	Limerick	Churchfield (Phase 2)	38	Cuid Housing Association		Stage 2 approved Q4-2014, full design/tender being prepared.				
903	REGENERATION	Limerick	Cosgrave Park	9	Co-operative Housing Ireland (Formerly NABCo)			Stage 3 approved Q1-2018, the scheme is now approved to proceed to tender.			
904	REGENERATION	Limerick	Palm Close	27	Cuid Housing Association		Stage 2 approved Q3-2016, full design/tender being prepared.				
905	REGENERATION	Limerick	Orchard Site	26	Oaklee Housing Trust		Stage 2 approved Q3-2017, full design/tender being prepared.				
906	REGENERATION	Limerick	176 & 177 Cliona Park	2	*N/A						Q2-2016
907	REGENERATION	Limerick	Cliona Park (Phase 2)	10	*N/A						Q2-2017
908	REGENERATION	Limerick	8-10 Gaol Lane	3	*N/A						Q4-2016
909	REGENERATION	Limerick	13 Weston Gardens	3	*N/A						Q2-2016
910	REGENERATION	Limerick	2016 Moyross Rebuild	6	*N/A						Q4-2016
911	REGENERATION	Limerick	2016 Southhill Rebuild	8	*N/A						Q4-2016
912	REGENERATION	Limerick	2016 St. Mary's Park Rebuild	9	*N/A						Q4-2016
913	REGENERATION	Limerick	BCW Vacant Refurbs, Lot 1 & 2**	14	*N/A						Q4-2016
914	REGENERATION	Limerick	St. Mary's Park Infills	15	*N/A						Q4-2018
915	REGENERATION	Limerick	Cliona Park (Phase 3)	18	Túath Housing Association Ltd		Stage 2 approved Q3-2016, full design/tender being prepared.				
916	REGENERATION	Limerick	45A-46A Cliona Park	2	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
917	REGENERATION	Limerick	Dalgaish Park	27	*N/A		Stage 2 approved Q3-2019, full design/tender being prepared.				
918	REGENERATION	Limerick	2017 St Mary's Park Rebuild	1	*N/A						Q4-2017
919	REGENERATION	Limerick	2017 Ballinacurra Weston Rebuild	1	*N/A						Q4-2017

920	REGENERATION	Limerick	2017 Southill Rebuilds	13	*N/A							Q4-2017
921	REGENERATION	Limerick	2017 Moyross Rebuild	1	*N/A							Q4-2017
922	REGENERATION	Limerick	Churchfield (Phase 1.1)	23	*N/A							Q2-2018
923	REGENERATION	Limerick	St. Mary's Park Infills (Phase 2)	4	*N/A							Q1-2019
924	SHIP CONSTRUCTION	Limerick	Patrick's Villas, Castleconnell	4	*N/A						Q3-2019	
925	SHIP CONSTRUCTION	Limerick	Ballysimon, Greenhill Road	14	*N/A				Stage 3 approved Q3-2019, the scheme is now approved to proceed to tender.			
926	SHIP CONSTRUCTION	Limerick	Gough Place, Rosbrien Road, Limerick	17	*N/A				Stage 3 approved Q3-2019, the scheme is now approved to proceed to tender.			
927	SHIP CONSTRUCTION	Limerick	1-12 Burke Avenue, Limerick City	12	*N/A						Q1-2019	
928	SHIP CONSTRUCTION	Limerick	Fannings Corner, Limerick City	3	*N/A						Q2-2019	
929	SHIP CONSTRUCTION	Limerick	Joseph Street, Limerick City	2	*N/A			Stage 2 approved Q2-2018, full design/tender being prepared.				
930	SHIP CONSTRUCTION	Limerick	Waller's Well, Limerick City (Phase 2)	13	*N/A						Q2-2019	
931	SHIP CONSTRUCTION	Limerick	Clonmacken, Limerick City	43	*N/A						Q3-2019	
932	SHIP CONSTRUCTION	Limerick	Deerpark, Adare	30	*N/A			Stage 1 approved Q2-2015, outline design and costs being prepared.				
933	SHIP CONSTRUCTION	Limerick	Glenview Drive, Hospital	20	*N/A				Stage 3 approved Q3-2018, the scheme is now approved to proceed to tender.			
934	SHIP CONSTRUCTION	Limerick	Clare Street, Limerick City	7	*N/A			Stage 2 approved Q3-2017, full design/tender being prepared.				
935	SHIP CONSTRUCTION	Limerick	Hasset Villas, Thomondgate	3	*N/A							Q4-2018
936	SHIP CONSTRUCTION	Limerick	Kilmurry Court, Garryowen	7	*N/A						Q3-2018	
937	SHIP CONSTRUCTION	Limerick	Rathbane Road, Limerick City	2	*N/A							Q1-2019
938	SHIP CONSTRUCTION	Limerick	Sycamore Avenue, Limerick City	5	*N/A							Q3-2019
939	SHIP CONSTRUCTION	Limerick	Lower Carey's Road, Limerick City	11	*N/A				Stage 3 approved Q3-2019, the scheme is now approved to proceed to tender.			

940	SHIP CONSTRUCTION	Limerick	Kileely Road, Moyross	5	*N/A		Stage 2 approved Q2-2018, full design/tender being prepared.				
941	SHIP CONSTRUCTION	Limerick	Clare Street, Limerick City	2	*N/A						Q4-2017
942	SHIP CONSTRUCTION	Limerick	Knocklong	12	*N/A	Stage 1 approved Q4-2017, outline design and costs being prepared.					
943	SHIP CONSTRUCTION	Limerick	Convent Street, King's Island	2	*N/A	Stage 1 approved Q1-2018, outline design and costs being prepared.					
944	SHIP CONSTRUCTION	Limerick	Colbert Terrace, Abbeyfeale	3	*N/A		Stage 2 approved Q4-2018, full design/tender being prepared.				
945	SHIP CONSTRUCTION	Limerick	Towerfield Crescent, Croom	3	*N/A		Stage 2 approved Q2-2019, full design/tender being prepared.				
946	SHIP CONSTRUCTION	Limerick	Ballygrennan Road, Limerick City	2	*N/A						Q4-2017
947	SHIP CONSTRUCTION RAPID	Limerick	Faha View, Patrickswell	16	*N/A					Q4-2018	
948	SHIP CONSTRUCTION RAPID	Limerick	Old Christians Site, Rathbane	43	*N/A			Stage 3 approved Q3-2018, the scheme is now approved to proceed to tender.			
949	SHIP CONSTRUCTION RAPID	Limerick	Barnakyle, Patrickswell (Site 2)	24	*N/A			Stage 3 approved Q3-2018, the scheme is now approved to proceed to tender.			
950	SHIP CONSTRUCTION TURNKEY	Limerick	Woodlawn Park, Ballysimon Road, Limerick	9	*N/A					Q1-2019	
951	SHIP CONSTRUCTION TURNKEY	Limerick	Woodlawn Park (Phase 2), Ballysimon Road,	1	*N/A					Q1-2019	
952	CALF Construction	Longford	Colmcille Terrace, Granard, Co. Longford. (Phase 1)	21	Túath Housing Association Ltd				Q2-2018		
953	CALF Turnkey	Longford	Cartrun Breac, Lisbrack Rd, Longford (Phase 1)	7	Cluid Housing						Q1-2017
954	SHIP CONSTRUCTION	Longford	Rathcline Road, Lanesborough	4	*N/A						Q3-2019
955	SHIP CONSTRUCTION	Longford	Edgeworthstown Road, Ballymahon	4	*N/A						Q1-2018
956	SHIP CONSTRUCTION	Longford	Daroge, Ballymahon	1	*N/A					Q3-2019	
957	SHIP CONSTRUCTION	Longford	'Rose Cottage', Ballinallee	6	*N/A			Stage 3 approved Q1-2019, the scheme is now approved to proceed to tender.			
958	SHIP CONSTRUCTION	Longford	St.Rita's, Park Road, Longford	8	*N/A	Stage 1 approved Q1-2019, outline design and costs being prepared.					
959	SHIP CONSTRUCTION	Longford	Fairgreen View, Longford Town	1	*N/A		Stage 2 approved Q2-2019, full design/tender being prepared.				

960	SHIP CONSTRUCTION	Longford	Cranleymore, Abbeylara	3	*N/A		Stage 2 approved Q2-2019, full design/tender being prepared.				
961	SHIP CONSTRUCTION	Longford	Cloonahard	1	*N/A		Stage 2 approved Q3-2019, full design/tender being prepared.				
962	SHIP CONSTRUCTION TURNKEY	Longford	Mill Race Park, Drumlish	14	*N/A						Q4-2017
963	SHIP CONSTRUCTION TURNKEY	Longford	Knock, Lanesborough	4	*N/A						Q3-2018
964	SHIP CONSTRUCTION TURNKEY	Longford	Mill Race Park, Drumlish (Phase 2)	2	*N/A						Q1-2018
965	SHIP CONSTRUCTION TURNKEY	Longford	Ballinamuck	7	*N/A						Q4-2018
966	SHIP CONSTRUCTION TURNKEY	Longford	Ballinamuck (Phase 2)	4	*N/A						Q3-2019
967	SHIP CONSTRUCTION TURNKEY	Longford	Ballinamuck (Phase 3)	6	*N/A				Stage 4 approved Q3-2018, the scheme is fully approved.		
968	SHIP CONSTRUCTION TURNKEY	Longford	Rock View, Cloondara	5	*N/A						Q4-2018
969	SHIP CONSTRUCTION TURNKEY	Longford	Greville Court, Granard	14	*N/A					Q3-2018	
970	SHIP CONSTRUCTION TURNKEY	Longford	Knock, Lanesborough (Phase 2)	29	*N/A						Q4-2018
971	SHIP CONSTRUCTION TURNKEY	Longford	Mill Race Park, Drumlish	2	*N/A					Q1-2019	
972	SHIP CONSTRUCTION TURNKEY	Longford	Carragh, Granard	4	*N/A						Q3-2019
973	SHIP CONSTRUCTION TURNKEY	Longford	Church Street, Edgeworthstown	5	*N/A					Q1-2019	
974	SHIP CONSTRUCTION TURNKEY	Longford	Smithfield, Legan	18	*N/A				Stage 4 approved Q2-2019, the scheme is fully approved.		
975	SHIP CONSTRUCTION TURNKEY	Longford	Mill Race Park, Drumlish	4	*N/A					Q2-2019	
976	SHIP CONSTRUCTION TURNKEY	Longford	Mill Race Park, Drumlish	4	*N/A						Q2-2019
977	SHIP CONSTRUCTION TURNKEY	Longford	Carragh, Granard (Phase 4)	6	*N/A				Stage 4 approved Q1-2019, the scheme is fully approved.		
978	SHIP CONSTRUCTION TURNKEY	Longford	Carragh, Granard (Phase 2)	4	*N/A						Q2-2019
979	SHIP CONSTRUCTION TURNKEY	Longford	Mill Race Park, Drumlish (Phase 3)	4	*N/A						Q3-2019

980	SHIP CONSTRUCTION TURNKEY	Longford	Abhainn Glas, Edgeworthstown	4	*N/A					Q3-2019	
981	SHIP CONSTRUCTION TURNKEY	Longford	Carragh, Granard(Phase 3)	4	*N/A				Stage 4 approved Q1-2019, the scheme is fully approved.		
982	SHIP CONSTRUCTION TURNKEY	Longford	Mill Race Park, Drumlish	2	*N/A				Stage 4 approved Q1-2019, the scheme is fully approved.		
983	SHIP CONSTRUCTION TURNKEY	Longford	Carragh, Granard	7	*N/A					Q1-2019	
984	CALF Construction	Louth	Bishops Court, Dundalk, Co Louth (Phase 1)	2	Túath Housing Association Ltd					Q4-2018	
985	CALF Construction	Louth	Fire Station Site, Scarlett St, Drogheda (Phase 1)	15	North & East Housing Association Ltd					Q2-2018	
986	CALF Construction	Louth	Post Tender - Clos na Manach, Carlingford, Co Louth (Phase 1)	10	Túath Housing Association Ltd						Q2-2018
987	CALF Construction	Louth	Slieve Row Crescent, Dundalk (Phase 1)	1	Cluid Housing						Q2-2016
988	CALF Turnkey	Louth	2 units An Rian, Termonfeckin Rd., Drogheda, Co. Louth (Phase 1)	2	North & East Housing Association Ltd						Q2-2019
989	CALF Turnkey	Louth	Aston Village, Drogheda (Phase 1)*	8	Respond						Q3-2018
990	CALF Turnkey	Louth	Castle Court, Castlebellingham, Louth (Phase 1)	4	Cluid Housing						Q1-2017
991	CALF Turnkey	Louth	Castle Court, Castlebellingham, Louth (Phase 2)	10	Cluid Housing						Q1-2017
992	CALF Turnkey	Louth	Castleguard, Ardee, Co. Louth (Phase 1)	9	Túath Housing Association Ltd						Q1-2018
993	CALF Turnkey	Louth	Castleguard, Ardee, Co. Louth (Phase 2)*	20	Túath Housing Association Ltd						Q1-2018
994	CALF Turnkey	Louth	Castleguard, Ardee, Co. Louth (Phase 3)	8	Túath Housing Association Ltd						Q3-2018
995	CALF Turnkey	Louth	Castleguard, Ardee, Co. Louth (Phase 4)	15	Túath Housing Association Ltd						Q3-2018
996	CALF Turnkey	Louth	Castleguard, Ardee, Co. Louth (Phase 5)	6	Túath Housing Association Ltd						Q4-2018
997	CALF Turnkey	Louth	Castleguard, Ardee, Co. Louth (Phase 6)*	22	Túath Housing Association Ltd						Q4-2018
998	CALF Turnkey	Louth	Castleguard, Ardee, Co. Louth (Phase 7)	22	Túath Housing Association Ltd						Q2-2019
999	CALF Turnkey	Louth	Cois Cuain, Upper Point Road, Dundalk, Co. Louth (Phase 1)*	13	Túath Housing Association Ltd						Q4-2018

1000	CALF Turnkey	Louth	Cois Cuain, Upper Point Road, Dundalk, Co. Louth (Phase 2)	8	Túath Housing Association Ltd							Q1-2019
1001	CALF Turnkey	Louth	Cois Cuain, Upper Point Road, Dundalk, Co. Louth (Phase 3)	7	Túath Housing Association Ltd							Q2-2019
1002	CALF Turnkey	Louth	Coulter Place Armagh Road (Phase 1)	10	Cluid Housing							Q1-2017
1003	CALF Turnkey	Louth	Coulter Place Armagh Road (Phase 2)	12	Cluid Housing							Q3-2017
1004	CALF Turnkey	Louth	Dowdallshill, Dundalk, Co. Louth (Phase 1)	13	North & East Housing Association Ltd						Q3-2018	
1005	CALF Turnkey	Louth	Dublin Road, Dundalk, Co. Louth (Phase 1)*	14	Respond							Q1-2019
1006	CALF Turnkey	Louth	Dublin Road, Dundalk, Co. Louth (Phase 2)*	17	Respond						Q3-2017	
1007	CALF Turnkey	Louth	Dundoogan, Haynestown, Dundalk, Co. Louth (Phase 1)*	11	Túath Housing Association Ltd							Q2-2019
1008	CALF Turnkey	Louth	Dundoogan, Haynestown, Dundalk, Co. Louth (Phase 2)*	14	Túath Housing Association Ltd							Q2-2019
1009	CALF Turnkey	Louth	Dundoogan, Haynestown, Dundalk, Co. Louth (Phase 3)*	15	Túath Housing Association Ltd							Q2-2019
1010	CALF Turnkey	Louth	Dundoogan, Haynestown, Dundalk, Co. Louth (Phase 4)*	47	Túath Housing Association Ltd							Q3-2019
1011	CALF Turnkey	Louth	Dundoogan, Haynestown, Dundalk, Co. Louth (Phase 5)*	25	Túath Housing Association Ltd						Q2-2018	
1012	CALF Turnkey	Louth	Harbour Grove, Dundalk, Co. Louth (Phase 1)	8	North & East Housing Association Ltd						Q3-2018	
1013	CALF Turnkey	Louth	Knock Shee, Old Golf Links Road, Blackrock, Co Louth (Phase 1)	3	Cluid Housing							Q4-2017
1014	CALF Turnkey	Louth	Liscorrie, Bog Lane, Drogheda (Phase 1)	41	Túath Housing Association Ltd							Q4-2017
1015	CALF Turnkey	Louth	Mount Hamilton, Dundalk, Co. Louth (Phase 1)	20	Cluid Housing						Q4-2018	
1016	CALF Turnkey	Louth	Racecourse Meadows, Dundalk, Co. Louth - Clanmil (Phase 1)	20	Clanmil Housing Association Ireland						Q1-2019	
1017	CALF Turnkey	Louth	Racecourse Meadows, Dundalk, Co. Louth - Clanmil (Phase 2)*	25	Clanmil Housing Association Ireland						Q1-2019	
1018	CALF Turnkey	Louth	Rath na Gloine, Commons Road, Louth (Phase 1)	3	Cluid Housing							Q3-2016
1019	CALF Turnkey	Louth	Rathmullen Road, Drogheda, Co. Louth (Phase 1)	3	North & East Housing Association Ltd							Q4-2018

1020	CALF Turnkey	Louth	Rathmullen Road, Drogheda, Co. Louth (Phase 2)	6	North & East Housing Association Ltd							Q2-2019
1021	CALF Turnkey	Louth	Rathmullen Road, Drogheda, Co. Louth (Phase 3)	3	North & East Housing Association Ltd							Q3-2019
1022	CALF Turnkey	Louth	Rathmullen Road, Drogheda, Co. Louth (Phase 4)	14	North & East Housing Association Ltd							Q3-2019
1023	CALF Turnkey	Louth	Rathmullen Road, Drogheda, Co. Louth (Phase 5)	28	North & East Housing Association Ltd					Q4-2017		
1024	CALF Turnkey	Louth	Rathmullen Road, Drogheda, Co. Louth (Tuath) (Phase 1)	4	Túath Housing Association Ltd							Q2-2018
1025	CALF Turnkey	Louth	Rathmullen Road, Drogheda, Co. Louth (Tuath) (Phase 2)	6	Túath Housing Association Ltd							Q3-2018
1026	CALF Turnkey	Louth	Rathmullen Road, Drogheda, Co. Louth (Tuath) (Phase 3)	4	Túath Housing Association Ltd							Q3-2018
1027	CALF Turnkey	Louth	Rathmullen Road, Drogheda, Co. Louth (Tuath) (Phase 4)	15	Túath Housing Association Ltd							Q4-2018
1028	CALF Turnkey	Louth	Rathmullen Road, Drogheda, Co. Louth (Tuath) (Phase 5)	6	Túath Housing Association Ltd							Q2-2019
1029	CALF Turnkey	Louth	Rathmullen Road, Drogheda, Co. Louth (Tuath) (Phase 6)	16	Túath Housing Association Ltd					Q4-2017		
1030	CALF Turnkey	Louth	Revised - 43 Units at Mount Hamilton, Dundalk, Co Louth (Phase 1)	12	Cluid Housing							Q4-2017
1031	CALF Turnkey	Louth	Revised - 43 Units at Mount Hamilton, Dundalk, Co Louth (Phase 2)	15	Cluid Housing							Q3-2019
1032	CALF Turnkey	Louth	Revised - 43 Units at Mount Hamilton, Dundalk, Co Louth (Phase 3)	16	Cluid Housing					Q1-2017		
1033	CALF Turnkey	Louth	Termon River, Baltray Road, Termonfeckin, Co. Louth (Phase 1)	1	North & East Housing Association Ltd					Q1-2018		
1034	CALF Turnkey	Louth	Termon River, Baltray Road, Termonfeckin, Drogheda, Co.Louth (Phase 1)*	1	North & East Housing Association Ltd					Q1-2018		
1035	CAS CONSTRUCTION	Louth	5 Slieveroe Crescent, Dundalk	1	Cluid Housing Association		Stage 2 approved Q2-2018, full design/tender being prepared.					
1036	CAS CONSTRUCTION	Louth	Castletowncooley, Riverstown, Dundalk	1	Túath Housing Association Ltd		Stage 2 approved Q4-2017, full design/tender being prepared.					
1037	CAS CONSTRUCTION	Louth	Barrack Street, Dundalk	21	Simon Community : Dundalk Simon		Stage 2 approved Q3-2018, full design/tender being prepared.					
1038	CAS CONSTRUCTION	Louth	Saltown, Dundalk	7	North & East Housing Association Ltd			Stage 3 approved Q3-2018, the scheme is now approved to proceed to tender.				
1039	CAS CONSTRUCTION	Louth	McArdle Green (Moneymore), Drogheda	1	North & East Housing Association Ltd							Q4-2018

1040	CAS CONSTRUCTION	Louth	Tierney Street, Ardee	7	Oaklee Housing Trust			Stage 3 approved Q1-2018, the scheme is now approved to proceed to tender.			
1041	CAS CONSTRUCTION	Louth	Tredagh View, Drogheda	1	Respond						Q1-2017
1042	CAS CONSTRUCTION	Louth	36 Strand Hill, Clogherhead	4	St. John of God Housing Association Ltd	Stage 1 approved Q2-2017, outline design and costs being prepared.					
1043	CAS CONSTRUCTION	Louth	Coulter Park, Dundalk	7	Túath Housing Association Ltd		Stage 2 approved Q2-2019, full design/tender being prepared.				
1044	CAS CONSTRUCTION	Louth	Four Winds, Mullacapple, Collon	1	St. John of God Housing Association Ltd		Stage 2 approved Q2-2019, full design/tender being prepared.				
1045	CAS CONSTRUCTION	Louth	St. John's Home, Peter's Hill, Drogheda	4	North & East Housing Association Ltd		Stage 2 approved Q2-2019, full design/tender being prepared.				
1046	CAS CONSTRUCTION	Louth	Riverwell Close, Dundalk	1	Respond		Stage 2 approved Q2-2019, full design/tender being prepared.				
1047	CAS CONSTRUCTION	Louth	Carntown, Ballymackenny, Drogheda	1	St. John of God Housing Association Ltd	Stage 1 approved Q2-2019, outline design and costs being prepared.					
1048	PUBLIC PRIVATE PARTNERSHIP (Bundle 1)	Louth	Ravel Ardee Road, Dunleer	80	*N/A					Q1-2019	
1049	REGENERATION	Louth	Cox's Demesne Phase 2a	14	*N/A						Q4-2016
1050	REGENERATION	Louth	Cox's Demesne Phase 2b	22	*N/A			Stage 3 approved Q2-2019, the scheme is now approved to proceed to tender.			
1051	SHIP CONSTRUCTION	Louth	55/57 Bothar Brugha, Drogheda	3	*N/A						Q4-2017
1052	SHIP CONSTRUCTION	Louth	Infill Housing Construction, Gort Uaine, Clogherhead, Co. Louth	1	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
1053	SHIP CONSTRUCTION	Louth	Infill Housing Construction, School Lane, Dunleer, Co. Louth	1	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
1054	SHIP CONSTRUCTION	Louth	CPO Bundle 2	4	*N/A						Q1-2018
1055	SHIP CONSTRUCTION	Louth	CPO Bundle 1	7	*N/A						Q4-2016
1056	SHIP CONSTRUCTION	Louth	CPO Bundle 1 - Phase 2	5	*N/A						Q2-2017
1057	SHIP CONSTRUCTION	Louth	CPO Bundle 1 - Phase 3	3	*N/A						Q3-2017
1058	SHIP CONSTRUCTION	Louth	Woodlands, Dunleer	4	*N/A						Q4-2016
1059	SHIP CONSTRUCTION	Louth	Boice Court, Drogheda (Phase 2 - 4)	69	*N/A		Stage 2 approved Q3-2017, full design/tender being prepared.				

1060	SHIP CONSTRUCTION	Louth	Father Finn Park (Phase 2)	17	*N/A			Stage 3 approved Q2-2019, the scheme is now approved to proceed to tender.			
1061	SHIP CONSTRUCTION	Louth	CPO Bundle 1 - Phase 4	7	*N/A						Q4-2017
1062	SHIP CONSTRUCTION	Louth	Mount Avenue, Dundalk	93	*N/A	Stage 1 approved Q4-2017, outline design and costs being prepared.					
1063	SHIP CONSTRUCTION	Louth	CPO Bundle 1 - Phase 5	1	*N/A						Q3-2018
1064	SHIP CONSTRUCTION	Louth	CPO Bundle 2 - Phase 2	1	*N/A						Q3-2018
1065	SHIP CONSTRUCTION	Louth	CPO Bundle 2 - Phase 6	4	*N/A					Q3-2017	
1066	SHIP CONSTRUCTION	Louth	CPO Bundle 3	2	*N/A						Q2-2017
1067	SHIP CONSTRUCTION	Louth	CPO Bundle 3 - Phase 2	1	*N/A						Q3-2017
1068	SHIP CONSTRUCTION	Louth	CPO Bundle 3 - Phase 3	4	*N/A						Q4-2017
1069	SHIP CONSTRUCTION	Louth	CPO Bundle 3 - Phase 7	2	*N/A						Q1-2019
1070	SHIP CONSTRUCTION	Louth	CPO Bundle 4	1	*N/A						Q3-2018
1071	SHIP CONSTRUCTION	Louth	CPO Bundle 1 - Phase 6	1	*N/A				Stage 4 approved Q1-2016, the scheme is fully approved.		
1072	SHIP CONSTRUCTION	Louth	CPO Bundle 4 - Phase 3	5	*N/A						Q1-2019
1073	SHIP CONSTRUCTION	Louth	CPO Bundle 3 - Phase 4	1	*N/A						Q2-2018
1074	SHIP CONSTRUCTION	Louth	CPO Bundle 3 - Phase 5	4	*N/A						Q3-2018
1075	SHIP CONSTRUCTION	Louth	CPO Bundle 2 - Phase 3	1	*N/A						Q1-2019
1076	SHIP CONSTRUCTION	Louth	CPO Bundle 2 - Phase 4	1	*N/A						Q4-2018
1077	SHIP CONSTRUCTION	Louth	CPO Bundle 4 - Phase 2	4	*N/A						Q4-2018
1078	SHIP CONSTRUCTION	Louth	CPO Bundle 3 - Phase 6	5	*N/A						Q4-2018
1079	SHIP CONSTRUCTION	Louth	CPO Bundle 4 - Phase 4	1	*N/A						Q4-2018

1100	SHIP CONSTRUCTION	Mayo	Deel Court, Crossmolina	3	*N/A				Stage 4 approved Q1-2019, the scheme is fully approved.		
1101	SHIP CONSTRUCTION	Mayo	Kilmaine	6	*N/A					Q3-2019	
1102	SHIP CONSTRUCTION	Mayo	Knockroe, Moygownagh	3	*N/A				Stage 4 approved Q1-2019, the scheme is fully approved.		
1103	SHIP CONSTRUCTION	Mayo	Church Road, Belmullet	5	*N/A				Stage 4 approved Q2-2019, the scheme is fully approved.		
1104	SHIP CONSTRUCTION	Mayo	Knocknageeha, Newport	1	*N/A						Q2-2019
1105	SHIP CONSTRUCTION	Mayo	Kilkelly Road, Knock (Phase 3)	4	*N/A						Q3-2018
1106	SHIP CONSTRUCTION	Mayo	Kilmeena (Phase 2)	4	*N/A						Q3-2018
1107	SHIP CONSTRUCTION	Mayo	Knockmore, Ballina	8	*N/A						Q1-2019
1108	SHIP CONSTRUCTION	Mayo	Radharc an tSaillin, Binghamstown, Belmullet (Phase 2)	4	*N/A						Q2-2019
1109	SHIP CONSTRUCTION	Mayo	Sliabh Rua, Foxford (Phase 3)	10	*N/A					Q4-2018	
1110	SHIP CONSTRUCTION	Mayo	Woodlands, Balla (Phase 3)	4	*N/A					Q4-2018	
1111	SHIP CONSTRUCTION	Mayo	Slianaunroe, Clogher (SRD)	1	*N/A						Q2-2017
1112	SHIP CONSTRUCTION	Mayo	Abbeyquarter, Ballyhaunis	18	*N/A					Q1-2019	
1113	SHIP CONSTRUCTION	Mayo	Tonragee West, Achill (Phase 2)	5	*N/A					Q1-2019	
1114	SHIP CONSTRUCTION	Mayo	Sli na Roba, Friarsquarter, Ballinrobe	16	*N/A					Q4-2018	
1115	SHIP CONSTRUCTION	Mayo	Marian Crescent, Ballina	4	*N/A						Q2-2018
1116	SHIP CONSTRUCTION	Mayo	Tubberhill, Westport (Phase 3)	21	*N/A						Q1-2018
1117	SHIP CONSTRUCTION	Mayo	St. Patrick's Terrace, Westport	1	*N/A						Q3-2017
1118	SHIP CONSTRUCTION	Mayo	Parke, Castlebar	8	*N/A					Q4-2018	
1119	SHIP CONSTRUCTION	Mayo	Killavally	10	*N/A					Q4-2018	

1120	SHIP CONSTRUCTION	Mayo	Kilkelly Road, Swinford	27	*N/A					Q1-2019	
1121	SHIP CONSTRUCTION	Mayo	Barhauve, Rosspoint (SRD)	1	*N/A						Q2-2018
1122	SHIP CONSTRUCTION	Mayo	Gluggaun, Ballycroy (SRD)	1	*N/A						Q4-2017
1123	SHIP CONSTRUCTION	Mayo	Glengad, Pollatomish (SRD)	1	*N/A						Q2-2018
1124	SHIP CONSTRUCTION	Mayo	Gorthbrack, Inver (SRD)	1	*N/A						Q1-2018
1125	SHIP CONSTRUCTION	Mayo	Cross	15	*N/A			Stage 2 approved Q3-2019, full design/tender being prepared.			
1126	SHIP CONSTRUCTION	Mayo	Bonniconlon	5	*N/A			Stage 2 approved Q2-2019, full design/tender being prepared.			
1127	SHIP CONSTRUCTION	Mayo	Cloonkeadagh Road, Kiltimagh	23	*N/A			Stage 2 approved Q3-2019, full design/tender being prepared.			
1128	SHIP CONSTRUCTION	Mayo	Rehins Fort, Ballina	50	*N/A			Stage 2 approved Q3-2019, full design/tender being prepared.			
1129	SHIP CONSTRUCTION TURNKEY	Mayo	Carrabeg, Newport Road, Castlebar	2	*N/A						Q4-2018
1130	SHIP CONSTRUCTION TURNKEY	Mayo	Cois Abhainn, Bonniconlon	2	*N/A						Q2-2019
1131	SHIP CONSTRUCTION TURNKEY	Mayo	Chapel Street, Louisburgh	3	*N/A					Q4-2018	
1132	SHIP CONSTRUCTION TURNKEY	Mayo	Bunree, Ballina	3	*N/A				Stage 4 approved Q2-2019, the scheme is fully approved.		
1133	SHIP CONSTRUCTION TURNKEY	Mayo	Friars Court, Ballina	2	*N/A					Q2-2019	
1134	SHIP CONSTRUCTION TURNKEY	Mayo	Riverside Drive, Ballina	3	*N/A					Q2-2019	
1135	SHIP CONSTRUCTION TURNKEY	Mayo	Davitt Terrace, Castlebar	4	*N/A					Q3-2019	
1136	SHIP CONSTRUCTION TURNKEY	Mayo	Ard Rua, Claremorris	7	*N/A					Q3-2019	
1137	SHIP CONSTRUCTION TURNKEY	Mayo	Bridge St., Louisburgh	1	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
1138	CALF Turnkey	Meath	18 units Churchfields, Ashbourne, Co. Meath (Phase 1)	18	Túath Housing Association Ltd						Q4-2018
1139	CALF Turnkey	Meath	5 units Dunville, Athlumney, Navan, Co. Meath (Phase 1)	5	Túath Housing Association Ltd						Q1-2019

1160	CALF Turnkey	Meath	Eastham Square, Bettystown, Meath (Phase 1)*	5	Cluid Housing							Q1-2019
1161	CALF Turnkey	Meath	Fitzherbert Wood, Slane Road, Navan, Co Meath (Phase 1)*	1	Túath Housing Association Ltd							Q3-2018
1162	CALF Turnkey	Meath	Fredrick Manor, Ashbourne, Co. Meath (Phase 1)	4	Cluid Housing						Q4-2017	
1163	CALF Turnkey	Meath	Fredrick Manor, Ashbourne, Co. Meath (Phase 2)	7	Cluid Housing						Q4-2017	
1164	CALF Turnkey	Meath	Gainsfield, Commons Road, Navan, Co. Meath (Phase 1)	20	Túath Housing Association Ltd						Q3-2018	
1165	CALF Turnkey	Meath	Gainsfield, Commons Road, Navan, Co. Meath (Phase 2)	21	Túath Housing Association Ltd						Q3-2018	
1166	CALF Turnkey	Meath	Gainsfield, Commons Road, Navan, Co. Meath (Phase 3)	13	Túath Housing Association Ltd						Q3-2018	
1167	CALF Turnkey	Meath	Grangehall, Dunshaughlin (Phase 1)	7	Túath Housing Association Ltd							Q2-2018
1168	CALF Turnkey	Meath	Kellets Grove, Dunshauglin, Co Meath (Phase 1)*	6	Túath Housing Association Ltd							Q1-2018
1169	CALF Turnkey	Meath	Mill Lane, Flower Hill, Navan, Co Meath (Phase 1)	20	Oaklee Housing							Q4-2016
1170	CALF Turnkey	Meath	Millrace Court, Emmet Street, Trim, Co Meath (Phase 1)	11	North & East Housing Association Ltd							Q2-2018
1171	CALF Turnkey	Meath	Milltown, Ashbourne, Co Meath (Phase 1)	11	Cluid Housing							Q1-2017
1172	CALF Turnkey	Meath	Milltown, Ashbourne, Co Meath (Phase 2)	36	Cluid Housing							Q4-2017
1173	CALF Turnkey	Meath	Milltown, Ashbourne, Co Meath (Phase 3)	20	Cluid Housing							Q4-2017
1174	CALF Turnkey	Meath	Moydervey Manor, Longwood, Trim, Co. Meath (Phase 1)*	6	Túath Housing Association Ltd						Q4-2018	
1175	CALF Turnkey	Meath	Moydervey Manor, Longwood, Trim, Co. Meath (Phase 2)	7	Túath Housing Association Ltd						Q4-2018	
1176	CALF Turnkey	Meath	Revised - Fitzherbert Wood, Slane Road, Navan, Co Meath (Phase 1)	3	Túath Housing Association Ltd							Q4-2018
1177	CALF Turnkey	Meath	Revised - Fitzherbert Wood, Slane Road, Navan, Co Meath (Phase 2)	6	Túath Housing Association Ltd							Q2-2019
1178	CALF Turnkey	Meath	Revised - Fitzherbert Wood, Slane Road, Navan, Co Meath (Phase 3)	2	Túath Housing Association Ltd							Q3-2019
1179	CALF Turnkey	Meath	Revised - Fitzherbert Wood, Slane Road, Navan, Co Meath (Phase 4)	5	Túath Housing Association Ltd							Q3-2019

1180	CALF Turnkey	Meath	Revised - Fitzherbert Wood, Slane Road, Navan, Co Meath (Phase 5)	4	Túath Housing Association Ltd					Q2-2018	
1181	CALF Turnkey	Meath	Revised - Fitzherbert Wood, Slane Road, Navan, Co Meath (Phase 6)	4	Túath Housing Association Ltd					Q2-2018	
1182	CALF Turnkey	Meath	Revised - Fitzherbert Wood, Slane Road, Navan, Co Meath (Phase 7)	20	Túath Housing Association Ltd					Q2-2018	
1183	CALF Turnkey	Meath	Royal Oaks, Enfield, Co Meath (Phase 1)*	4	Cluid Housing						Q2-2017
1184	CALF Turnkey	Meath	Seabury Lawns, Mornington, Co. Meath (Phase 1)	25	Cluid Housing						Q3-2017
1185	CALF Turnkey	Meath	Station Road, Dunboyne, Co. Meath (Phase 1)	24	Respond						Q4-2018
1186	CALF Turnkey	Meath	Tubberclair, Navan, Co Meath (Phase 1)	8	Cluid Housing						Q2-2016
1187	CALF Turnkey	Meath	Tubberclair, Navan, Co Meath (Phase 2)	7	Cluid Housing						Q3-2016
1188	CALF Turnkey	Meath	Tubberclair, Navan, Co Meath (Phase 3)	8	Cluid Housing						Q4-2016
1189	CAS CONSTRUCTION	Meath	Blackcastle, Slane Road, Navan	17	Túath Housing Association Ltd						Q4-2018
1190	SHIP CONSTRUCTION	Meath	Proudstown Road, Navan	4	*N/A						Q4-2018
1191	SHIP CONSTRUCTION	Meath	The Belfry, Trim	3	*N/A					Q1-2019	
1192	SHIP CONSTRUCTION	Meath	Bettystown (Phase 3)	13	*N/A					Q1-2019	
1193	SHIP CONSTRUCTION	Meath	St. Oliver's, Ratoath	17	*N/A					Q1-2018	
1194	SHIP CONSTRUCTION	Meath	Riverside, Kells	40	*N/A					Q1-2019	
1195	SHIP CONSTRUCTION	Meath	Cherry Court, Summerhill	19	*N/A						Q1-2019
1196	SHIP CONSTRUCTION	Meath	Connaught Grove, Athboy	32	*N/A						Q2-2018
1197	SHIP CONSTRUCTION	Meath	Nobber	19	*N/A				Stage 4 approved Q4-2018, the scheme is fully approved.		
1198	SHIP CONSTRUCTION	Meath	Carlanstown	13	*N/A					Q2-2019	
1199	SHIP CONSTRUCTION	Meath	Donore	21	*N/A		Stage 2 approved Q2-2018, full design/tender being prepared.				

1200	SHIP CONSTRUCTION	Meath	Dunshaughlin	26	*N/A			Stage 3 approved Q2-2019, the scheme is now approved to proceed to tender.			
1201	SHIP CONSTRUCTION	Meath	Bettystown (Phase 2)	2	*N/A						Q3-2019
1202	SHIP CONSTRUCTION	Meath	Bettystown (Phase 1)	16	*N/A						Q3-2017
1203	SHIP CONSTRUCTION	Meath	Farganstown	86	*N/A	Stage 1 approved Q1-2018, outline design and costs being prepared.					
1204	SHIP CONSTRUCTION	Meath	Blackhill Crescent, Donacorney	2	*N/A	Stage 1 approved Q3-2018, outline design and costs being prepared.					
1205	SHIP CONSTRUCTION	Meath	Archdeaconary Glebe, Kells	20	*N/A	Stage 1 approved Q3-2018, outline design and costs being prepared.					
1206	SHIP CONSTRUCTION	Meath	Nangle Court, Navan	6	*N/A	Stage 1 approved Q3-2018, outline design and costs being prepared.					
1207	SHIP CONSTRUCTION	Meath	Dept of Education site, Castle Street, Ashbourne	55	*N/A	Stage 1 approved Q3-2018, outline design and costs being prepared.					
1208	SHIP CONSTRUCTION	Meath	Church View, Rathmolyon	9	*N/A	Stage 1 approved Q3-2018, outline design and costs being prepared.					
1209	SHIP CONSTRUCTION RAPID	Meath	Kilmainhamwood	4	*N/A					Q1-2019	
1210	SHIP CONSTRUCTION RAPID	Meath	Cortown	10	*N/A					Q1-2019	
1211	SHIP CONSTRUCTION RAPID	Meath	Oldcastle	16	*N/A					Q1-2019	
1212	SHIP CONSTRUCTION TURNKEY	Meath	Cois Glaisin, Johnstown, Navan	19	*N/A						Q4-2018
1213	SHIP CONSTRUCTION TURNKEY	Meath	Cluain Adain, Clonmagadden, Navan	16	*N/A						Q4-2018
1214	SHIP CONSTRUCTION TURNKEY	Meath	Dun Eimear, Bettystown, Co. Meath	8	*N/A						Q3-2019
1215	SHIP CONSTRUCTION TURNKEY	Meath	Bracken Hill, Kilmessan	3	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
1216	SHIP CONSTRUCTION TURNKEY	Meath	Cluain Adain, Clonmagadden, Navan	4	*N/A						Q3-2019
1217	SHIP CONSTRUCTION TURNKEY	Meath	Cois Glaisin Walk, Johnstown, Navan	5	*N/A						Q4-2018
1218	SHIP CONSTRUCTION TURNKEY	Meath	Cois Glaisin Walk, Johnstown, Navan	4	*N/A						Q3-2019
1219	SHIP CONSTRUCTION TURNKEY	Meath	Cois Glaisin, Johnstown, Navan	8	*N/A						Q2-2019

1220	CALF Construction	Monaghan	Post Tender - Liseggerton Road, Clones (Phase 1)	6	Oaklee Housing							Q4-2018
1221	CALF Turnkey	Monaghan	Bree, Castleblayney, Co. Monaghan (Phase 1)	8	Túath Housing Association Ltd							Q2-2019
1222	CALF Turnkey	Monaghan	Bree, Castleblayney, Co. Monaghan (Phase 2)	14	Túath Housing Association Ltd							Q2-2019
1223	CALF Turnkey	Monaghan	Bree, Castleblayney, Co. Monaghan (Phase 3)	8	Túath Housing Association Ltd							Q2-2019
1224	CALF Turnkey	Monaghan	Bree, Castleblayney, Co. Monaghan (Phase 4)	8	Túath Housing Association Ltd							Q2-2019
1225	CALF Turnkey	Monaghan	Kingscourt Road, Carrickmacross, Co Monaghan (Phase 1)	18	Respond							Q2-2018
1226	CALF Turnkey	Monaghan	Kingscourt Road, Carrickmacross, Co Monaghan (Phase 2)	12	Respond							Q2-2018
1227	CALF Turnkey	Monaghan	Kingscourt Road, Carrickmacross, Co Monaghan (Phase 3)	20	Respond							Q2-2018
1228	CAS CONSTRUCTION	Monaghan	Drumillard, Castleblayney (Phase 2)	2	Castleblayney Care Housing Association Ltd		Stage 2 approved Q1-2018, full design/tender being prepared.					
1229	CAS CONSTRUCTION	Monaghan	Liseggerton, Clones	16	Oaklee Housing Trust				Stage 4 approved Q3-2019, the scheme is fully approved.			
1230	CAS CONSTRUCTION	Monaghan	Convent Lands, Carrickmacross	7	Respond							Q2-2017
1231	SHIP CONSTRUCTION	Monaghan	Bree, Castleblayney	8	*N/A							Q2-2019
1232	SHIP CONSTRUCTION	Monaghan	Latlorcan, Monaghan Town	43	*N/A							Q3-2018
1233	SHIP CONSTRUCTION	Monaghan	Davy's & Adjacent Porperty, Fermanagh St., Clones	3	*N/A							Q3-2019
1234	SHIP CONSTRUCTION	Monaghan	Boyle Sports Site, Fermanagh St., Clones	3	*N/A							Q3-2019
1235	SHIP CONSTRUCTION	Monaghan	82 & 83 Fermanagh St., Clones	3	*N/A							Q3-2019
1236	SHIP CONSTRUCTION	Monaghan	An Bonnan Bui & Flower Shop, Fermanagh St., Clones	6	*N/A							Q3-2019
1237	SHIP CONSTRUCTION	Monaghan	2a & 3 Analore St., Clones	2	*N/A							Q3-2019
1238	SHIP CONSTRUCTION	Monaghan	Abbey Gatehouse, Analore St., Clones	4	*N/A							Q3-2019
1239	SHIP CONSTRUCTION	Monaghan	Lui Na Greine, Scotstown	32	*N/A		Stage 2 approved Q2-2019, full design/tender being prepared.					

1260	CAS CONSTRUCTION	Offaly	Scurragh, Birr	6	Cluid Housing Association					Q1-2019	
1261	CAS CONSTRUCTION	Offaly	Clonminch, Tullamore	19	Oaklee Housing Trust		Stage 2 approved Q1-2019, full design/tender being prepared.				
1262	CAS CONSTRUCTION	Offaly	Presentation Convent, Portlarlinton	32	Sophia Housing Association Ltd	Stage 1 approved Q1-2019, outline design and costs being prepared.					
1263	SHIP CONSTRUCTION	Offaly	Chancery Lane, Tullamore	14	*N/A					Q3-2018	
1264	SHIP CONSTRUCTION	Offaly	Circular Road, Daingean	7	*N/A	Stage 1 approved Q2-2017, outline design and costs being prepared.					
1265	SHIP CONSTRUCTION	Offaly	Kylebeg, Banagher (Phase 2)	18	*N/A	Stage 1 approved Q3-2017, outline design and costs being prepared.					
1266	SHIP CONSTRUCTION	Offaly	Blundell Wood, Edenderry	33	*N/A					Q4-2017	
1267	SHIP CONSTRUCTION	Offaly	Church Street, Clara	3	*N/A	Stage 1 approved Q3-2019, outline design and costs being prepared.					
1268	SHIP CONSTRUCTION	Offaly	Beechgrove, Belmont	7	*N/A	Stage 1 approved Q3-2019, outline design and costs being prepared.					
1269	SHIP CONSTRUCTION	Offaly	Raheen, Clara	38	*N/A	Stage 1 approved Q3-2019, outline design and costs being prepared.					
1270	SHIP CONSTRUCTION	Offaly	Elderberry Drive, Moneygall	4	*N/A	Stage 1 approved Q3-2019, outline design and costs being prepared.					
1271	SHIP CONSTRUCTION	Offaly	Sr. Senan Avenue, Edenderry	4	*N/A	Stage 1 approved Q3-2019, outline design and costs being prepared.					
1272	SHIP CONSTRUCTION TURNKEY	Offaly	McGregor, Birr (Phase 2)	8	*N/A				Stage 4 approved Q3-2018, the scheme is fully approved.		
1273	SHIP CONSTRUCTION TURNKEY	Offaly	Mill Race, Ferbane	5	*N/A						Q4-2017
1274	SHIP CONSTRUCTION TURNKEY	Offaly	Cluain na Spideoga, Cloghan	6	*N/A						Q2-2019
1275	SHIP CONSTRUCTION TURNKEY	Offaly	Frankford, Kilcormac	12	*N/A						Q4-2018
1276	SHIP CONSTRUCTION TURNKEY	Offaly	McGregor, Birr (Phase 1)	4	*N/A					Q1-2019	
1277	SHIP CONSTRUCTION TURNKEY	Offaly	Cluain na Greine, Cloneygowan	4	*N/A					Q3-2019	
1278	CALF Turnkey	Roscommon	Castle View Apartments, Block A, Roscommon Town (Phase 1)	10	Co-operative Housing Ireland					Q2-2019	
1279	CALF Turnkey	Roscommon	Revised - Monksfield Park, Bealnamulla, Athlone (Phase 1)	13	Cluid Housing						Q3-2018

1280	CALF Turnkey	Roscommon	River Oaks, Kilcolman, Ballaghaderreen, Co. Roscommon (Phase 1)	12	Respond						Q1-2018
1281	PUBLIC PRIVATE PARTNERSHIP (Bundle 2)	Roscommon	The Walk, Roscommon Town	53	*N/A				Q2-2019		
1282	SHIP CONSTRUCTION	Roscommon	Cloonfad	3	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
1283	SHIP CONSTRUCTION	Roscommon	Greenfields, Blackstick Road, Roscommon Town	6	*N/A						Q3-2017
1284	SHIP CONSTRUCTION	Roscommon	River Oaks, Ballaghaderreen	10	*N/A						Q4-2017
1285	SHIP CONSTRUCTION	Roscommon	Silveroe Meadows, Boyle	12	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
1286	SHIP CONSTRUCTION	Roscommon	Cluain Fraoigh, Cloonbeirne	7	*N/A			Stage 3 approved Q2-2019, the scheme is now approved to proceed to tender.			
1287	SHIP CONSTRUCTION	Roscommon	Old Tuam Road, Monkland, Athlone	2	*N/A			Stage 3 approved Q2-2019, the scheme is now approved to proceed to tender.			
1288	SHIP CONSTRUCTION	Roscommon	Meadowbrook, Ballyclare Td., Ballyleague, Co. Roscommon	18	*N/A		Stage 2 approved Q3-2019, full design/tender being prepared.				
1289	SHIP CONSTRUCTION	Roscommon	Lisroyne Td., Strokestown	10	*N/A	Stage 1 approved Q1-2019, outline design and costs being prepared.					
1290	SHIP CONSTRUCTION TURNKEY	Roscommon	Monksland, Athlone	10	*N/A						Q3-2018
1291	SHIP CONSTRUCTION TURNKEY	Roscommon	Station Road, Termon, Boyle	10	*N/A						Q1-2019
1292	SHIP CONSTRUCTION TURNKEY	Roscommon	Lisroyne Court, Strokestown	10	*N/A					Q3-2018	
1293	SHIP CONSTRUCTION TURNKEY	Roscommon	Warren Grove, Boyle	4	*N/A						Q4-2018
1294	SHIP CONSTRUCTION TURNKEY	Roscommon	Monksfield, Monkland, Co. Roscommon	2	*N/A					Q3-2019	
1295	CAS CONSTRUCTION	Sligo	Cuan Iosa, Ballymote	8	Society of Saint Vincent de Paul						Q4-2018
1296	CAS CONSTRUCTION	Sligo	Killeshin, First Sea Road, Sligo	5	Newgrove Housing Association Ltd		Stage 2 approved Q2-2019, full design/tender being prepared.				
1297	SHIP CONSTRUCTION	Sligo	94 St Joseph's Terrace	1	*N/A					Q4-2018	
1298	SHIP CONSTRUCTION	Sligo	Collooney	15	*N/A					Q4-2018	
1299	SHIP CONSTRUCTION	Sligo	Knappagh Road	28	*N/A					Q4-2018	

1340	CALF Turnkey	South Dublin	The Mews, Citywest Village, Citywest, Dublin 24 (Phase 1)*	22	Fold Housing Association Ireland Ltd					Q3-2019	
1341	CALF Turnkey	South Dublin	The Rise, Citywest Village, Citywest, Dublin 24 (Phase 1)*	13	Fold Housing Association Ireland Ltd					Q1-2018	
1342	CALF Turnkey	South Dublin	Tullyhall, Lucan, Co Dublin (Phase 1)*	2	Túath Housing Association Ltd						Q3-2017
1343	CALF Turnkey	South Dublin	Tullyhall, Lucan, Co Dublin (Phase 2)*	2	Túath Housing Association Ltd						Q4-2018
1344	CALF Turnkey	South Dublin	Westpark, Garters Lane, Saggert, Co Dublin (Phase 1)	28	Cluid Housing						Q4-2018
1345	CALF Turnkey	South Dublin	Westpark, Garters Lane, Saggert, Co Dublin (Phase 2)	28	Cluid Housing						Q2-2019
1346	CALF Turnkey	South Dublin	Westpark, Garters Lane, Saggert, Co Dublin (Phase 3)	28	Cluid Housing					Q2-2018	
1347	CALF Turnkey	South Dublin	Wilkins Court, Limekiln Lane, Dublin 12 (Phase 1)*	6	Circle Voluntary Housing Association Ltd						Q2-2019
1348	CALF Turnkey	South Dublin	Wilkins View, Greenhills, Dublin 12 (Phase 1)*	3	Circle Voluntary Housing Association Ltd						Q2-2018
1349	CAS CONSTRUCTION	South Dublin	Collinstown Grove, Clondalkin	4	Túath Housing Association Ltd					Q1-2019	
1350	CAS CONSTRUCTION	South Dublin	Old Nangor Road, Clondalkin	10	Simon Community : Dublin Simon				Stage 4 approved Q3-2019, the scheme is fully approved.		
1351	PUBLIC PRIVATE PARTNERSHIP (Bundle 1)	South Dublin	Corkage Grange (part of Kilarbery)	109	*N/A					Q1-2019	
1352	SHIP CONSTRUCTION	South Dublin	Killinarden, Tallaght	17	*N/A						Q4-2018
1353	SHIP CONSTRUCTION	South Dublin	Letts Field, Neilstown, Clondalkin	37	*N/A						Q4-2018
1354	SHIP CONSTRUCTION	South Dublin	Owendoher, Ballyboden, Rathfarnham	40	*N/A						Q1-2019
1355	SHIP CONSTRUCTION	South Dublin	Dromcarra, Tallaght	14	*N/A						Q4-2018
1356	SHIP CONSTRUCTION	South Dublin	Fortunestown (MacUilliam)	28	*N/A						Q4-2018
1357	SHIP CONSTRUCTION	South Dublin	Mayfield Estate, Clondalkin	17	*N/A						Q2-2018
1358	SHIP CONSTRUCTION	South Dublin	St Marks Green, Clondalkin	11	*N/A						Q3-2018
1359	SHIP CONSTRUCTION	South Dublin	St. Marks Avenue, Clondalkin	41	*N/A	Stage 1 approved Q1-2015, outline design and costs being prepared.					

1380	CALF Turnkey	Tipperary	Ashgrove, Monadreen, Thurles, Co. Tipperary (Phase 1)	17	Co-operative Housing Ireland					Q1-2019	
1381	CALF Turnkey	Tipperary	Mill Street, Carrick on Suir, Co. Tipperary (Phase 1)	22	Túath Housing Association Ltd					Q4-2018	
1382	CAS CONSTRUCTION	Tipperary	Ballinagrana, Carrick on Suir	3	Camphill Communities of Ireland		Stage 2 approved Q3-2019, full design/tender being prepared.				
1383	CAS CONSTRUCTION	Tipperary	Castle Street, Carrick on Suir	1	Camphill Communities of Ireland		Stage 2 approved Q3-2019, full design/tender being prepared.				
1384	CAS CONSTRUCTION	Tipperary	The Strand, Carrick on Suir	3	Camphill Communities of Ireland		Stage 2 approved Q3-2019, full design/tender being prepared.				
1385	CAS CONSTRUCTION	Tipperary	Glennconnor Road, Clonmel	9	Cluid Housing Association		Stage 2 approved Q4-2017, full design/tender being prepared.				
1386	CAS CONSTRUCTION	Tipperary	Stanwix House, Kickham Street, Thurles	19	Thurles Lions Trust Housing Assoc.		Stage 2 approved Q3-2018, full design/tender being prepared.				
1387	CAS CONSTRUCTION TURNKEY	Tipperary	Monastery Close, Templemore Road, Thurles	15	Thurles Lions Trust Housing Assoc.						Q2-2019
1388	SHIP CONSTRUCTION	Tipperary	Mulkear View, Newport, Tipperary	3	*N/A						Q4-2018
1389	SHIP CONSTRUCTION	Tipperary	Ard na Greine, Clonmel	2	*N/A		Stage 2 approved Q1-2018, full design/tender being prepared.				
1390	SHIP CONSTRUCTION	Tipperary	Knockanrawley	28	*N/A			Stage 3 approved Q2-2019, the scheme is now approved to proceed to tender.			
1391	SHIP CONSTRUCTION	Tipperary	Mill Road, Thurles	28	*N/A		Stage 2 approved Q1-2018, full design/tender being prepared.				
1392	SHIP CONSTRUCTION	Tipperary	Mulkear View, Newport	11	*N/A		Stage 2 approved Q4-2017, full design/tender being prepared.				
1393	SHIP CONSTRUCTION	Tipperary	Treacy Park, Carrick on Suir	1	*N/A						Q3-2018
1394	SHIP CONSTRUCTION	Tipperary	Templetouhy	10	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
1395	SHIP CONSTRUCTION	Tipperary	Borrisoleigh	12	*N/A	Stage 1 approved Q1-2016, outline design and costs being prepared.					
1396	SHIP CONSTRUCTION	Tipperary	Abbey Street, Cahir	10	*N/A			Stage 3 approved Q3-2019, the scheme is now approved to proceed to tender.			
1397	SHIP CONSTRUCTION	Tipperary	Borrisokane	16	*N/A				Stage 4 approved Q1-2019, the scheme is fully approved.		
1398	SHIP CONSTRUCTION	Tipperary	Portroe, Nenagh	14	*N/A		Stage 2 approved Q1-2018, full design/tender being prepared.				
1399	SHIP CONSTRUCTION	Tipperary	CloughJordan	2	*N/A				Stage 4 approved Q2-2019, the scheme is fully approved.		

1400	SHIP CONSTRUCTION	Tipperary	Glennonor Road, Clonmel	26	*N/A					Q4-2018	
1401	SHIP CONSTRUCTION	Tipperary	Gortataggart, Thurles	2	*N/A						Q4-2018
1402	SHIP CONSTRUCTION	Tipperary	Kilcooly Way, Gortnahoe	5	*N/A					Q1-2019	
1403	SHIP CONSTRUCTION	Tipperary	Lacey Avenue, Templemore	3	*N/A						Q3-2016
1404	SHIP CONSTRUCTION	Tipperary	Mitchel St., Thurles	1	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
1405	SHIP CONSTRUCTION	Tipperary	Borrisoleigh	1	*N/A						Q4-2016
1406	SHIP CONSTRUCTION	Tipperary	Lower Ballingarry	1	*N/A						Q2-2016
1407	SHIP CONSTRUCTION	Tipperary	Poulamaleen, Faugheen	1	*N/A						Q2-2016
1408	SHIP CONSTRUCTION	Tipperary	Cormack Drive, Nenagh	12	*N/A		Stage 2 approved Q2-2018, full design/tender being prepared.				
1409	SHIP CONSTRUCTION	Tipperary	Lacey Avenue, Templemore	1	*N/A						Q3-2017
1410	SHIP CONSTRUCTION	Tipperary	Borrisoleigh	1	*N/A						Q4-2018
1411	SHIP CONSTRUCTION	Tipperary	Bansha	14	*N/A		Stage 2 approved Q2-2019, full design/tender being prepared.				
1412	SHIP CONSTRUCTION	Tipperary	Twomileborris, Thurles	22	*N/A		Stage 2 approved Q2-2019, full design/tender being prepared.				
1413	SHIP CONSTRUCTION	Tipperary	Donohill,	4	*N/A		Stage 2 approved Q3-2019, full design/tender being prepared.				
1414	SHIP CONSTRUCTION	Tipperary	Mullinahone	10	*N/A		Stage 2 approved Q3-2019, full design/tender being prepared.				
1415	SHIP CONSTRUCTION	Tipperary	Clerihan	14	*N/A		Stage 2 approved Q3-2019, full design/tender being prepared.				
1416	SHIP CONSTRUCTION	Tipperary	Ard Alainn, Moyne	9	*N/A		Stage 2 approved Q3-2019, full design/tender being prepared.				
1417	SHIP CONSTRUCTION	Tipperary	Ardcroney	4	*N/A		Stage 1 approved Q3-2019, outline design and costs being prepared.				
1418	SHIP CONSTRUCTION TURNKEY	Tipperary	Cloneen Road, Fethard	6	*N/A						Q2-2019
1419	SHIP CONSTRUCTION TURNKEY	Tipperary	Strylea, Fethard	3	*N/A					Q4-2018	

1420	SHIP CONSTRUCTION TURNKEY	Tipperary	Ardan, Borrisokane	9	*N/A						Q4-2018
1421	SHIP CONSTRUCTION TURNKEY	Tipperary	An Grianan, Killenaule, Thurles	4	*N/A						Q4-2018
1422	SHIP CONSTRUCTION TURNKEY	Tipperary	Ardan, Borrisokane (Phase 2)	4	*N/A						Q2-2019
1423	SHIP CONSTRUCTION TURNKEY	Tipperary	An Grianan, Killenaule, Thurles (Phase 2)	5	*N/A					Q4-2018	
1424	SHIP CONSTRUCTION TURNKEY	Tipperary	Prior Park, Clonmel	41	*N/A				Stage 4 approved Q2-2019, the scheme is fully approved.		
1425	SHIP CONSTRUCTION TURNKEY	Tipperary	Ma Charoin, Manna South, Templemore	13	*N/A					Q3-2019	
1426	SHIP CONSTRUCTION TURNKEY	Tipperary	Cloneen Road, Fethard (Phase 2)	5	*N/A						Q3-2019
1427	SHIP CONSTRUCTION TURNKEY	Tipperary	Cloneen Road, Fethard (Phase 3)	6	*N/A					Q4-2018	
1428	SHIP CONSTRUCTION TURNKEY	Tipperary	Glencree, Newport	3	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
1429	SHIP CONSTRUCTION TURNKEY	Tipperary	Cloneen Road, Fethard (Phase 4)	4	*N/A					Q4-2018	
1430	SHIP CONSTRUCTION TURNKEY	Tipperary	An Grianan, Killenaule, Thurles	5	*N/A					Q4-2018	
1431	CALF Construction	Waterford	St Johns College, Waterford (Phase 1)	36	Respond						Q1-2016
1432	CALF Turnkey	Waterford	Kilbarry, Waterford (Phase 1)	69	Respond					Q4-2018	
1433	CALF Turnkey	Waterford	The Walk, Fairfield Park, Kilcohan, Waterford (Phase 1)	40	Circle Voluntary Housing Association Ltd					Q2-2018	
1434	CAS CONSTRUCTION	Waterford	Convent Hill, Tramore	10	Society of Saint Vincent de Paul						Q1-2017
1435	CAS CONSTRUCTION	Waterford	Powersfield, Hennessys Road, Waterford	3	Focus Ireland					Q3-2019	
1436	CAS CONSTRUCTION	Waterford	Wadding Manor, Ferrybank	10	Respond				Stage 4 approved Q1-2019, the scheme is fully approved.		
1437	CAS CONSTRUCTION	Waterford	Gleann Ealach, Dunhill	8	Gleann Ealach Housing Association		Stage 2 approved Q4-2017, full design/tender being prepared.				
1438	CAS CONSTRUCTION	Waterford	The Paddocks, Williamstown Rd. Waterford	9	Anvers Housing Association Ltd			Stage 3 approved Q2-2018, the scheme is now approved to proceed to tender.			
1439	PUBLIC PRIVATE PARTNERSHIP (Bundle 2)	Waterford	Slievekeale, Waterford City	58	*N/A					Q2-2019	

1440	SHIP CONSTRUCTION	Waterford	An Garran, Crobally Upper, Tramore	50	*N/A		Stage 2 approved Q2-2018, full design/tender being prepared.				
1441	SHIP CONSTRUCTION	Waterford	Alms Houses, Tallow	4	*N/A						Q4-2018
1442	SHIP CONSTRUCTION	Waterford	Ardmore Park/Priory Lawn, Waterford City	5	*N/A				Stage 4 approved Q2-2019, the scheme is fully approved.		
1443	SHIP CONSTRUCTION	Waterford	Ballinroad, Dungarvan	21	*N/A					Q2-2019	
1444	SHIP CONSTRUCTION	Waterford	Barrack Street, Cappoquin	4	*N/A						Q4-2017
1445	SHIP CONSTRUCTION	Waterford	Coolfin Woods, Portlaoise	12	*N/A						Q2-2019
1446	SHIP CONSTRUCTION	Waterford	Larchville, Waterford City	5	*N/A			Stage 3 approved Q2-2018, the scheme is now approved to proceed to tender.			
1447	SHIP CONSTRUCTION	Waterford	Patrick Street, Tramore	2	*N/A						Q3-2018
1448	SHIP CONSTRUCTION	Waterford	Doyle Street, Waterford City	4	*N/A	Stage 1 approved Q1-2014, outline design and costs being prepared.					
1449	SHIP CONSTRUCTION	Waterford	Old Cinema Site, Dungarvan	15	*N/A						Q4-2016
1450	SHIP CONSTRUCTION	Waterford	The Glen, Bridge St, Waterford	17	*N/A		Stage 2 approved Q3-2018, full design/tender being prepared.				
1451	SHIP CONSTRUCTION	Waterford	Clarendon Court, Penrose Lane, Waterford	24	*N/A	Stage 1 approved Q1-2018, outline design and costs being prepared.					
1452	SHIP CONSTRUCTION	Waterford	Summerland Square, Waterford	12	*N/A			Stage 3 approved Q1-2019, the scheme is now approved to proceed to tender.			
1453	SHIP CONSTRUCTION	Waterford	Rough Sleeper Emerg Accom, Bath St, Waterford City	4	*N/A					Q1-2019	
1454	SHIP CONSTRUCTION	Waterford	Graigueshoneen, Kiltomas, Co Waterford	24	*N/A		Stage 2 approved Q3-2019, full design/tender being prepared.				
1455	SHIP CONSTRUCTION	Waterford	Mount Esker, Ballytruckle Road, Waterford City	13	*N/A	Stage 1 approved Q2-2019, outline design and costs being prepared.					
1456	SHIP CONSTRUCTION RAPID	Waterford	Ballygunner, Waterford City	49	*N/A		Stage 2 approved Q3-2019, full design/tender being prepared.				
1457	SHIP CONSTRUCTION RAPID	Waterford	Ballynaneashagh, Waterford City	20	*N/A	Stage 1 approved Q2-2018, outline design and costs being prepared.					
1458	SHIP CONSTRUCTION TURNKEY	Waterford	Kilrush, Dungarvan	8	*N/A						Q3-2018
1459	SHIP CONSTRUCTION TURNKEY	Waterford	Gibbethill, Gracedieu	5	*N/A						Q3-2018

1460	SHIP CONSTRUCTION TURNKEY	Waterford	Carrickphierish, Gracedieu, Waterford	31	*N/A							Q4-2018
1461	SHIP CONSTRUCTION TURNKEY	Waterford	Shandon, Dungarvan	5	*N/A							Q3-2018
1462	SHIP CONSTRUCTION TURNKEY	Waterford	Airport Road, Waterford City	33	*N/A							Q4-2018
1463	SHIP CONSTRUCTION TURNKEY	Waterford	Kilrush, Dungarvan - Phase 2	10	*N/A							Q4-2018
1464	SHIP CONSTRUCTION TURNKEY	Waterford	Kilrush, Dungarvan - Phase 3	21	*N/A							Q4-2018
1465	SHIP CONSTRUCTION TURNKEY	Waterford	Lacken Road, Waterford	20	*N/A							Q3-2019
1466	SHIP CONSTRUCTION TURNKEY	Waterford	Lacken Road, Waterford - Phase 2	14	*N/A						Q4-2018	
1467	SHIP CONSTRUCTION TURNKEY	Waterford	Lacken Road, Waterford - Phase 3	10	*N/A						Q4-2018	
1468	SHIP CONSTRUCTION TURNKEY	Waterford	Lacken Road, Waterford - Phase 4	11	*N/A					Stage 4 approved Q3-2018, the scheme is fully approved.		
1469	SHIP CONSTRUCTION TURNKEY	Waterford	Shandon, Dungarvan	6	*N/A							Q3-2019
1470	SHIP CONSTRUCTION TURNKEY	Waterford	Railway Gardens, Lismore	6	*N/A							Q3-2019
1471	SHIP CONSTRUCTION TURNKEY	Waterford	Shandon, Dungarvan	8	*N/A					Stage 4 approved Q2-2019, the scheme is fully approved.		
1472	SHIP CONSTRUCTION TURNKEY	Waterford	Railway Gardens, Lismore - Phase 2	6	*N/A							Q3-2019
1473	SHIP CONSTRUCTION TURNKEY	Waterford	Railway Gardens, Lismore - Phase 2	5	*N/A							Q3-2019
1474	SHIP CONSTRUCTION TURNKEY	Waterford	Shandon, Dungarvan	6	*N/A					Stage 4 approved Q2-2019, the scheme is fully approved.		
1475	SHIP CONSTRUCTION TURNKEY	Waterford	Mount Suir, Gracedieu, Carrickphierish - 18 apts	18	*N/A					Stage 4 approved Q3-2019, the scheme is fully approved.		
1476	CALF Turnkey	Westmeath	Cluain Mullen, Castlepollard, Co. Westmeath (Phase 1)	8	Túath Housing Association Ltd							Q2-2019
1477	CALF Turnkey	Westmeath	Cluain Mullen, Castlepollard, Westmeath (Phase 1)	2	Túath Housing Association Ltd							Q2-2017
1478	CALF Turnkey	Westmeath	Rahanine, Rochfortbridge, Co Westmeath (Phase 1)	12	Túath Housing Association Ltd							Q4-2018
1479	CAS CONSTRUCTION	Westmeath	Farran, Mullingar	4	Túath Housing Association Ltd					Stage 4 approved Q3-2019, the scheme is fully approved.		

1480	CAS CONSTRUCTION TURNKEY	Westmeath	Ardmore Road, Mullingar	14	Túath Housing Association Ltd				Stage 4 approved Q3-2019, the scheme is fully approved.		
1481	CAS CONSTRUCTION TURNKEY	Westmeath	Ardmore Road, Mullingar	22	Túath Housing Association Ltd				Stage 4 approved Q3-2019, the scheme is fully approved.		
1482	SHIP CONSTRUCTION	Westmeath	Lissywollen, Athlone	55	*N/A				Stage 4 approved Q2-2019, the scheme is fully approved.		
1483	SHIP CONSTRUCTION	Westmeath	Bun Daire, Kinnegad (Phase 3)	12	*N/A					Q3-2019	
1484	SHIP CONSTRUCTION	Westmeath	St. Laurence's Terrace, Mullingar	9	*N/A						Q4-2018
1485	SHIP CONSTRUCTION	Westmeath	Ennell Court, Mullingar	1	*N/A						Q1-2018
1486	SHIP CONSTRUCTION	Westmeath	Arcadia, Athlone	19	*N/A					Q2-2018	
1487	SHIP CONSTRUCTION	Westmeath	Ennell Court, Mullingar	3	*N/A						Q2-2016
1488	SHIP CONSTRUCTION	Westmeath	Grange Crescent, Mullingar	2	*N/A						Q1-2016
1489	SHIP CONSTRUCTION	Westmeath	Ennell Court, Mullingar (Phase 2)	31	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
1490	SHIP CONSTRUCTION	Westmeath	Cloghanboy, Athlone	10	*N/A				Stage 4 approved Q1-2019, the scheme is fully approved.		
1491	SHIP CONSTRUCTION	Westmeath	Bishopsgate, Mullingar	2	*N/A					Q3-2019	
1492	SHIP CONSTRUCTION	Westmeath	Arcadia, Athlone	21	*N/A		Stage 2 approved Q3-2019, full design/tender being prepared.				
1493	SHIP CONSTRUCTION	Westmeath	Canal Avenue, Mullingar	22	*N/A	Stage 1 approved Q1-2019, outline design and costs being prepared.					
1494	SHIP CONSTRUCTION	Westmeath	Arcadia, Athlone	14	*N/A					Q2-2018	
1495	SHIP CONSTRUCTION	Westmeath	Railway Terrace, Mullingar	24	*N/A	Stage 1 approved Q3-2019, outline design and costs being prepared.					
1496	SHIP CONSTRUCTION	Westmeath	Bishopsgate, Mullingar - Phase 2	2	*N/A					Q3-2019	
1497	SHIP CONSTRUCTION	Westmeath	Railway Terrace, Mullingar	16	*N/A	Stage 1 approved Q3-2019, outline design and costs being prepared.					
1498	SHIP CONSTRUCTION RAPID	Westmeath	O'Growney Green, Mullingar	14	*N/A	Stage 1 approved Q2-2018, outline design and costs being prepared.					
1499	SHIP CONSTRUCTION RAPID	Westmeath	Dalton Park, Mullingar	12	*N/A	Stage 1 approved Q3-2019, outline design and costs being prepared.					

1500	SHIP CONSTRUCTION RAPID	Westmeath	Water Street, Castlepollard	7	*N/A	Stage 1 approved Q3-2019, outline design and costs being prepared.					
1501	SHIP CONSTRUCTION RAPID	Westmeath	Ennell Court, Mullingar (Phase 1)	15	*N/A	Stage 1 approved Q3-2019, outline design and costs being prepared.					
1502	SHIP CONSTRUCTION TURNKEY	Westmeath	Belvedere Hills, Mullingar	21	*N/A						Q4-2017
1503	SHIP CONSTRUCTION TURNKEY	Westmeath	Cloon Lara, Mullingar	12	*N/A						Q2-2019
1504	SHIP CONSTRUCTION TURNKEY	Westmeath	Abbeybrook, Kilbeggan	7	*N/A						Q1-2019
1505	SHIP CONSTRUCTION TURNKEY	Westmeath	Lakepoint, Mullingar	31	*N/A				Stage 4 approved Q2-2019, the scheme is fully approved.		
1506	SHIP CONSTRUCTION TURNKEY	Westmeath	Coill Rua, Mullingar	8	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
1507	CALF Turnkey	Wexford	9 Units, Gleann an Ghairdin, Gorey, Co. Wexford (Phase 1)	9	Túath Housing Association Ltd				Q3-2019		
1508	CALF Turnkey	Wexford	Ard Uisce, Wexford Town (Phase 1)	5	Túath Housing Association Ltd						Q4-2017
1509	CALF Turnkey	Wexford	Ard Uisce, Whiterock, Wexford (Phase 1)	1	Túath Housing Association Ltd						Q1-2018
1510	CALF Turnkey	Wexford	Ard Uisce, Whiterock, Wexford (Phase 1)	6	Túath Housing Association Ltd						Q1-2018
1511	CALF Turnkey	Wexford	Ard Uisce, Whiterock, Wexford (Phase 1)*	6	Túath Housing Association Ltd						Q1-2017
1512	CALF Turnkey	Wexford	Ballyboggan, Castlebridge, Co Wexford (Phase 1)	10	Co-operative Housing Ireland						Q4-2018
1513	CALF Turnkey	Wexford	Fearach Cnoic, Greenville, The Moyne, Enniscorthy (Phase 1)*	34	Oaklee Housing						Q4-2018
1514	CALF Turnkey	Wexford	Fearach Cnoic, Greenville, The Moyne, Enniscorthy (Phase 2)	6	Oaklee Housing						Q2-2019
1515	CALF Turnkey	Wexford	Gleann an Ghairdin, Gorey (Phase 1)	18	Túath Housing Association Ltd					Q4-2018	
1516	CALF Turnkey	Wexford	Greenville, Enniscorthy, Co. Wexford (Phase 1)*	6	Oaklee Housing						Q2-2019
1517	CALF Turnkey	Wexford	Hunters Green, Gorey (Phase 1)	7	Co-operative Housing Ireland						Q2-2016
1518	CALF Turnkey	Wexford	Hunters Green, Gorey (Phase 2)	11	Co-operative Housing Ireland						Q3-2016
1519	CALF Turnkey	Wexford	Hunters Green, Gorey (Phase 3)	11	Co-operative Housing Ireland						Q1-2017

1540	SHIP CONSTRUCTION	Wexford	SN Castlemoyle, New Ross	1	*N/A					Q4-2018	
1541	SHIP CONSTRUCTION	Wexford	Cloghultagh, Taghmon	18	*N/A					Q2-2019	
1542	SHIP CONSTRUCTION	Wexford	Coolcotts, Clonard	7	*N/A					Q3-2018	
1543	SHIP CONSTRUCTION	Wexford	Creagh, Gorey	10	*N/A						Q1-2019
1544	SHIP CONSTRUCTION	Wexford	Danescastle	10	*N/A						Q1-2019
1545	SHIP CONSTRUCTION	Wexford	Slippery Green, Wexford	10	*N/A						Q3-2019
1546	SHIP CONSTRUCTION	Wexford	Whiterock Hill, Wexford	20	*N/A		Stage 2 approved Q2-2018, full design/tender being prepared.				
1547	SHIP CONSTRUCTION	Wexford	Cois Mara	2	*N/A						Q3-2018
1548	SHIP CONSTRUCTION	Wexford	Killeens, Wexford	40	*N/A		Stage 2 approved Q3-2019, full design/tender being prepared.				
1549	SHIP CONSTRUCTION	Wexford	Oylegate	2	*N/A						Q2-2018
1550	SHIP CONSTRUCTION	Wexford	Cherryorchard, Enniscorthy	8	*N/A						Q3-2018
1551	SHIP CONSTRUCTION	Wexford	Ross Road, Enniscorthy	1	*N/A					Q3-2018	
1552	SHIP CONSTRUCTION	Wexford	Baile Eoghain, Gorey	5	*N/A						Q4-2018
1553	SHIP CONSTRUCTION	Wexford	Baile an Trá, Riverchapel (Courtown Ardamine)	10	*N/A						Q2-2016
1554	SHIP CONSTRUCTION	Wexford	Shanna Court, Coolcotts	8	*N/A						Q1-2016
1555	SHIP CONSTRUCTION	Wexford	Francis Street, Wexford	1	*N/A						Q1-2017
1556	SHIP CONSTRUCTION	Wexford	Commodore Barry	1	*N/A						Q2-2016
1557	SHIP CONSTRUCTION	Wexford	Glentire, The Ballagh, Enniscorthy	7	*N/A					Q2-2019	
1558	SHIP CONSTRUCTION	Wexford	Rosetown, Rosslare, Co Wexford	36	*N/A		Stage 1 approved Q1-2018, outline design and costs being prepared.				
1559	SHIP CONSTRUCTION	Wexford	Carley's Bridge, Enniscorthy, Co Wexford	17	*N/A		Stage 1 approved Q1-2018, outline design and costs being prepared.				

1560	SHIP CONSTRUCTION	Wexford	Creagh (East), Gorey	4	*N/A	Stage 1 approved Q2-2018, outline design and costs being prepared.						
1561	SHIP CONSTRUCTION	Wexford	Rosbercon, New Ross	28	*N/A	Stage 1 approved Q4-2018, outline design and costs being prepared.						
1562	SHIP CONSTRUCTION	Wexford	Baile Eoghain, Gorey (Phase 2)	4	*N/A							Q4-2018
1563	SHIP CONSTRUCTION	Wexford	Wexford Street, Gorey	20	*N/A	Stage 1 approved Q1-2019, outline design and costs being prepared.						
1564	SHIP CONSTRUCTION	Wexford	Rosemary Heights, Ferns, Co. Wicklow	7	*N/A	Stage 1 approved Q2-2019, outline design and costs being prepared.						
1565	SHIP CONSTRUCTION	Wexford	Bullawn, Irishtown, New Ross	2	*N/A	Stage 1 approved Q2-2019, outline design and costs being prepared.						
1566	SHIP CONSTRUCTION	Wexford	Ballyhine, Barntown, Co. Wexford	6	*N/A	Stage 1 approved Q2-2019, outline design and costs being prepared.						
1567	SHIP CONSTRUCTION	Wexford	Whiterock Hill, Wexford (Phase 2)	24	*N/A		Stage 2 approved Q2-2018, full design/tender being prepared.					
1568	SHIP CONSTRUCTION	Wexford	Creagh (West), Gorey	8	*N/A	Stage 1 approved Q2-2018, outline design and costs being prepared.						
1569	SHIP CONSTRUCTION TURNKEY	Wexford	Madeira Oaks, Wexford	8	*N/A							Q3-2017
1570	SHIP CONSTRUCTION TURNKEY	Wexford	Gleann an Ghairdin, Ballytegan Road, Gorey	8	*N/A							Q1-2018
1571	SHIP CONSTRUCTION TURNKEY	Wexford	Ard Uisce, Whiterock, Wexford	11	*N/A							Q4-2018
1572	SHIP CONSTRUCTION TURNKEY	Wexford	Castlebridge, Co Wexford	3	*N/A							Q3-2018
1573	SHIP CONSTRUCTION TURNKEY	Wexford	Gleann an Ghairdin, Ballytegan Road, Gorey (Phase 2a)	2	*N/A							Q2-2019
1574	SHIP CONSTRUCTION TURNKEY	Wexford	Ard Uisce, Whiterock, Wexford - Phase 2	10	*N/A							Q1-2019
1575	SHIP CONSTRUCTION TURNKEY	Wexford	Gleann an Ghairdin, Ballytegan Road, Gorey (Phase 1b)	10	*N/A							Q4-2018
1576	SHIP CONSTRUCTION TURNKEY	Wexford	Glen Aoibhinn, Ardamine, Gorey	5	*N/A							Q4-2018
1577	SHIP CONSTRUCTION TURNKEY	Wexford	Glen Aoibhinn, Ardamine, Gorey - Phase 2	2	*N/A							Q1-2019
1578	SHIP CONSTRUCTION TURNKEY	Wexford	Whitewater Estuary, Ballyhack, Co. Wexford	3	*N/A						Stage 4 approved Q1-2019, the scheme is fully approved.	
1579	SHIP CONSTRUCTION TURNKEY	Wexford	Riverchapel Lane, Gorey	4	*N/A						Stage 4 approved Q1-2019, the scheme is fully approved.	

1580	SHIP CONSTRUCTION TURNKEY	Wexford	Ard Uisce, White rock, Wexford-Phase 3	4	*N/A						Q2-2019
1581	SHIP CONSTRUCTION TURNKEY	Wexford	Glen Aoibhinn, Ardamine, Gorey - Phase 3	3	*N/A				Stage 4 approved Q4-2018, the scheme is fully approved.		
1582	SHIP CONSTRUCTION TURNKEY	Wexford	Ard Uisce, White rock, Wexford Phase 4	10	*N/A						Q3-2019
1583	SHIP CONSTRUCTION TURNKEY	Wexford	Airhill, Belvedere Rd, Wexford	3	*N/A					Q2-2019	
1584	SHIP CONSTRUCTION TURNKEY	Wexford	St. Martin's Road, Rosslare Harbour	4	*N/A				Stage 4 approved Q2-2019, the scheme is fully approved.		
1585	SHIP CONSTRUCTION TURNKEY	Wexford	Airhill, Belvedere Rd, Wexford	4	*N/A					Q2-2019	
1586	SHIP CONSTRUCTION TURNKEY	Wexford	Gleann an Ghairdin, Ballytegan Road, Gorey (Phase 2b)	2	*N/A					Q1-2018	
1587	SHIP CONSTRUCTION TURNKEY	Wexford	Michael Street, New Ross	3	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
1588	SHIP CONSTRUCTION TURNKEY	Wexford	19 Units at Ard Uisce	19	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
1589	SHIP CONSTRUCTION TURNKEY	Wexford	Gleann an Ghairdin, Ballytegan Road, Gorey (Phase 2 C)	1	*N/A						Q3-2019
1590	CALF Turnkey	Wicklow	1 - 14 Wentworth Place, Wicklow Town (Phase 1)	14	Túath Housing Association Ltd				Q4-2018		
1591	CALF Turnkey	Wicklow	Abbey St, Wicklow (Phase 1)	6	Túath Housing Association Ltd						Q4-2018
1592	CALF Turnkey	Wicklow	Fairgreen Manor, Dunlavin, Co. Wicklow (Phase 1)*	40	Circle Voluntary Housing Association Ltd					Q3-2018	
1593	CALF Turnkey	Wicklow	Glenheron, Greystones, Co. Wicklow (Phase 1)*	5	Túath Housing Association Ltd						Q2-2018
1594	CALF Turnkey	Wicklow	Glenheron, Greystones, Co. Wicklow (Phase 1)*	8	Túath Housing Association Ltd						Q4-2018
1595	CALF Turnkey	Wicklow	Glenheron, Greystones, Co. Wicklow (Phase 2)*	7	Túath Housing Association Ltd						Q2-2019
1596	CALF Turnkey	Wicklow	Glenheron, Greystones, Co. Wicklow (Phase 3)*	4	Túath Housing Association Ltd					Q1-2018	
1597	CALF Turnkey	Wicklow	Hazelbrook Rise, Ballybeg, Rathnew, Co. Wicklow (Phase 1)*	15	Co-operative Housing Ireland						Q4-2018
1598	CALF Turnkey	Wicklow	Hazelbrook Rise, Ballybeg, Rathnew, Co. Wicklow (Phase 2)	73	Co-operative Housing Ireland						Q3-2019
1599	CALF Turnkey	Wicklow	Ternlee, Cooldross Lane, Kilcoole, Co. Wicklow (Phase 1)*	4	Cluid Housing						Q2-2019

1600	CALF Turnkey	Wicklow	Ternlee, Cooldross Lane, Kilcoole, Co. Wicklow (Phase 2)*	2	Cluid Housing					Q4-2017	
1601	CALF Turnkey	Wicklow	The Meadows, Ballynerrin, Wicklow Town (Phase 1)*	7	Túath Housing Association Ltd						Q4-2018
1602	CALF Turnkey	Wicklow	Woodpark, Rathdrum, Co. Wicklow (Phase 1)*	4	Túath Housing Association Ltd						Q3-2019
1603	CAS CONSTRUCTION SINGLE STAGE	Wicklow	Hollybrook Park, Bray, Co. Wicklow	4	St. John of God Housing Association Ltd				Stage 4 approved Q3-2019, the scheme is fully approved.		
1604	PUBLIC PRIVATE PARTNERSHIP (Bundle 1)	Wicklow	Convent Lands	51	*N/A					Q1-2019	
1605	SHIP CONSTRUCTION	Wicklow	Delaney Park, Emoclew Road, Arklow (Phase 3)	21	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
1606	SHIP CONSTRUCTION	Wicklow	Druids Brook, Kilcoole	2	*N/A						Q3-2019
1607	SHIP CONSTRUCTION	Wicklow	Delaney Park, Emoclew Road, Arklow	17	*N/A						Q3-2019
1608	SHIP CONSTRUCTION	Wicklow	Delaney Park, Emoclew Road, Arklow (Phase 2)	26	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
1609	SHIP CONSTRUCTION	Wicklow	FCA Hall, Wicklow Town	8	*N/A					Q3-2018	
1610	SHIP CONSTRUCTION	Wicklow	Kilmantain Place, Bray	4	*N/A				Stage 4 approved Q2-2019, the scheme is fully approved.		
1611	SHIP CONSTRUCTION	Wicklow	O'Byrne Road, Bray	1	*N/A						Q4-2018
1612	SHIP CONSTRUCTION	Wicklow	St Mary's Rd., Arklow (Old Library Site)	7	*N/A						Q4-2018
1613	SHIP CONSTRUCTION	Wicklow	Jameson Heights, Kilmacanogue	20	*N/A					Q2-2019	
1614	SHIP CONSTRUCTION	Wicklow	Avondale Heights, Rathdrum	20	*N/A						Q4-2018
1615	SHIP CONSTRUCTION	Wicklow	Kilbride Lane, Bray (Murphy's Lands)	42	*N/A					Q1-2019	
1616	SHIP CONSTRUCTION	Wicklow	16A Oak Drive, Blessington	1	*N/A						Q3-2019
1617	SHIP CONSTRUCTION	Wicklow	Carrig Eden, 1 Marine Road, Greystones	30	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
1618	SHIP CONSTRUCTION	Wicklow	Farrankelly, Greystones (Phase 2)	24	*N/A					Q1-2019	
1619	SHIP CONSTRUCTION	Wicklow	Sheehan Court, Back Street, Arklow	7	*N/A		Stage 2 approved Q3-2019, full design/tender being prepared.				

1620	SHIP CONSTRUCTION RAPID	Wicklow	Sli na Slainte, Whitehall, Baltinglass	23	*N/A					Q1-2019	
1621	SHIP CONSTRUCTION RAPID	Wicklow	Merrymeeting View, Rathnew	46	*N/A					Q2-2019	
1622	SHIP CONSTRUCTION RAPID	Wicklow	Coolattin Oaks (Ph4), Carnew	30	*N/A					Q3-2019	
1623	SHIP CONSTRUCTION RAPID	Wicklow	Shillelagh Phase 4	22	*N/A		Stage 2 approved Q2-2019, full design/tender being prepared.				
1624	SHIP CONSTRUCTION RAPID	Wicklow	Ashtown Lane, Wicklow Town	40	*N/A	Stage 1 approved Q2-2019, outline design and costs being prepared.					
1625	SHIP CONSTRUCTION RAPID	Wicklow	Ard na Greine, West Ward, Bray	31	*N/A	Stage 1 approved Q2-2019, outline design and costs being prepared.					
1626	SHIP CONSTRUCTION RAPID	Wicklow	Avondale Heights, Rathdrum	20	*N/A	Stage 1 approved Q2-2019, outline design and costs being prepared.					
1627	SHIP CONSTRUCTION RAPID	Wicklow	Mountainview, NTMK	28	*N/A		Stage 2 approved Q3-2019, full design/tender being prepared.				
1628	SHIP CONSTRUCTION RAPID	Wicklow	Sli na Slainte, Whitehall, Baltinglass	11	*N/A				Stage 4 approved Q1-2019, the scheme is fully approved.		
1629	SHIP CONSTRUCTION TURNKEY	Wicklow	Mill Court, Tinahely	2	*N/A						Q2-2018
1630	SHIP CONSTRUCTION TURNKEY	Wicklow	No. 7 Mill Court, Tinahely	1	*N/A						Q4-2018
1631	SHIP CONSTRUCTION TURNKEY	Wicklow	Heatherside, Vale Road, Arklow	10	*N/A						Q2-2019
1632	SHIP CONSTRUCTION TURNKEY	Wicklow	Fernhill, Arklow	1	*N/A						Q3-2018
1633	SHIP CONSTRUCTION TURNKEY	Wicklow	Mill Court, Tinahely	1	*N/A						Q1-2019
1634	SHIP CONSTRUCTION TURNKEY	Wicklow	Merrymeeting, Rathnew	2	*N/A				Stage 4 approved Q4-2018, the scheme is fully approved.		
1635	SHIP CONSTRUCTION TURNKEY	Wicklow	Bollarney Woods, Wicklow Town	10	*N/A						Q3-2019
1636	SHIP CONSTRUCTION TURNKEY	Wicklow	Mill Court, Tinahely	1	*N/A						Q2-2019
1637	SHIP CONSTRUCTION TURNKEY	Wicklow	Kirvin Hill, Rathnew	2	*N/A						Q2-2019
1638	SHIP CONSTRUCTION TURNKEY	Wicklow	Rossmore, NTMK	1	*N/A						Q2-2019
1639	SHIP CONSTRUCTION TURNKEY	Wicklow	Heatherside, Vale Road, Arklow	15	*N/A						Q3-2019

1640	SHIP CONSTRUCTION TURNKEY	Wicklow	Heatherside, Vale Road, Arklow	4	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
1641	SHIP CONSTRUCTION TURNKEY	Wicklow	Heatherside, Vale Road, Arklow	40	*N/A				Stage 4 approved Q3-2019, the scheme is fully approved.		
1642	SHIP CONSTRUCTION TURNKEY	Wicklow	Bollarney Woods, Wicklow Town	4	*N/A					Q2-2018	
1643	SHIP CONSTRUCTION TURNKEY	Wicklow	Bollarney Woods, Wicklow Town	16	*N/A					Q2-2018	
1644	SHIP CONSTRUCTION TURNKEY	Wicklow	Heatherside, Vale Road, Arklow	9	*N/A					Q3-2018	
1645	SHIP CONSTRUCTION TURNKEY	Wicklow	Bollarney Woods Phase 2	3	*N/A					Q2-2018	
